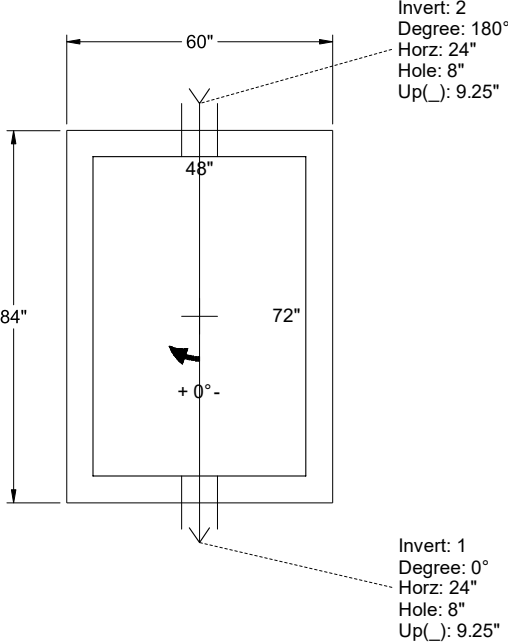

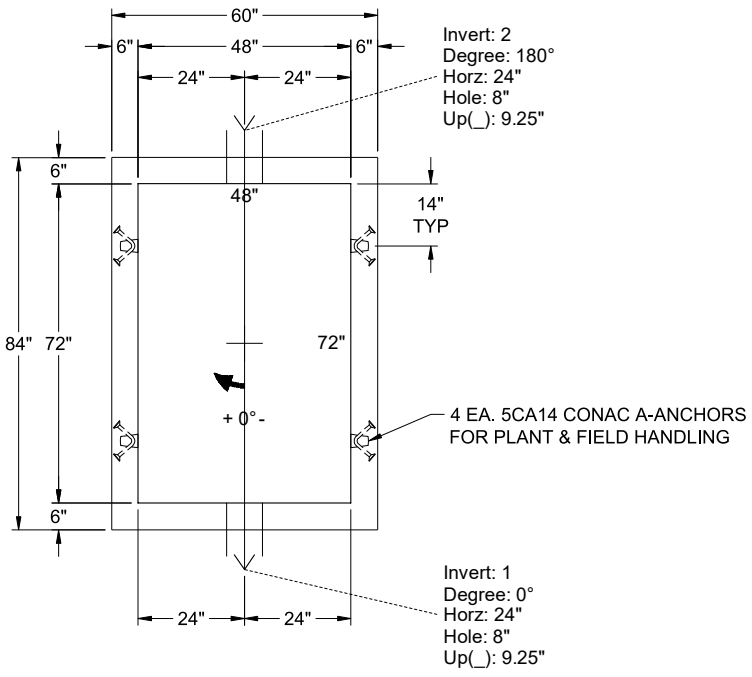



Job Name: 26-2466 - Second Look Meter Vault Job Location: CPU Contractor: Second Look Lawn & Landscape				Plant: 100 6/22/2026 2:43:51 PM		Tech: J. Horsley PC: T. Lewis					
Structure ID: QL1											
P1 BX4872-06BAVF				BOX BASE 6inW, 6inF, Variable Ht F/n							
P3) 36" x 36" - CASTING (cast in) - 3" P2) 48" x 72" - CB FLAT TOP 6"W w/36"x36" HATCH F/F - 8" P1) 48" x 72" - BOX BASE 6inW, 6inF, Variable Ht F/n - 48" 1) HATCH (Alum.) - HALLIDAY W1S 36"x36" 1) This Structure Includes a Cast-in Item - Halliday W1S 36" x 36" Hatch (Supplied by iCast) 1) SECONDARY POUR 1) 48" x 72" - Conseal CS-102 1.00" 2) PSX - 8QRS-S NYLO				0 lb 2591 lb 8867 lb 78 lb 0 lb 0 lb 0 lb 0 lb 13 lb ----- 11549 lb Structure Total:		Structure Notes: 1. PER ASTM C-913 SPECIFICATIONS 2. CONCRETE: 4,500 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 8" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE 4. HALLIDAY W1S 36" X 36" HATCH SUPPLIED BY ICAST - TO BE CAST INTO FLAT LID 5. WET STICK 18" X 24" #5 L-BARS @ 12" C.C. E.W. (GRADE 60) OUT OF FLOOR FOR WALL POUR TIE-IN (24 EA. L-BARS REQUIRED)					
FIRST POUR (FLOOR): 2,538 LBS SECOND POUR (WALLS): 6,329 LBS											
Rim: 4.67' Rim to Invert: 3.653' Slack: 0.04" Sump: 12.204" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	1.017'	0°	30"	2" PVC SCH40	2.375"	PSX 8QRS-S NYLO	8"	8"	9.25"	0"	
Invert 2	1.017'	180°	30"	2" PVC SCH40	2.375"	PSX 8QRS-S NYLO	8"	8"	9.25"	0"	
Invert 3											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: n/a		Wall Thickness: 6" Floor Height: 6"		Height (Int): 48" Height (Ext): 54"		Weight (Net): 8867 lb Volume (Net): 2.26cu.yd	

Job Name: 26-2466 - Second Look Meter Vault Job Location: CPU Contractor: Second Look Lawn & Landscape					Plant: 100 6/22/2026 2:43:51 PM		Tech: J. Horsley PC: T. Lewis				
Structure ID: QL1											
P1 BX4872-06BAVF BOX BASE 6inW, 6inF, Variable Ht F/n											
P3) 36" x 36" - CASTING (cast in) - 3" P2) 48" x 72" - CB FLAT TOP 6"W w/36"x36" HATCH F/F - 8" P1) 48" x 72" - BOX BASE 6inW, 6inF, Variable Ht F/n - 48" 1) HATCH (Alum.) - HALLIDAY W1S 36"x36" 1) This Structure Includes a Cast-in Item - Halliday W1S 36" x 36" Hatch (Supplied by iCast) 1) SECONDARY POUR 1) 48" x 72" - Conseal CS-102 1.00" 2) PSX - 8QRS-S NYLO					0 lb 2591 lb 8867 lb 78 lb 0 lb 0 lb 0 lb 0 lb 13 lb Structure Total: 11549 lb		Structure Notes: - PER ASTM C-913 SPECIFICATIONS - CONCRETE: 4,500 PSI AT 28 DAYS - REINFORCEMENT: #5 BAR @ 8" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE - HALLIDAY W1S 36" X 36" HATCH SUPPLIED BY ICAST - TO BE CAST INTO FLAT LID - LIFTERS: 4 EA. 5CA14 CONAC A-ANCHORS FOR PLANT & FIELD HANDLING - INSTALLED AS SHOWN				
FIRST POUR (FLOOR): 2,538 LBS SECOND POUR (WALLS): 6,329 LBS											
Rim: 4.67' Rim to Invert: 3.653' Slack: 0.04" Sump: 12.204" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	1.017'	0°	30"	2" PVC SCH40	2.375"	PSX 8QRS-S NYLO	8"	8"	9.25"	0"	
Invert 2	1.017'	180°	30"	2" PVC SCH40	2.375"	PSX 8QRS-S NYLO	8"	8"	9.25"	0"	
Invert 3											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: n/a		Wall Thickness: 6" Floor Height: 6"		Height (Int): 48" Height (Ext): 54"		Weight (Net): 8867 lb Volume (Net): 2.26cu.yd	
