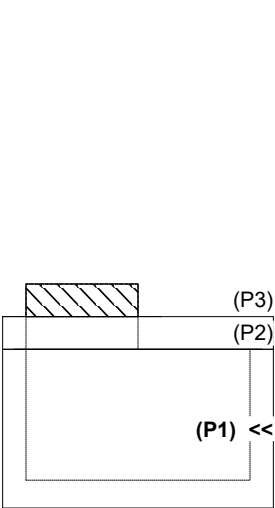
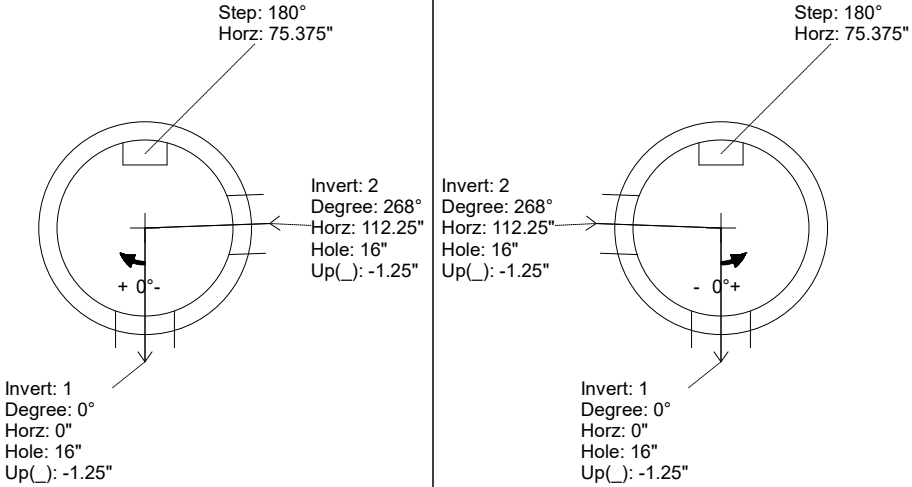



Job Name: 26-2090 - Monroe Co Area Tech Center Renovation Job Location: Tompkinsville, KY Contractor: Lindsey's Dirt Works LLC					Plant: 100 7/20/2026 6:19:37 PM		Tech: Jared - F PC: M. Sullivan				
Structure ID: 5 ST-MH											
P1 MH048BAVF		MH BASE Custom Ht F/n									
P3) 24" - CASTING HEIGHT - 7" P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/F - 7" P1) 48" - MH BASE Custom Ht F/n - 28" 1) CASTING - HOE MC-375 F/C Storm 1) 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 16 2) MH Step ML-10-TDS-NCR - 10"						0 lb 1286 lb 3115 lb 271 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 4672 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE MC-375 F/C STORM). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 862'		Rim to Invert: 3.54'		Slack: 0.48"		Sump: 0"		Step Position: 180°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	858.46'	0°	0"	12" HDPE	14.5"	Hole 16	16"	16.312"	-1.25"	0"	
Invert 2	858.46'	268°	135.625"	12" HDPE	14.5"	Hole 16	16"	16.312"	-1.25"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)						UPSIDE-DOWN VIEW (int. dimensions)					
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 28" Height (Ext): 34"		Weight (Net): 3115 lb Volume (Net): 0.8cu.yd		
