

Structure ID: 142

P1 BX24300808VF

BOX BASE 8inW, 8inF, Variable Ht F/n

- P3) 15" x 27" - P.I.P. - BY OTHERS - 8"
- P2) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8"
- P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht F/n - 38"
- 1) 24" x 30" - Conseal CS-102 1.00"
- 1) 15" x 27" - Conseal CS-102 1.00"
- 1) Hole - 20
- 1) Hole - 18
- 2) Hole - 4

0 lb
 963 lb
 4408 lb
 0 lb
 0 lb
 0 lb
 0 lb
 0 lb
 0 lb
 Structure Total: 5371 lb



- Structure Notes:
****KYTC STATE PROJECT****
 1. PER KYTC DBI TYPE 13G / ASTM C-913 SPECS
 2. CONCRETE: 4,000 PSI AT 28 DAYS
 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
 4. NO STORM INVERT
 5. NO STEPS
 6. HOE KY-230G FRAME & GRATE SUPPLIED BY OTHERS

Rim: 563.24' Rim to Invert: 4.5' Slack: 0" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	558.74'	0°	20"	15" HDPE	17.6"	Hole 20	20"	20"	-2.5"	0"
Invert 2	558.99'	180°	20"	12" HDPE	14.5"	Hole 18	18"	18"	0"	0"
Invert 3	561.24'	90°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	30"	0"
Invert 4	561.24'	270°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	30"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

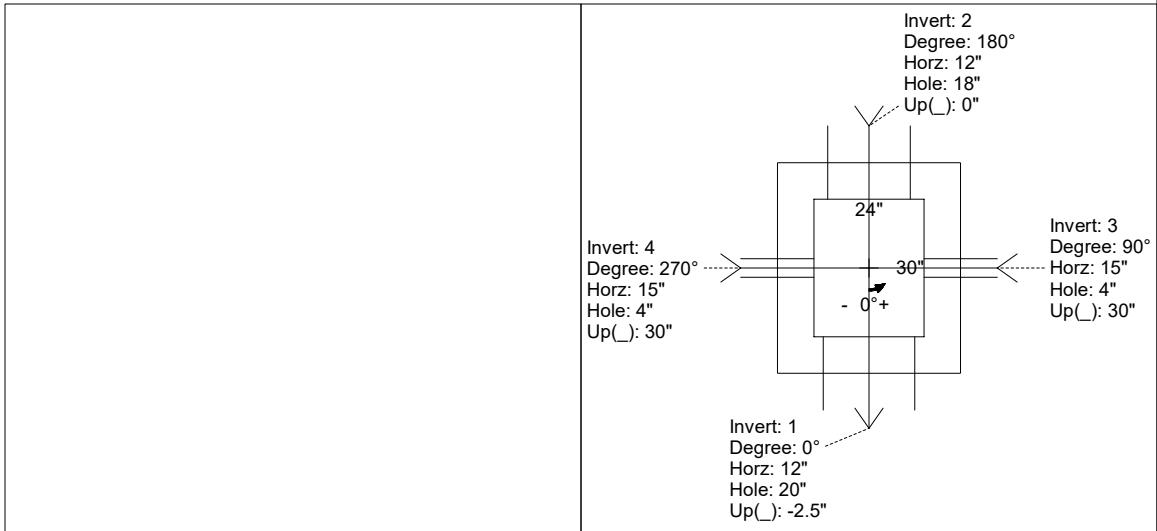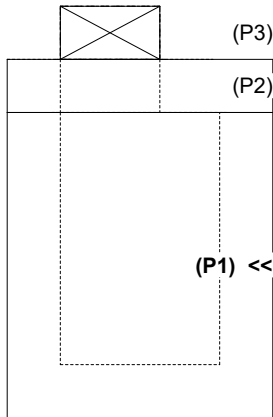

INSIDE WALL DIMENSIONS

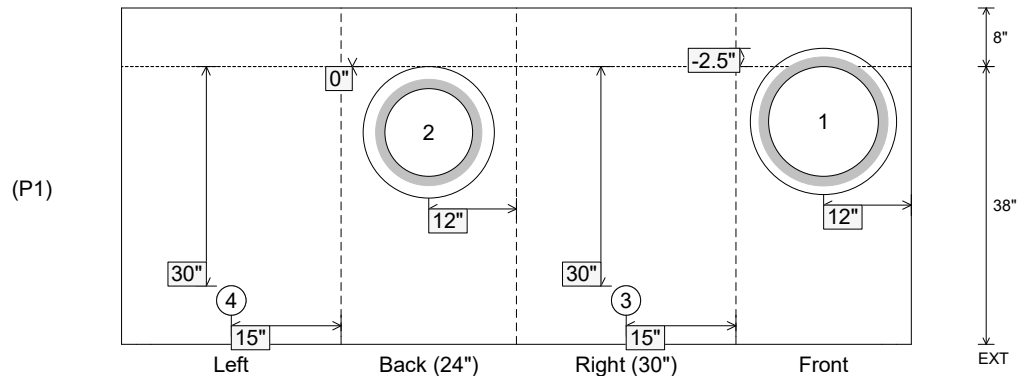

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 38" Height (Ext): 46"	Weight (Net): 4408 lb Volume (Net): 1.13cu.yd
----------------------------------	-------------------------------	--	--	--
