



Job Name: 25-3452 - Churchill Downs Skye Terrace Improvements Job Location: Louisville, KY 40208 Contractor: Louisville Paving and Construction				Plant: 100 4/30/2026 1:21:45 PM		Tech: Jared - F PC: J. Jarvis				
Structure ID: S115										
P1 MH048BAVF		MH BASE Custom Ht T/n								
P4) 32" x 32" - CASTING HEIGHT - 3" P3) 48" - MH FLAT TOP w/32"x32" Hole F/G - 12" P2) 48" - MH RISER T/G - 48" P1) 48" - MH BASE Custom Ht T/n - 40" 1) CASTING - HOE 595 F/G 2) 48" - Conseal CS-102 1.00" 1) 32" x 32" - Conseal CS-102 1.00" 1) Hole - 30 1) Hole - 16 1) Hole - 24						0 lb 1629 lb 3267 lb 3611 lb 376 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 8884 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 595 F/G) REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
Rim: 454.25' Rim to Invert: 8.61' Slack: 0.32" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	445.64'	0°	0"	24" HDPE	27.8"	Hole 30	30"	32.406"	-1.875"	0"
Invert 2										
Invert 3	445.89'	227°	114.875"	18" HDPE	21.2"	Hole 24	24"	25.133"	1.375"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

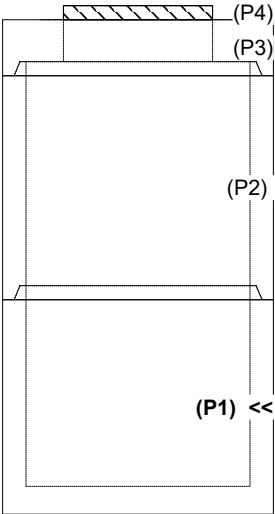

(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

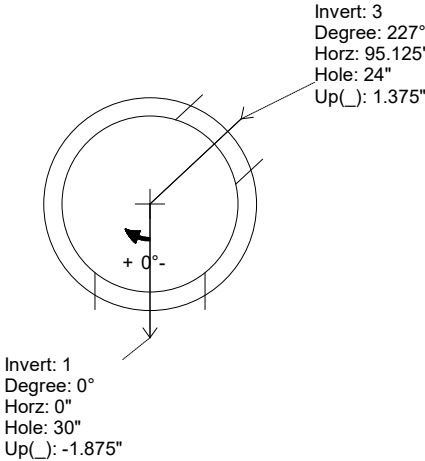

Invert: 1
Degree: 0°
Horz: 0"
Hole: 30"
Up(): -1.875"

Invert: 3
Degree: 227°
Horz: 95.125"
Hole: 24"
Up(): 1.375"


UPSIDE-DOWN VIEW (int. dimensions)

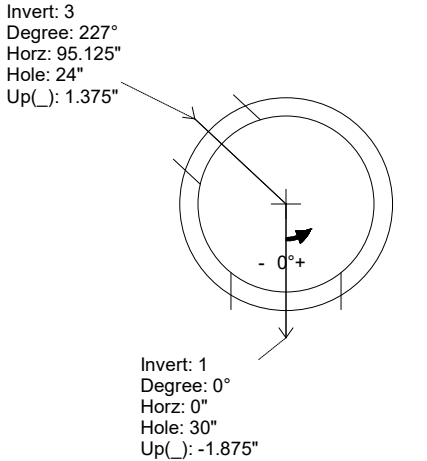

Invert: 1
Degree: 0°
Horz: 0"
Hole: 30"
Up(): -1.875"

Invert: 3
Degree: 227°
Horz: 95.125"
Hole: 24"
Up(): 1.375"

INSIDE WALL DIMENSIONS

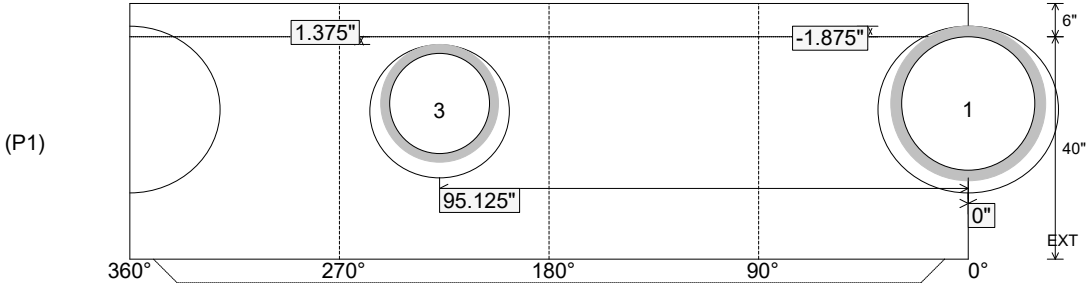

(P1)

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 40" Height (Ext): 46"	Weight (Net): 3611 lb Volume (Net): 0.92cu.yd
----------------------------------	---------------------------------	--	--	--
