



Job Name: 25-1401 Irwin Landing Ph. 1 Job Location: Murfreesboro, TN Contractor: Bear Construction LLC					Plant: Beaver Dam 6/9/2026 10:37:00 AM		Tech: S. Felletter PC: Erica Bradley				
Structure ID: R13											
P1 MH048BAVF		MH BASE Custom Ht T/n									
P3) 28" x 28" - CASTING HEIGHT - 5" P2) 48" - MH FLAT TOP w/28"x28" Hole F/G - 12" P1) 48" - MH BASE Custom Ht T/n - 65.5" 1) 48" - STORM INVERT CHANNEL - 1/4 HEIGHT 1) CASTING - JBS 3104-V SINGLE SET 1) 48" - Conseal CS-102 1.00" 1) 28" x 28" - Conseal CS-102 1.00" 3) Hole - 26" 5) MH Step ML-10-TDS-NCR - 10"					0 lb 1368 lb 5206 lb 1075 lb 250 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 7899 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (JBS-3104 SINGLE SET). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 574.67' Rim to Invert: 6.67' Slack: 0.04" Sump: 2.5" Step Position: 67°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	568'	0°	0"	18" RCP B WALL	23"	Hole 26	26"	27.476"	0"	0"	
Invert 2	570.75'	134°	67.823"	18" RCP B WALL	23"	Hole 26	26"	27.476"	33"	0"	
Invert 3	568'	226°	114.389"	18" RCP B WALL	23"	Hole 26	26"	27.476"	0"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

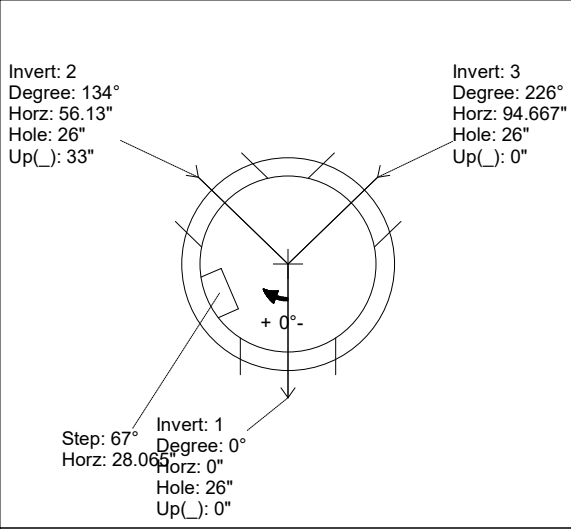

UPSIDE-DOWN VIEW (int. dimensions)

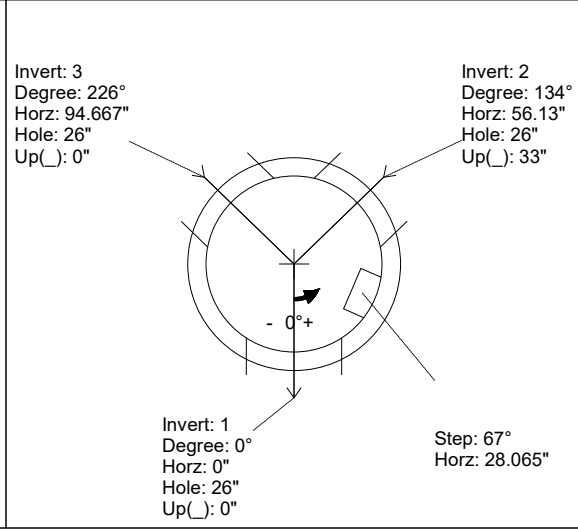


INSIDE WALL DIMENSIONS

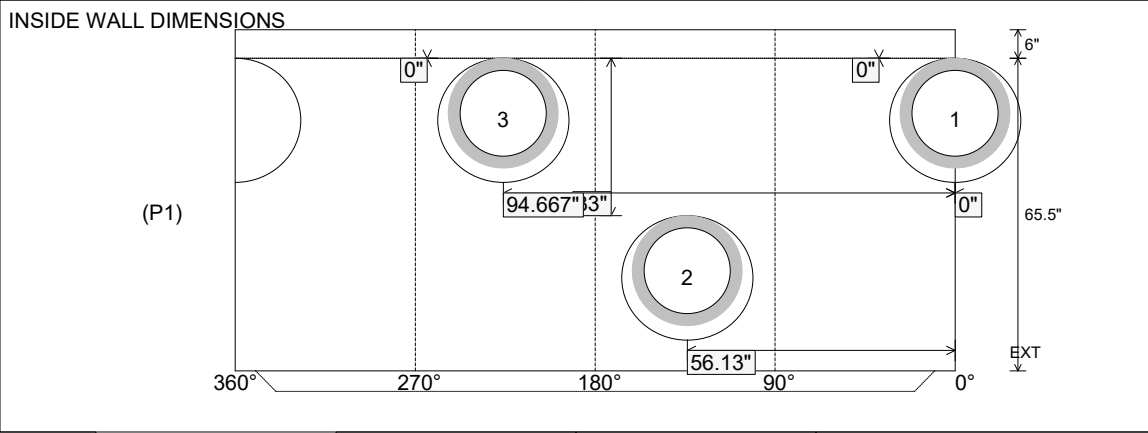


Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 65.5" Height (Ext): 71.5"	Weight (Net): 5206 lb Volume (Net): 1.33cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 25-1401 Irwin Landing Ph. 1 Job Location: Murfreesboro, TN Contractor: Bear Construction LLC					Plant: Beaver Dam 6/9/2026 10:37:00 AM		Tech: S. Felletter PC: Erica Bradley				
Structure ID: R13											
P1 MH048BAVF		MH BASE Custom Ht T/n									
P3) 28" x 28" - CASTING HEIGHT - 5" P2) 48" - MH FLAT TOP w/28"x28" Hole F/G - 12" P1) 48" - MH BASE Custom Ht T/n - 65.5" 1) 48" - STORM INVERT CHANNEL - 1/4 HEIGHT 1) CASTING - JBS 3104-V SINGLE SET 1) 48" - Conseal CS-102 1.00" 1) 28" x 28" - Conseal CS-102 1.00" 3) Hole - 26" 5) MH Step ML-10-TDS-NCR - 10"					0 lb 1368 lb 5206 lb 1075 lb 250 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 7899 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (JBS-3104 SINGLE SET). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. Invert channel drawing 1/4 Height storm invert				
Rim: 574.67' Rim to Invert: 6.67' Slack: 0.04" Sump: 2.5" Step Position: 67°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	568'	0°	0"	18" RCP B WALL	23"	Hole 26	26"	27.476"	0"	0"	
Invert 2	570.75'	134°	67.823"	18" RCP B WALL	23"	Hole 26	26"	27.476"	33"	0"	
Invert 3	568'	226°	114.389"	18" RCP B WALL	23"	Hole 26	26"	27.476"	0"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

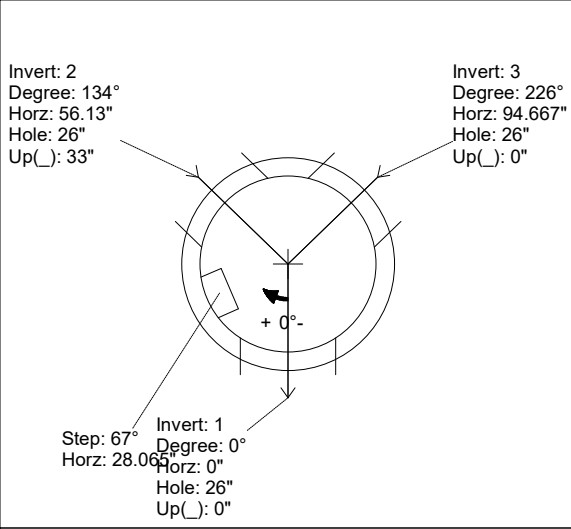

UPSIDE-DOWN VIEW (int. dimensions)

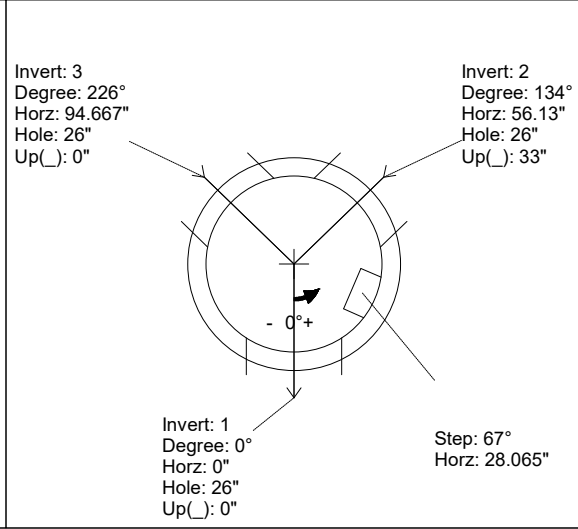

INSIDE WALL DIMENSIONS

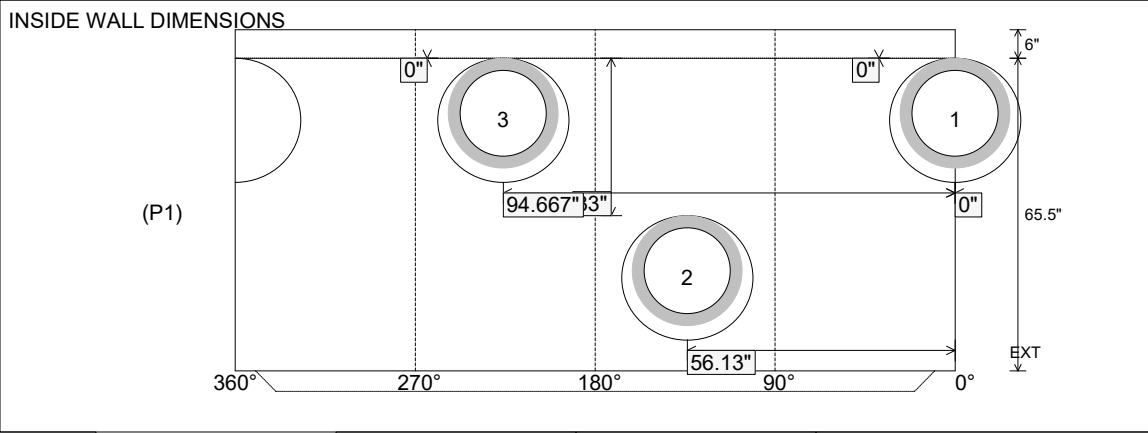

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 65.5" Height (Ext): 71.5"	Weight (Net): 5206 lb Volume (Net): 1.33cu.yd
----------------------------------	---------------------------------	--	--	--
