



Job Name: 25-1401 Irwin Landing Ph. 1 Job Location: Murfreesboro, TN Contractor: Bear Construction LLC					Plant: Beaver Dam 6/9/2026 10:37:26 AM		Tech: S. Felletter PC: Erica Bradley				
Structure ID: R51											
P1 MH048BAVF		MH BASE Custom Ht F/n									
P3) 20" x 34" - CASTING HEIGHT - 7" P2) 48" - MH FLAT TOP - TDOT NO 10 (20"x34" Hole) F/F - 10" P1) 48" - MH BASE Custom Ht F/n - 69" 1) 48" - STORM INVERT CHANNEL - 1/4 HEIGHT 1) CASTING - JBS 3123 MODIFIED SET 1) 48" - SGL 1"x14.5' Butyl (2x) 2) Hole - 26						0 lb 1646 lb 5684 lb 1075 lb 250 lb 0 lb 0 lb ----- 8655 lb		Structure Notes: 1. PER TDOT D-CB-10RA / ASTM C478 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (JBS-3123 MOD SET). REINFORCING PER ASTM A615 (GRADE 60). ** PER TDOT STD DRAWING D-CB-10RA ** - TOP SLAB - DBL MAT #5 BARS. - RISER (As .24) - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.			
Rim: 568.01' Rim to Invert: 6.96' Slack: 0.02" Sump: 2.5" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	561.05'	0°	0"	18" RCP B WALL	23"	Hole 26	26"	27.476"	0"	0"	
Invert 2	561.05'	200°	101.229"	18" RCP B WALL	23"	Hole 26	26"	27.476"	0"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

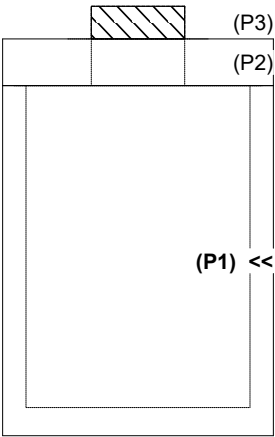

(P3)
(P2)
(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

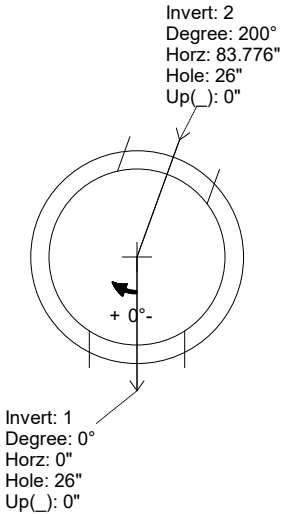

Invert: 2
Degree: 200°
Horz: 83.776"
Hole: 26"
Up(_): 0"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 26"
Up(_): 0"


UPSIDE-DOWN VIEW (int. dimensions)

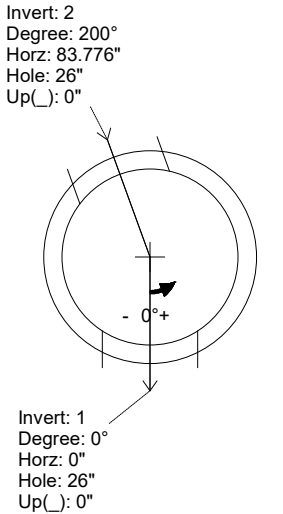

Invert: 2
Degree: 200°
Horz: 83.776"
Hole: 26"
Up(_): 0"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 26"
Up(_): 0"

INSIDE WALL DIMENSIONS

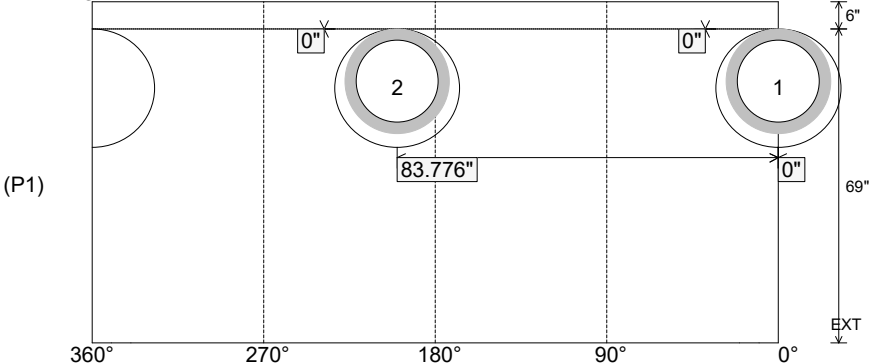

(P1)


360° 270° 180° 90° 0°

EXT


Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 69" Height (Ext): 75"	Weight (Net): 5684 lb Volume (Net): 1.45cu.yd
----------------------------------	-------------------------------	--	--	--

Job Name: 25-1401 Irwin Landing Ph. 1 Job Location: Murfreesboro, TN Contractor: Bear Construction LLC					Plant: Beaver Dam 6/9/2026 10:37:26 AM		Tech: S. Felletter PC: Erica Bradley				
Structure ID: R51											
P1 MH048BAVF		MH BASE Custom Ht F/n									
P3) 20" x 34" - CASTING HEIGHT - 7" P2) 48" - MH FLAT TOP - TDOT NO 10 (20"x34" Hole) F/F - 10" P1) 48" - MH BASE Custom Ht F/n - 69" 1) 48" - STORM INVERT CHANNEL - 1/4 HEIGHT 1) CASTING - JBS 3123 MODIFIED SET 1) 48" - SGL 1"x14.5' Butyl (2x) 2) Hole - 26					0 lb 1646 lb 5684 lb 1075 lb 250 lb 0 lb 0 lb ----- Structure Total: 8655 lb		Structure Notes: . 1. PER TDOT D-CB-10RA / ASTM C478 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (JBS-3123 MOD SET). REINFORCING PER ASTM A615 (GRADE 60). ** PER TDOT STD DRAWING D-CB-10RA ** - TOP SLAB - DBL MAT #5 BARS. - RISER (As .24) - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.				
Rim: 568.01' Rim to Invert: 6.96' Slack: 0.02" Sump: 2.5" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	561.05'	0°	0"	18" RCP B WALL	23"	Hole 26	26"	27.476"	0"	0"	
Invert 2	561.05'	200°	101.229"	18" RCP B WALL	23"	Hole 26	26"	27.476"	0"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

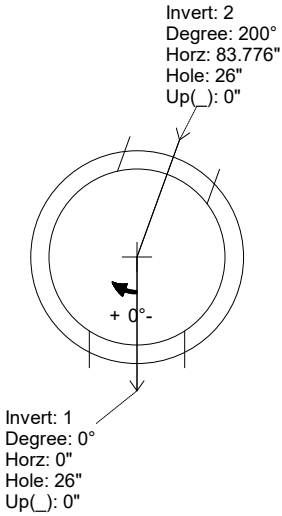

UPSIDE-DOWN VIEW (int. dimensions)

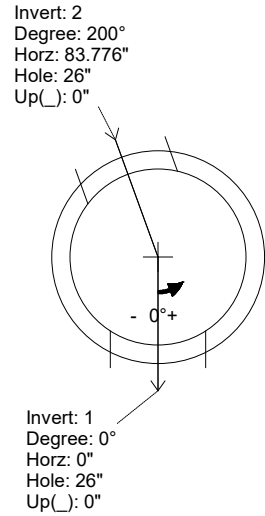

INSIDE WALL DIMENSIONS

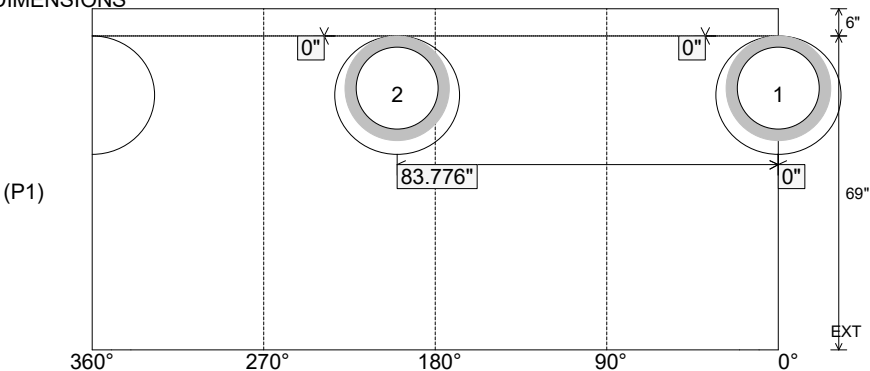

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 69" Height (Ext): 75"	Weight (Net): 5684 lb Volume (Net): 1.45cu.yd
----------------------------------	-------------------------------	--	--	--
