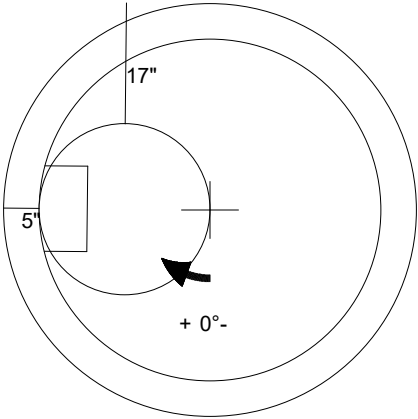



Job Name: 23-2309 - Richland Estates Subdivision		Plant: 100	Tech: J. Horsley	
Job Location: Portland, TN		6/30/2026 8:53:31 AM	PC: T. Lewis	
Contractor: Core & Main LP (BG)				
Structure ID: 02 SS-MH				
P3 MH048CN36X		ECC XYPEX CONE w/ 24" HOLE		
P5) 24" - CASTING HEIGHT - 6" P4) 24" - XYPEX GRADE RING - 4" P3) 48" - ECC XYPEX CONE w/ 24" HOLE - 36" P2) 48" - MH RISER w/XYPEX - 24" P1) 48" - MH BASE w/XYPEX - 24" 1) JOINT WRAP - 0.065"x12"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) 48" - Conseal CS-102 1.00" (Double) 1) 48" - Conseal CS-231 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 7) MH Step ML-10-TDS-NCR - 10"		0 lb 270 lb 2251 lb 1677 lb 2911 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 0 lb 0 lb 16 lb 0 lb ----- 8565 lb Structure Total:	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = XYPEX C-500 NF RED 4. CASTING BY OTHERS (JBS 1155 F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 2251 lb Volume (Net): 0.57cu.yd
