

Contractor: Core & Main LP (BG)

TECH: J. Horsley

Plant: 100



Size: 32" x 32"

Rim to Invert: 2.75'

Floor Height: 8"


Slack: 0"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P2) 32" x 32" - CASTING HEIGHT - 4"
P1) 32" x 32" - BOX BASE 8inW, 8inF, Variable Ht - 29"
1) 32" x 32" - Conseal CS-102 1.00"
1) DOGHOUSE INVRTD - 32"x30"

0 lb
4198 lb
0 lb
0 lb



Structure Total: 4198 lb

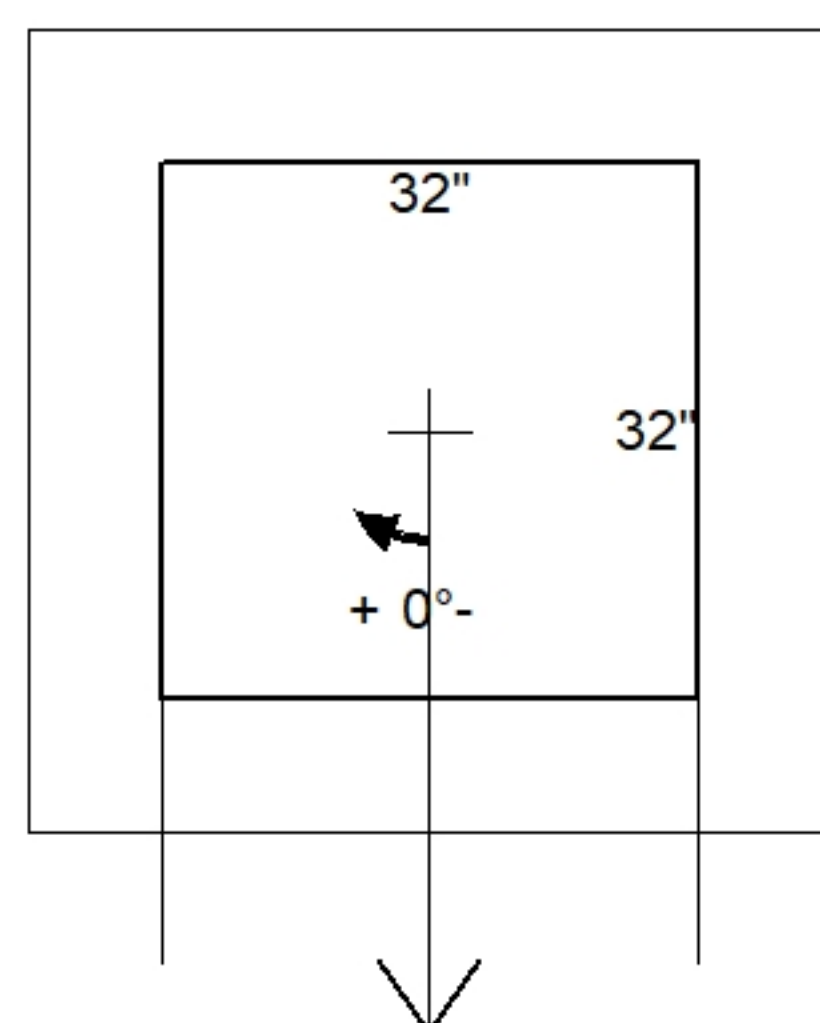

Invert: 1
Degree: 0°

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	806.7'							
Reducer								
Invert 1	803.95'	0°	24" RCP B WALL	30"	32" x 30"	DOGHOUSE INVRTD 32"x30"	-3"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

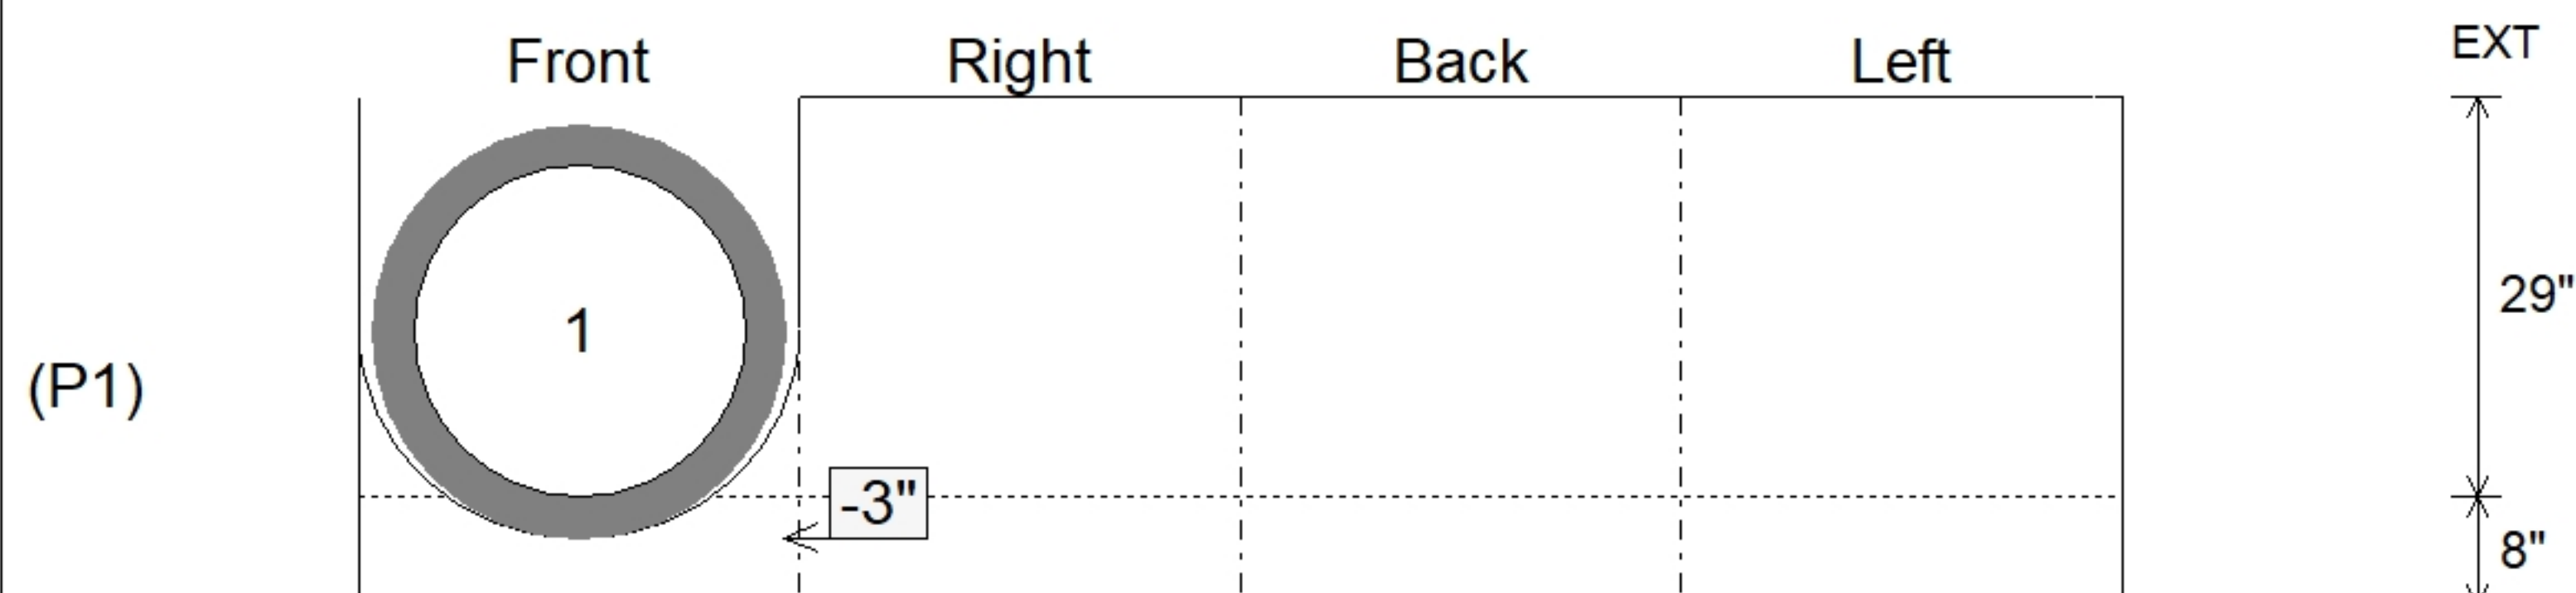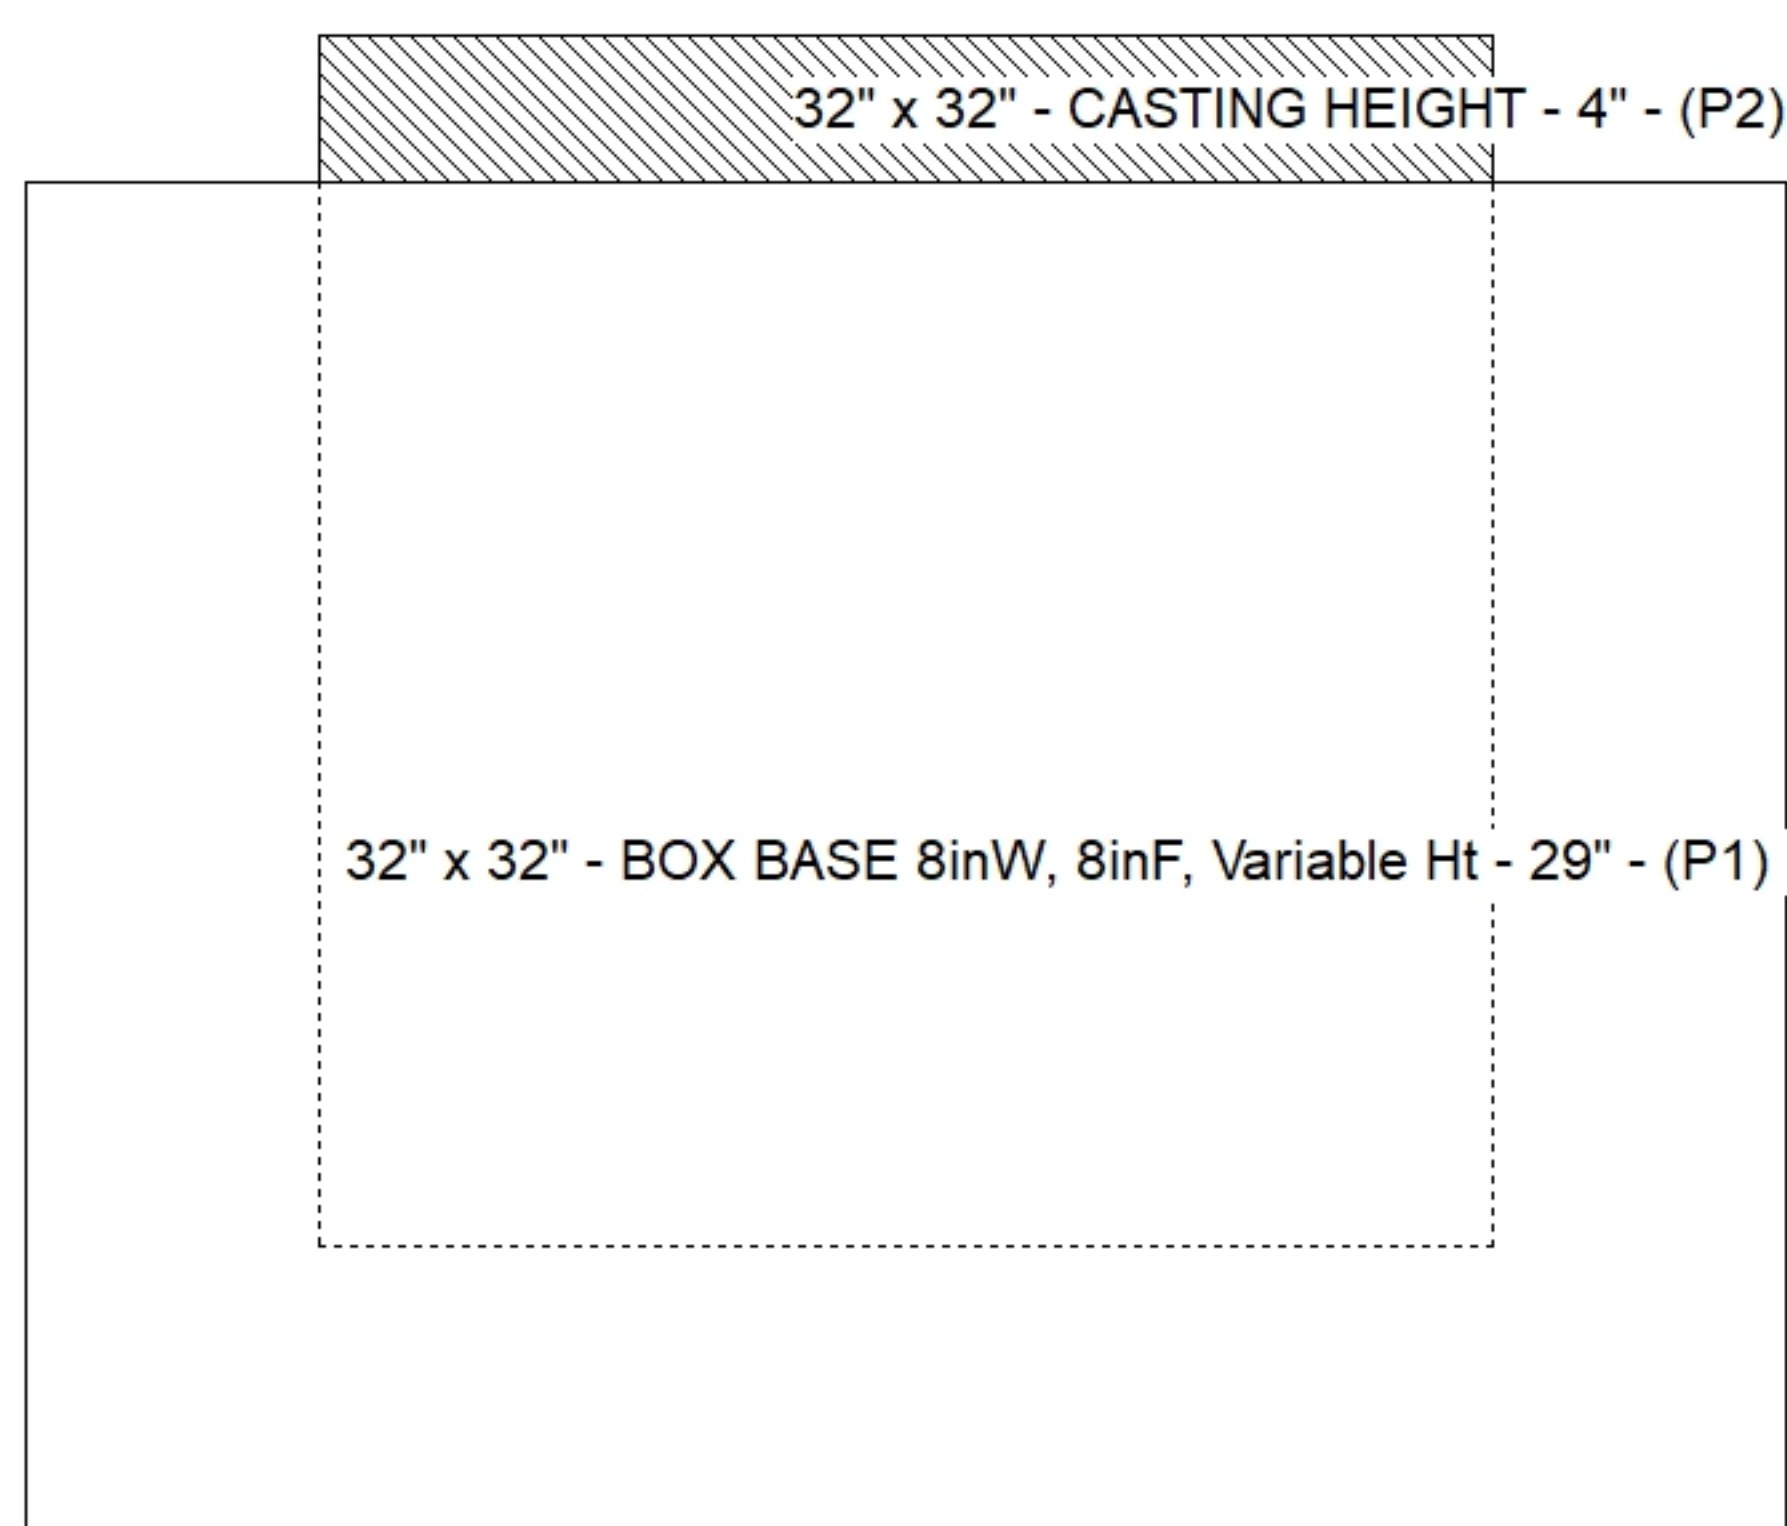

Submittal Drawing
7/2/2026 8:20:34 AM

SUBMITTAL
APPROVED BY:
