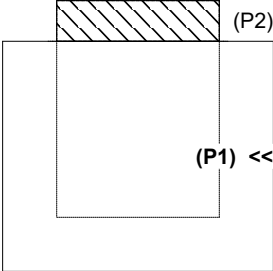
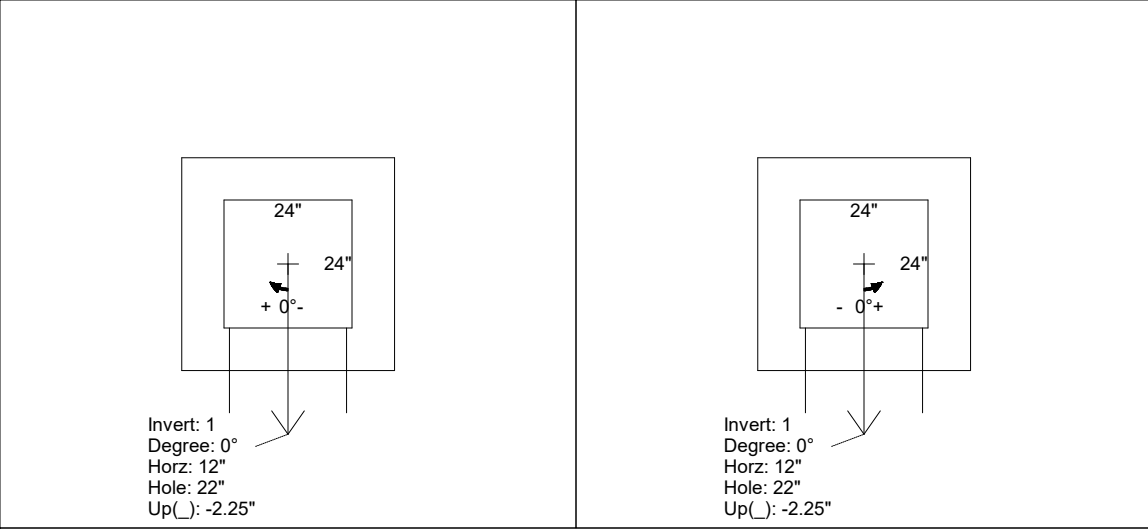
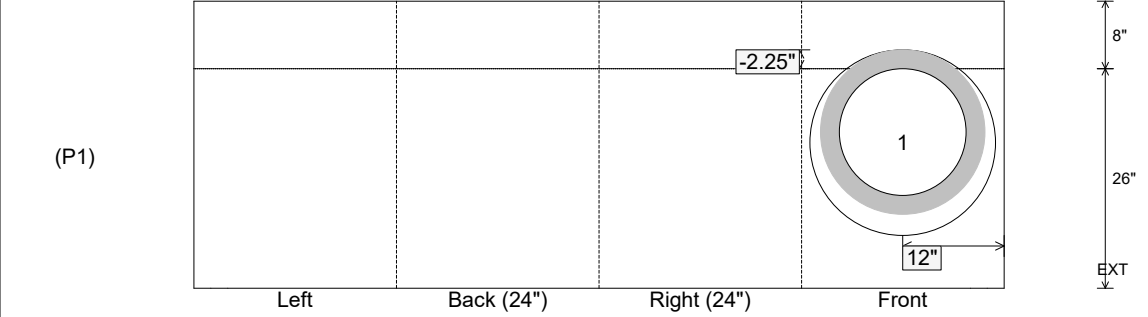


Job Name: 23-2309 - Richland Estates Subdivision Job Location: Portland, TN Contractor: Core & Main LP (BG)					Plant: 100 6/30/2026 8:52:15 AM		Tech: J. Horsley PC: T. Lewis				
Structure ID: 18 ST-SCI											
P1 BX2424-08BAVF BOX BASE 8inW, 8inF, Variable Ht											
P2) 24" x 24" - CASTING HEIGHT - 6" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht - 26" 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 22"						0 lb 3053 lb 0 lb 0 lb ----- Structure Total: 3053 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY OTHERS (NEENAH R-3501 TR/TL). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 806.18' Rim to Invert: 2.83' Slack: 1.96" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	803.35'	0°	20"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-2.25"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)											
 											
INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 26" Height (Ext): 34"		Weight (Net): 3053 lb Volume (Net): 0.78cu.yd		
