

Contractor: Core & Main LP (BG)


TECH: J. Horsley

Plant: 100




Slack: 1.68"


Structure Total: 2914 lb

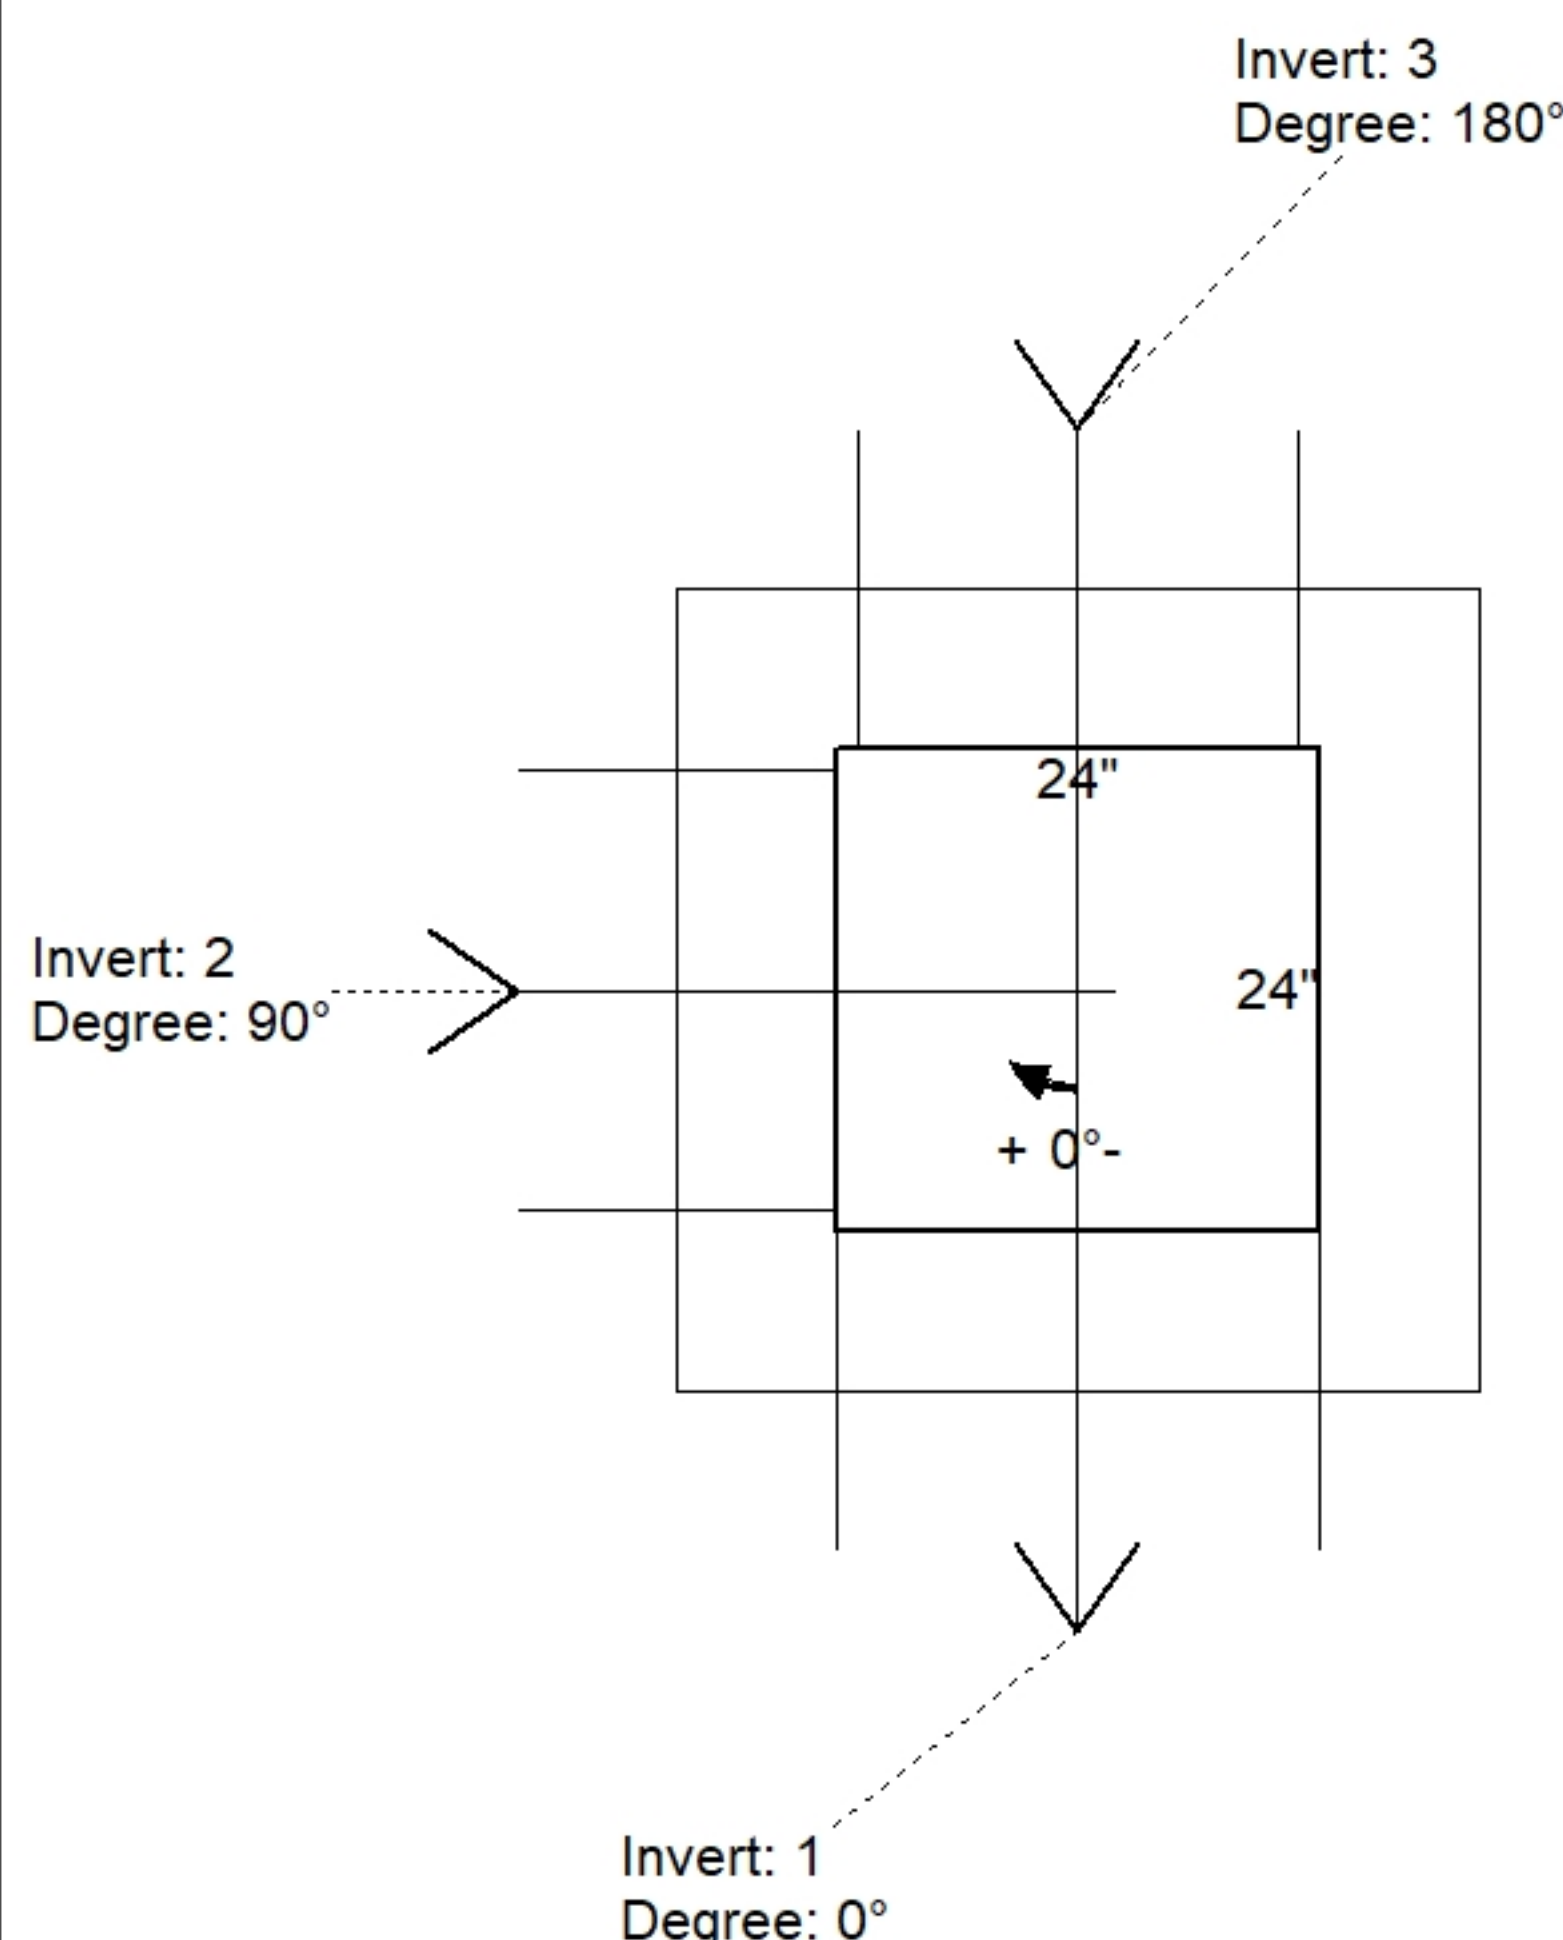

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	808.64'							
Reducer								
Invert 1	805.5'	0°	18" HDPE	21.2"	24"	Hole 24	-1.6"	P1
Invert 2	805.5'	90°	15" RCP B WALL	19.5"	22"	Hole 22	-2.25"	P1
Invert 3	805.5'	180°	15" RCP B WALL	19.5"	22"	Hole 22	-2.25"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

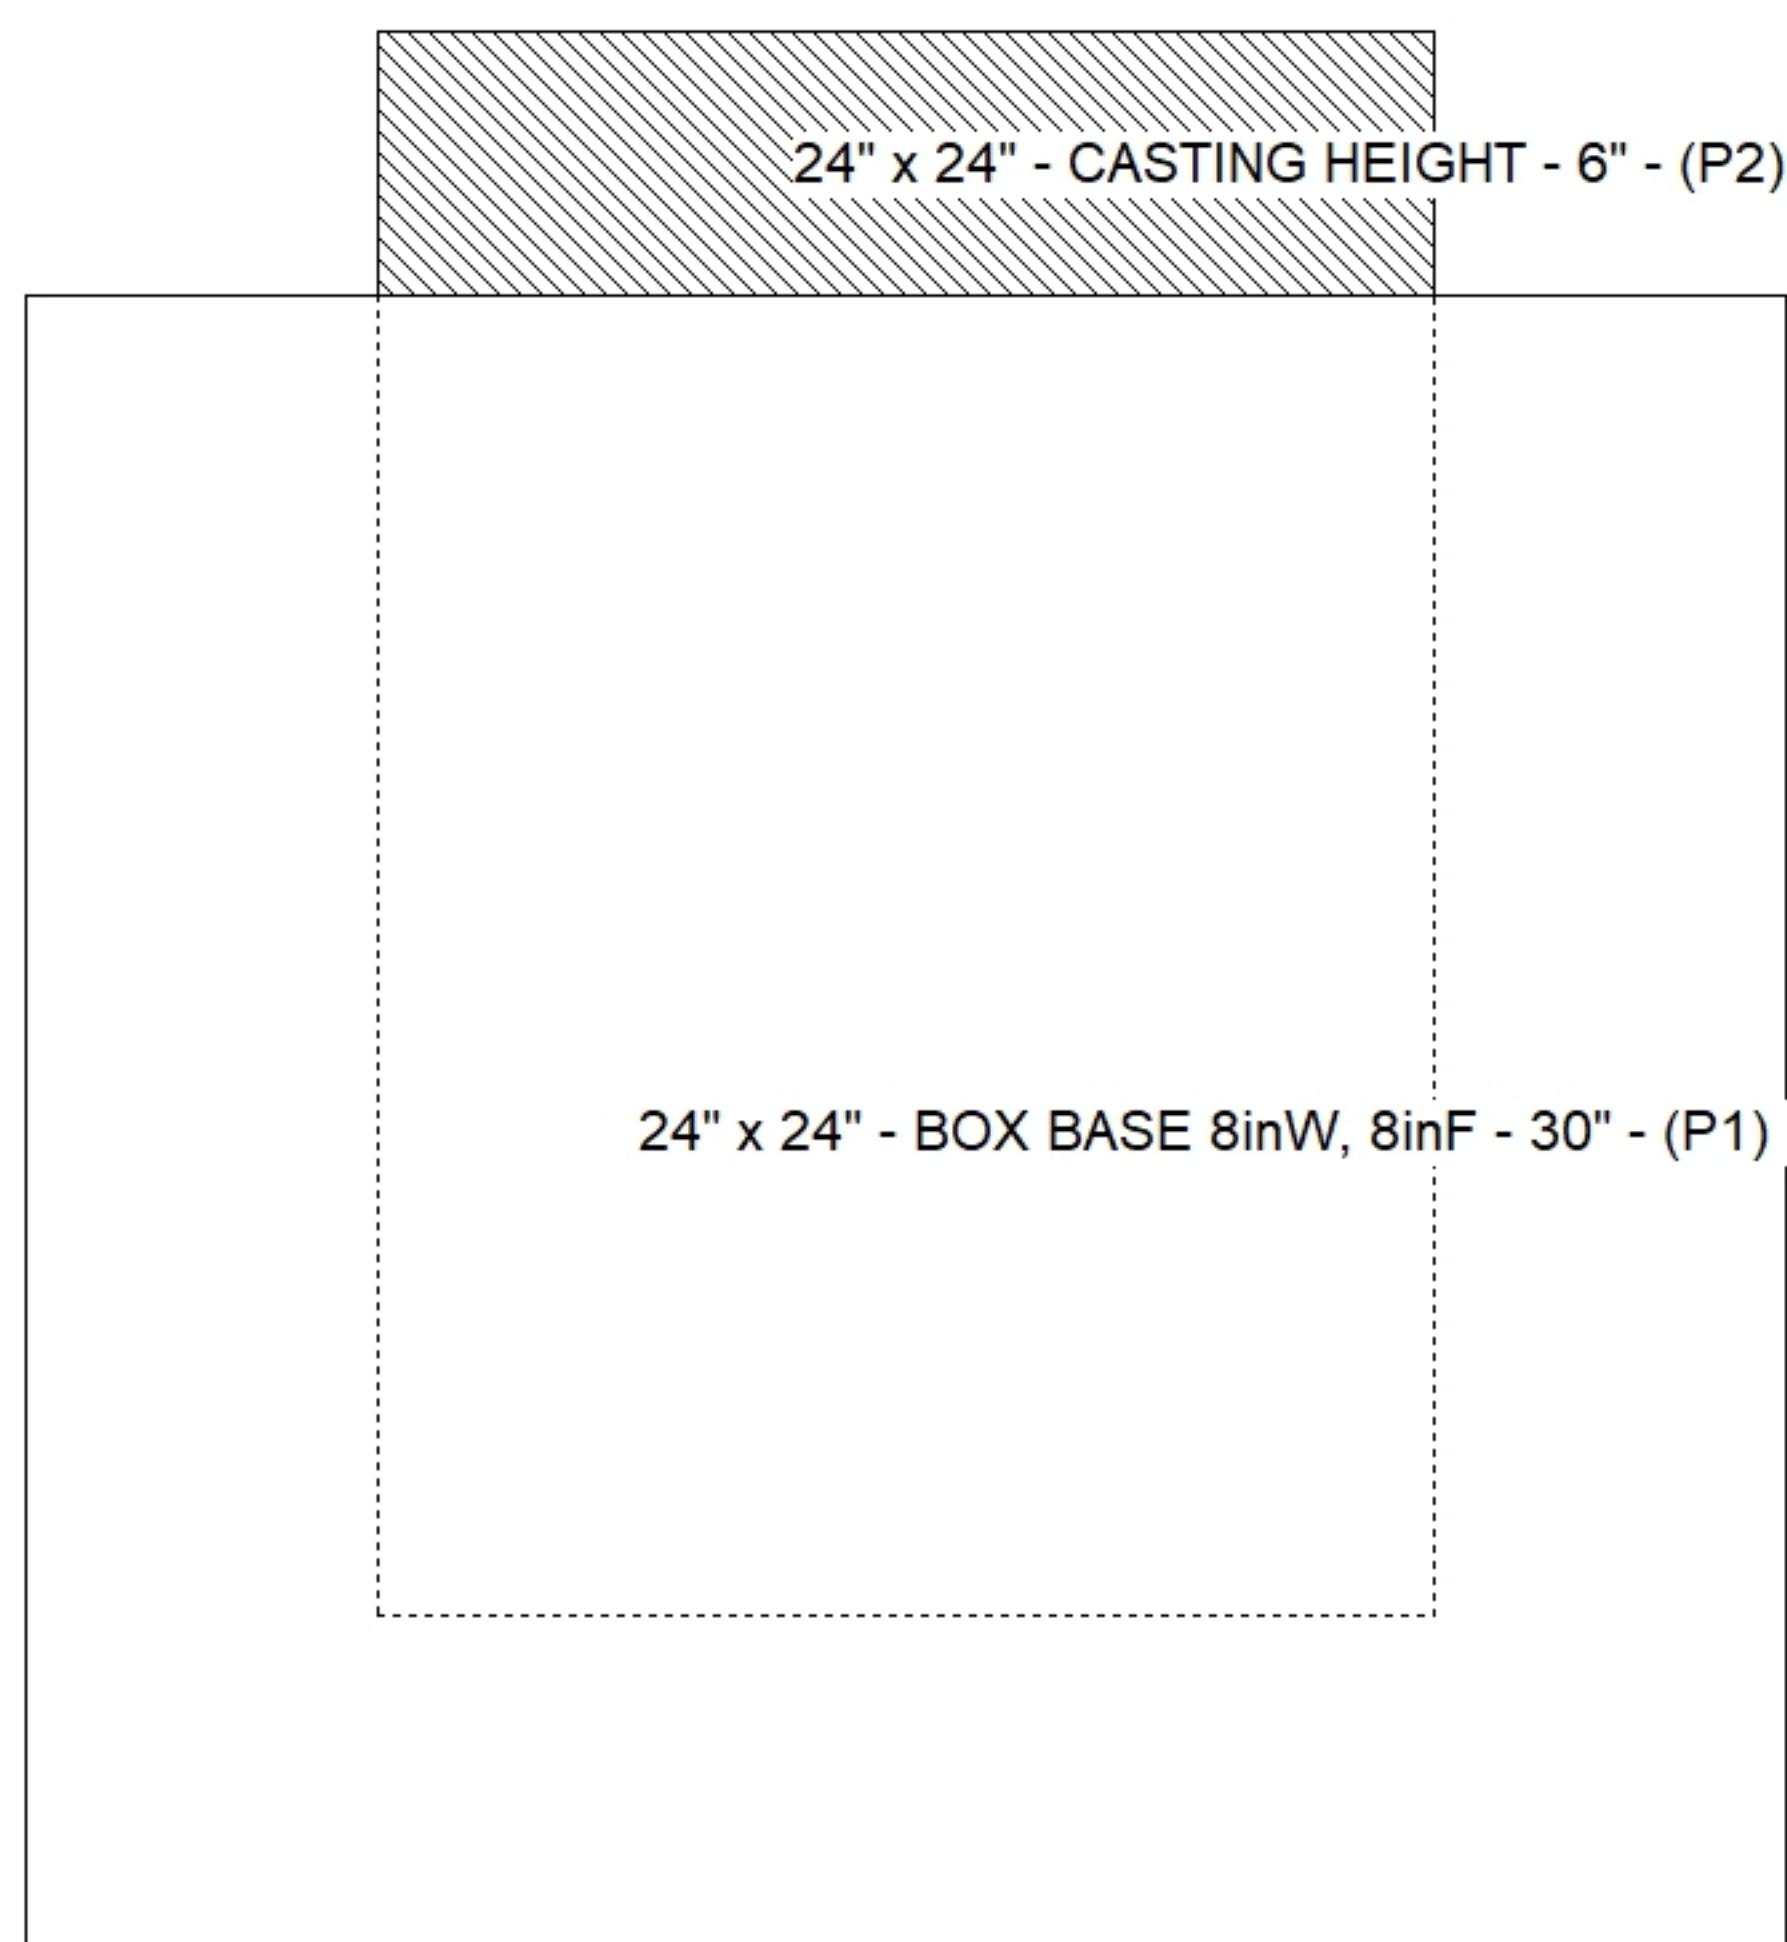

Default - Interior Dimensions

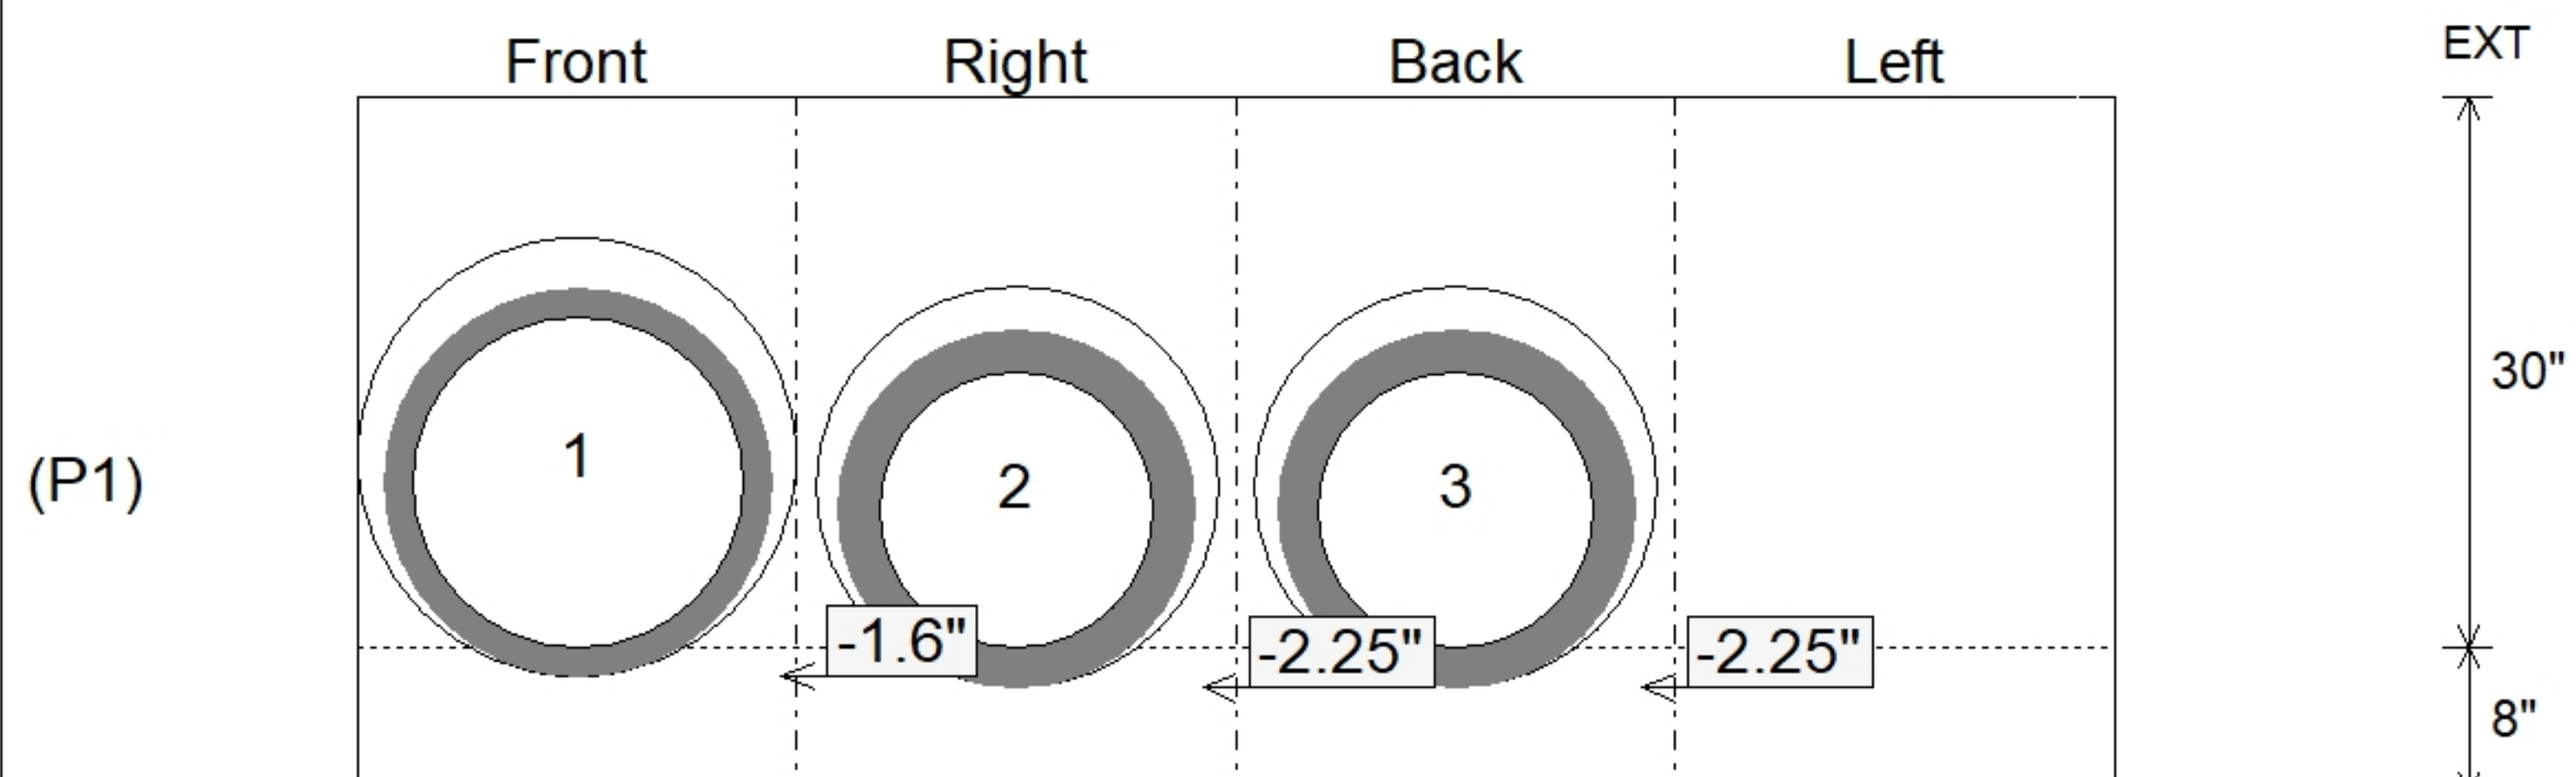

SUBMITTAL
APPROVED BY:
