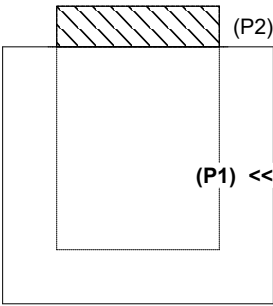
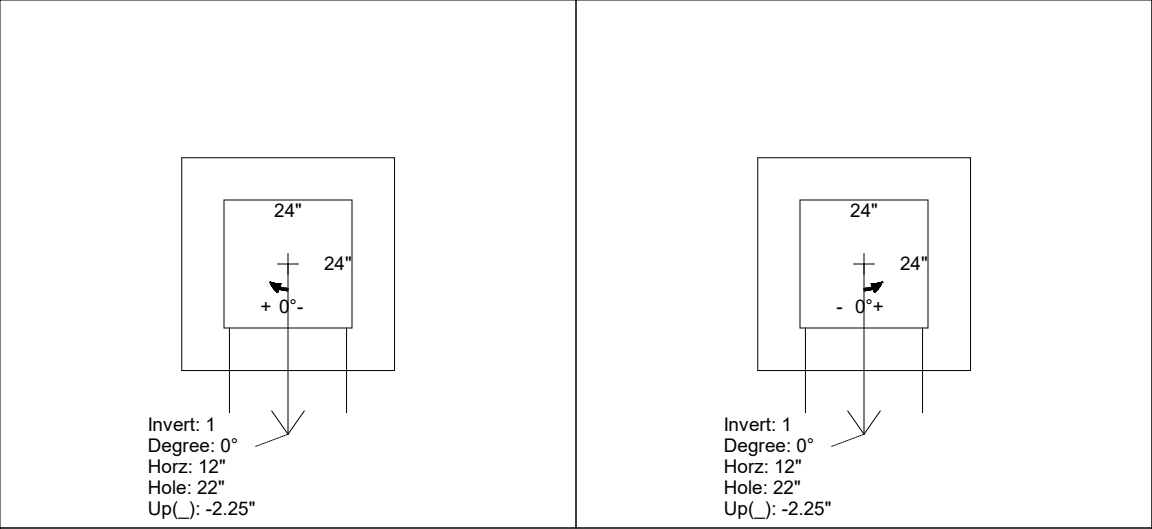
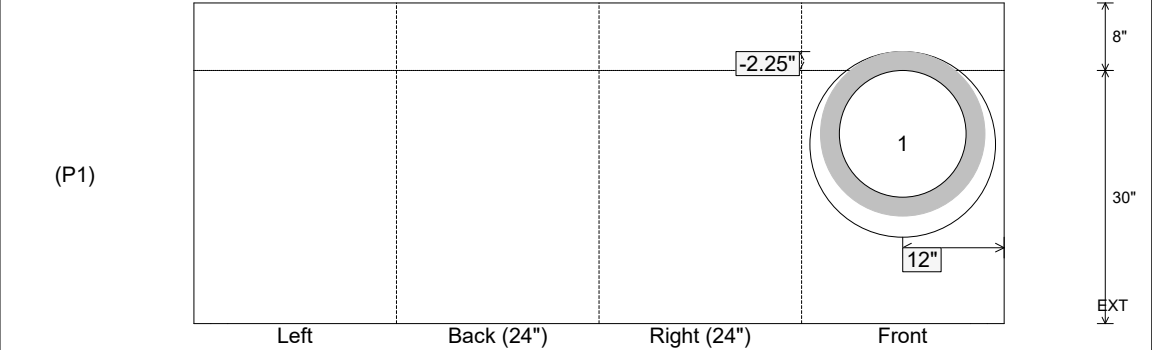


Job Name: 23-2309 - Richland Estates Subdivision Job Location: Portland, TN Contractor: Core & Main LP (BG)					Plant: 100 6/30/2026 8:52:17 AM		Tech: J. Horsley PC: T. Lewis				
Structure ID: 21 ST-SCI											
P1 BX2424-08BA30 BOX BASE 8inW, 8inF											
P2) 24" x 24" - CASTING HEIGHT - 6" P1) 24" x 24" - BOX BASE 8inW, 8inF - 30" 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 22						0 lb 3397 lb 0 lb 0 lb ----- Structure Total: 3397 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY OTHERS (NEENAH R-3501 TR/TL). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 808.64' Rim to Invert: 3.03' Slack: 0.36" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	805.61'	0°	20"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-2.25"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)   INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 30" Height (Ext): 38"		Weight (Net): 3397 lb Volume (Net): 0.87cu.yd		
