


Contractor: Seven Earthmovers LLC

Plant: 100



Slack: 0"

Structure Total: 9324 lb

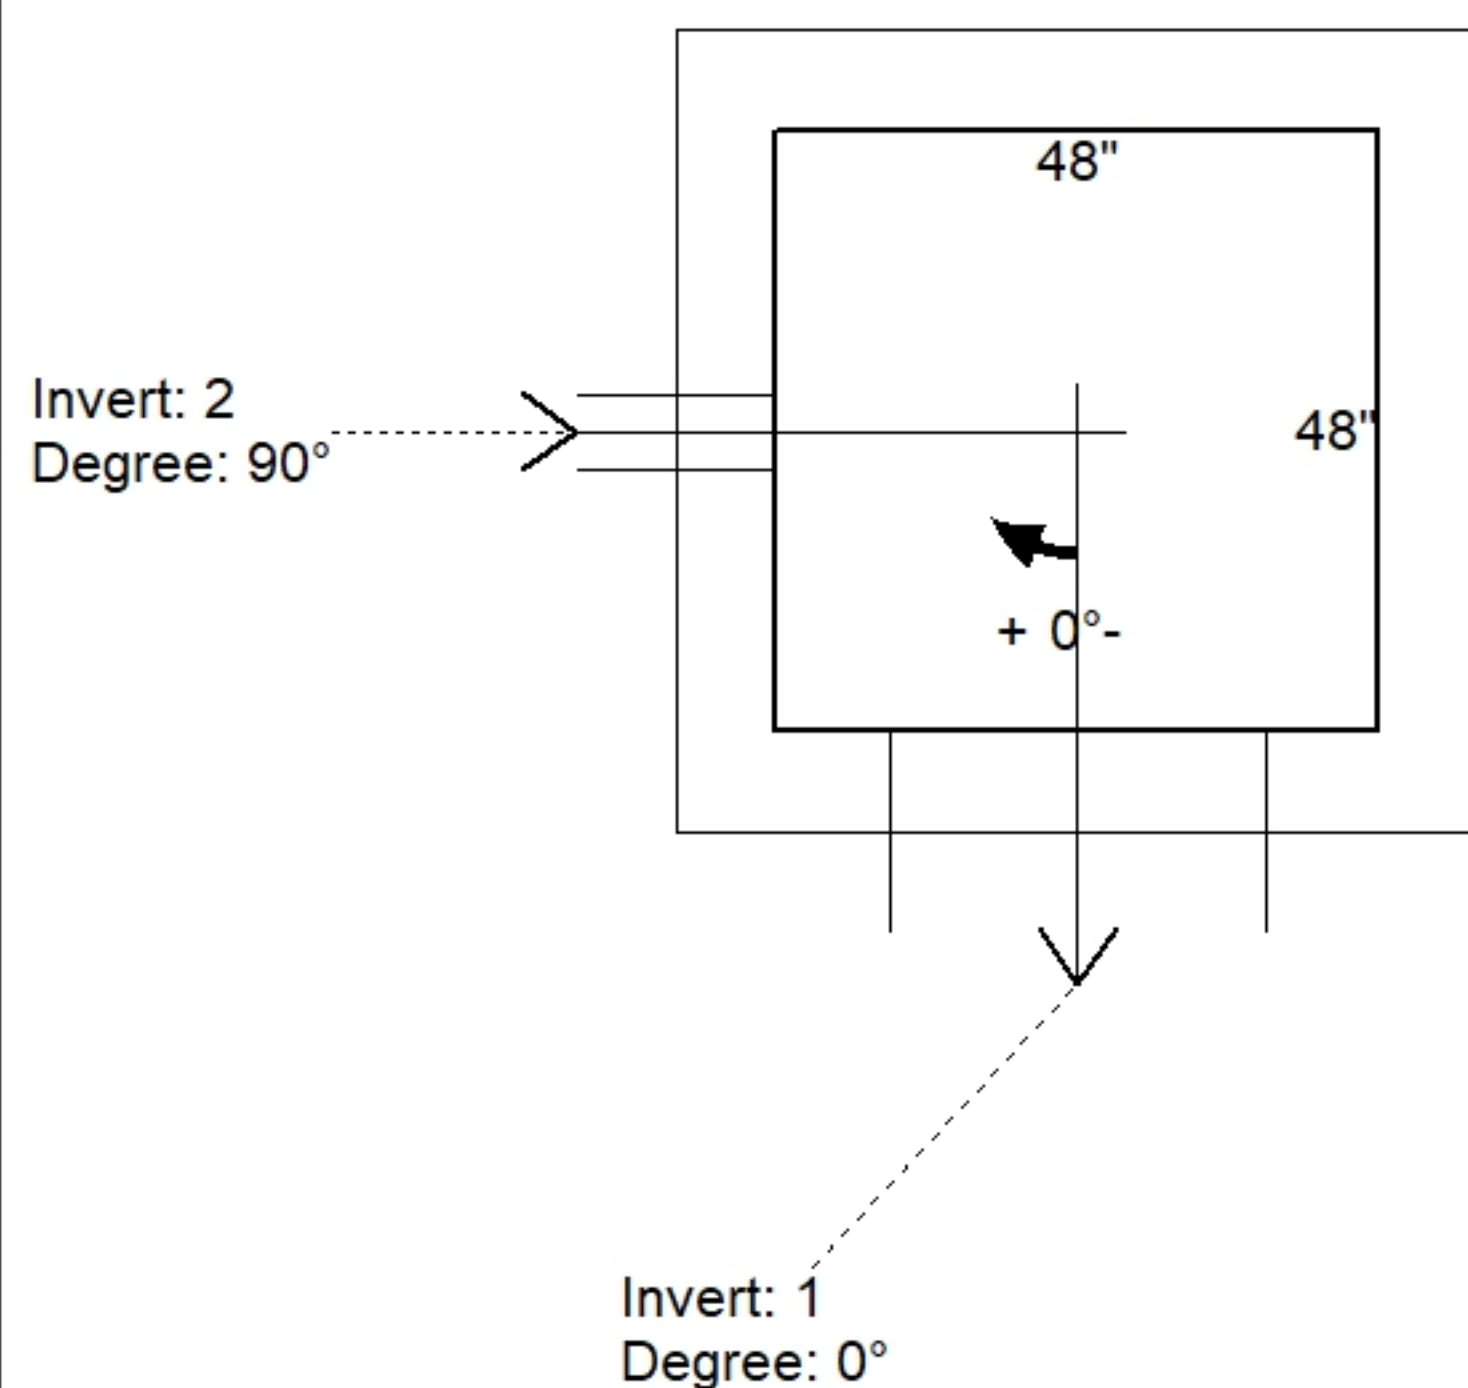


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	862'							
Reducer								
Invert 1	858'	0°	24" HDPE	27.8"	30"	Hole 30	-1.875"	P1
Invert 2	858'	90°	4" HDPE (perf pipe)	4.8"	6"	Hole 6	-0.375"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

48" x 48" - CASTING HEIGHT - 1" - (P2)

48" x 48" - BOX BASE 8inW, 8inF, Variable Ht F/n - 47" - (P1)

The diagram shows a rectangular box with a dashed outline. The top edge is labeled "48" x 48" - CASTING HEIGHT - 1" - (P2)". The bottom edge is labeled "48" x 48" - BOX BASE 8inW, 8inF, Variable Ht F/n - 47" - (P1)".

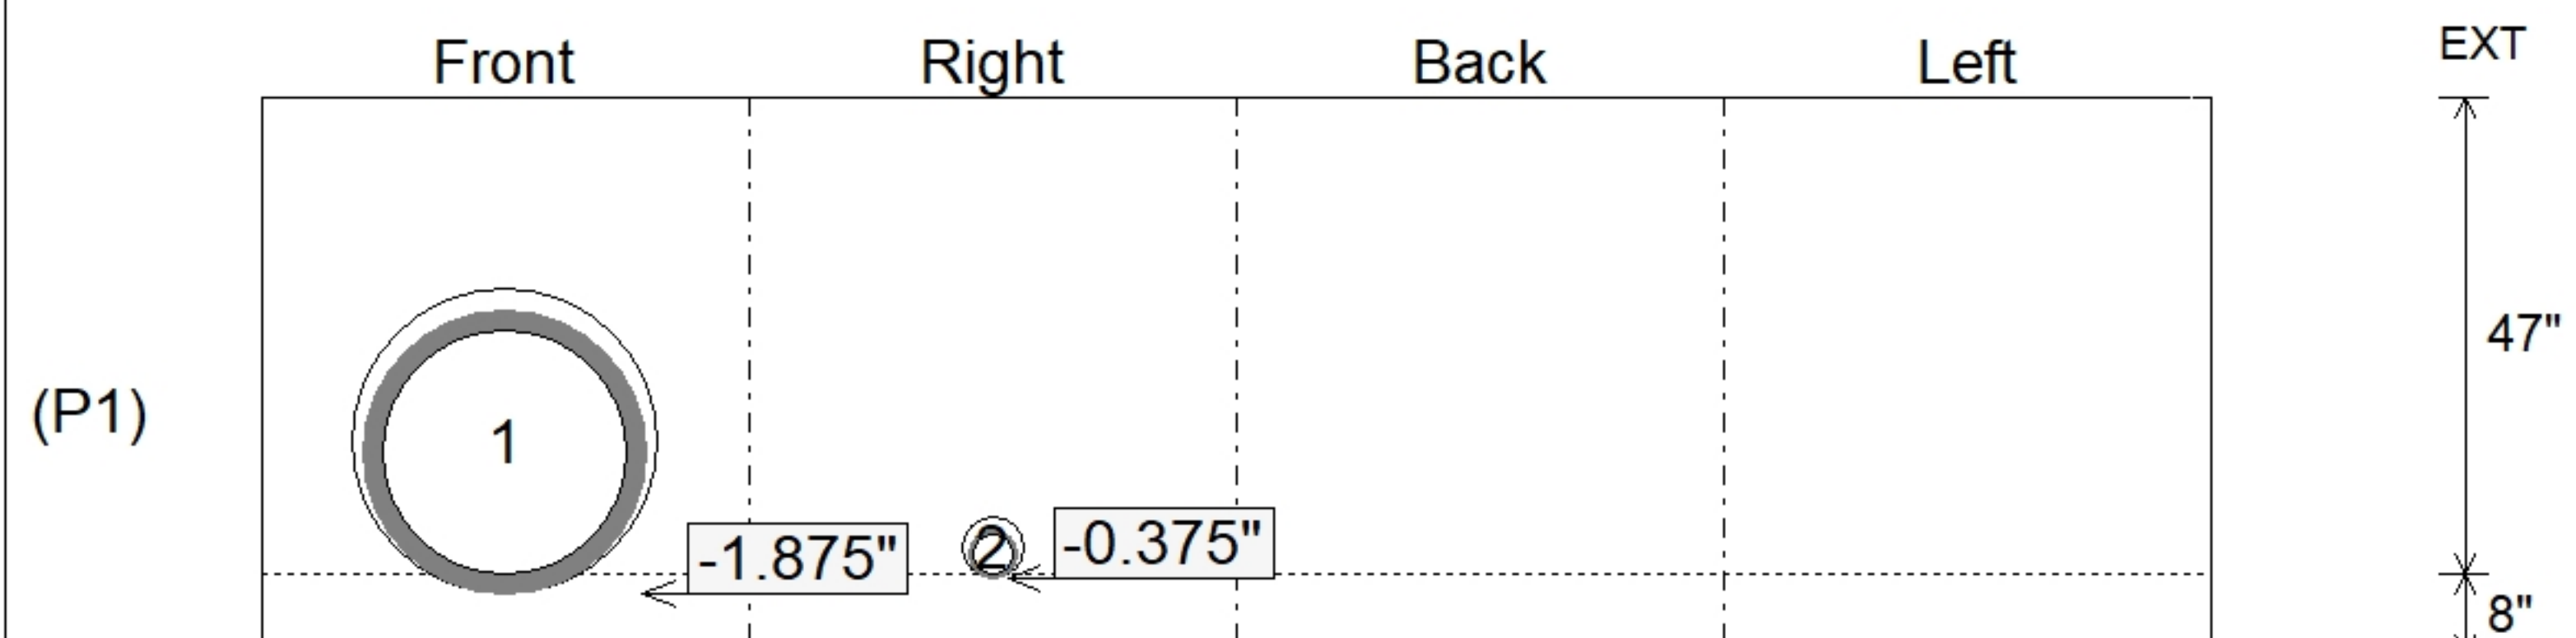

SUBMITTAL
APPROVED BY:
