
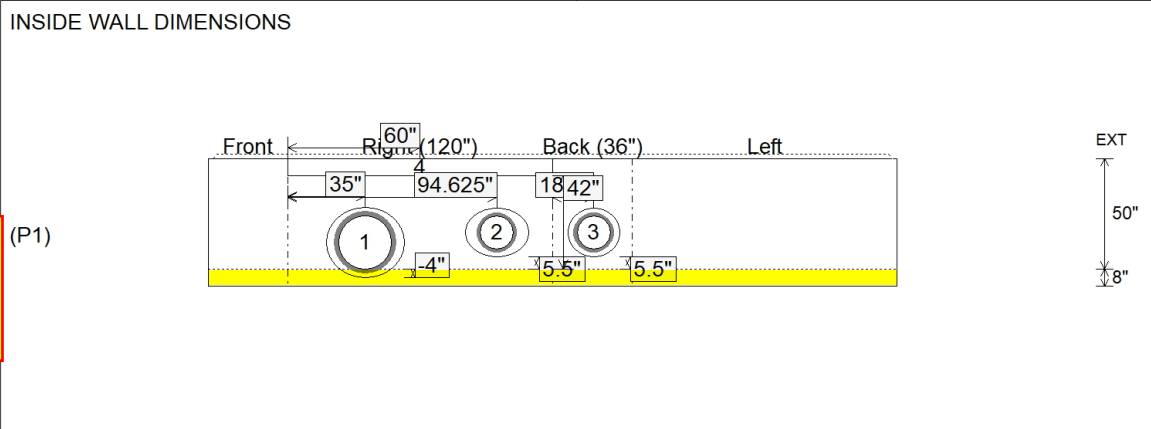
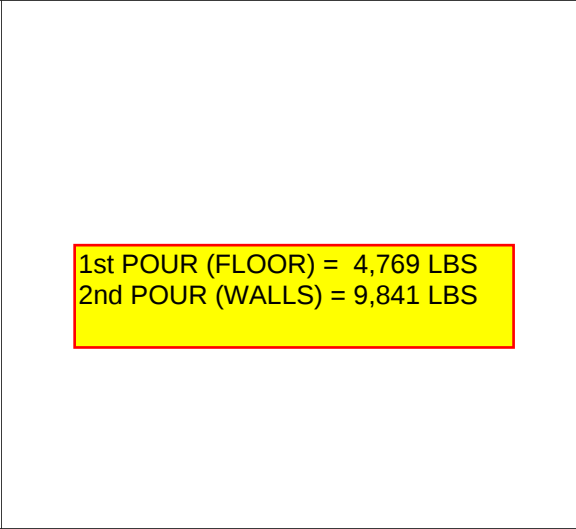
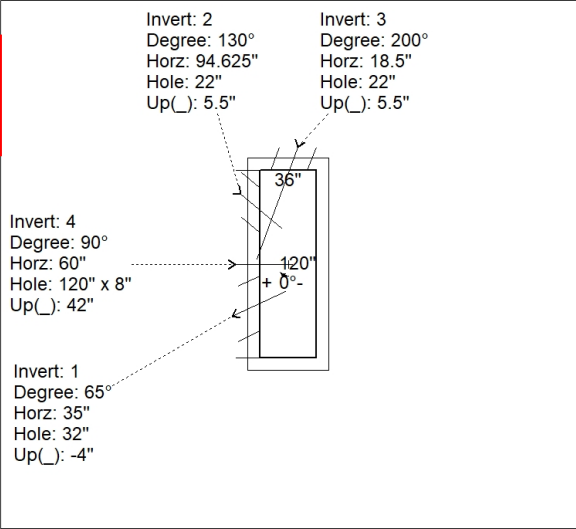


Job Name: 23-2404 Hampton Hills (Phase 1) Job Location: Richmond, KY Contractor: Seven Earthmovers LLC					Plant: 100 5/19/2026 12:59:18 PM		Tech: J. Horsley PC: C. Golf					
Structure ID: CBI-C3												
P1 BX36120-08VF		BOX BASE 8inW, 8inF, Variable Ht T/n										
P2) 36" x 120" - CB INLET KY A 10' TOP SAG F/G - 10" P1) 36" x 120" - BOX BASE 8inW, 8inF, Variable Ht T/n - 50" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) Hole - 32 2) Hole - 22 1) Horiz Slot n/n - 120"x8"					4866 lb 14610 lb 206 lb 0 lb 0 lb 0 lb Structure Total: 19682 lb		<u>Structure Notes:</u> 1. PER KYTC CBI A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING (HOE KY-206) TO BE CAST INTO TOP PHASE. REINFORCING PER ASTM AS615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - BASE WALLS (As .31) #5 BARS AT 12" C.C.E.W. - BASE FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 885.29'					Rim to Invert: 5'		Slack: 0"		Sump: 0"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	880.29'	65°	39.375"	24" ADS N-12	28"	Hole 32	32"	35.308"	-4"	-15"		
Invert 2	881.04'	130°	109.375"	15" ADS N-12	18"	Hole 22	22"	28.719"	5.5"	15"		
Invert 3	881.04'	200°	29.5"	15" ADS N-12	18"	Hole 22	22"	23.412"	5.5"	-20"		
Invert 4	883.79'	90°	68"	120" x 8" Horiz Slot	120" x 8"	Horiz Slot 120"x8"	120" x 8"	120"	42"	0"		
Invert 5												
Invert 6												
Invert 7												
Invert 8												
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimensions) STUB \$5 BARS 20" OU TO OF SLOT, PET KY A CBI SPEC'S 1st POUR (FLOOR) = 4,769 LBS 2nd POUR (WALLS) = 9,841 LBS INSIDE WALL DIMENSIONS 1st POUR (FLOOR) STUB #5 L BARS OUT TOP OF FLOOR FOR CONNECTING WALLS 												
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 50" Height (Ext): 58"		Weight (Net): 14610 lb Volume (Net): 3.73cu.yd		


Job Name: 23-2404 Hampton Hills (Phase 1) Job Location: Richmond, KY Contractor: Seven Earthmovers LLC					Plant: 100 5/19/2026 12:59:18 PM		Tech: J. Horsley PC: C. Golf				
Structure ID: CBI-C3											
P1A BX36120-08VF		BOX BASE 8inW, 8inF, Variable Ht T/n									
P2) 36" x 120" - CB INLET KY A 10' TOP SAG F/G - 10" P1) 36" x 120" - BOX BASE 8inW, 8inF, Variable Ht T/n - 50" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) Hole - 32 2) Hole - 22 1) Horiz Slot n/n - 120"x8"					4866 lb 14610 lb 206 lb 0 lb 0 lb 0 lb Structure Total: 19682 lb		<u>Structure Notes:</u> 1. PER KYTC CBI A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING (HOE KY-206) TO BE CAST INTO TOP PHASE. REINFORCING PER ASTM AS615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - BASE WALLS (As .31) #5 BARS AT 12" C.C.E.W. - BASE FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 885.29'		Rim to Invert: 5'		Slack: 0"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	880.29'	65°	39.375"	24" ADS N-12	28"	Hole 32	32"	35.308"	-4"	-15"	
Invert 2	881.04'	130°	109.375"	15" ADS N-12	18"	Hole 22	22"	28.719"	5.5"	15"	
Invert 3	881.04'	200°	29.5"	15" ADS N-12	18"	Hole 22	22"	23.412"	5.5"	-20"	
Invert 4	883.79'	90°	68"	120" x 8" Horiz Slot	120" x 8"	Horiz Slot 120"x8"	120" x 8"	120"	42"	0"	
Invert 5											
Invert 6											
Invert 7											
Invert 8											

STUB \$5 BARS 20" OU TO OF SLOT, PET KY A CBI SPEC'S

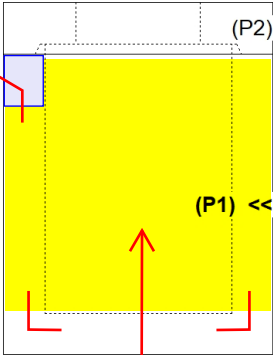


2nd POUR (WALLS)

RIGHT-SIDE UP VIEW (int. dimensions)

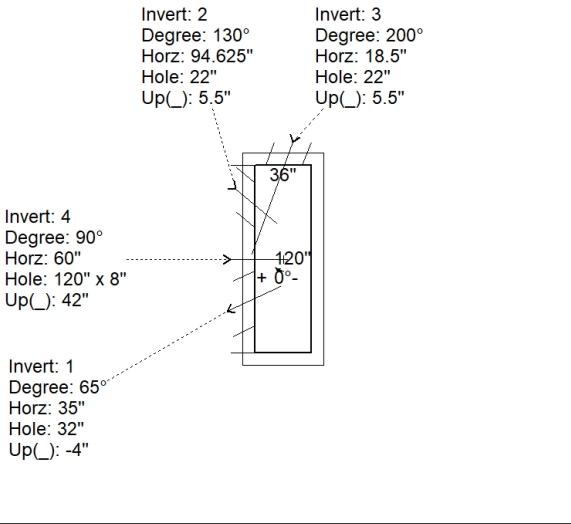

INSIDE WALL DIMENSIONS



1st POUR (FLOOR) = 4,769 LBS
2nd POUR (WALLS) = 9,841 LBS
