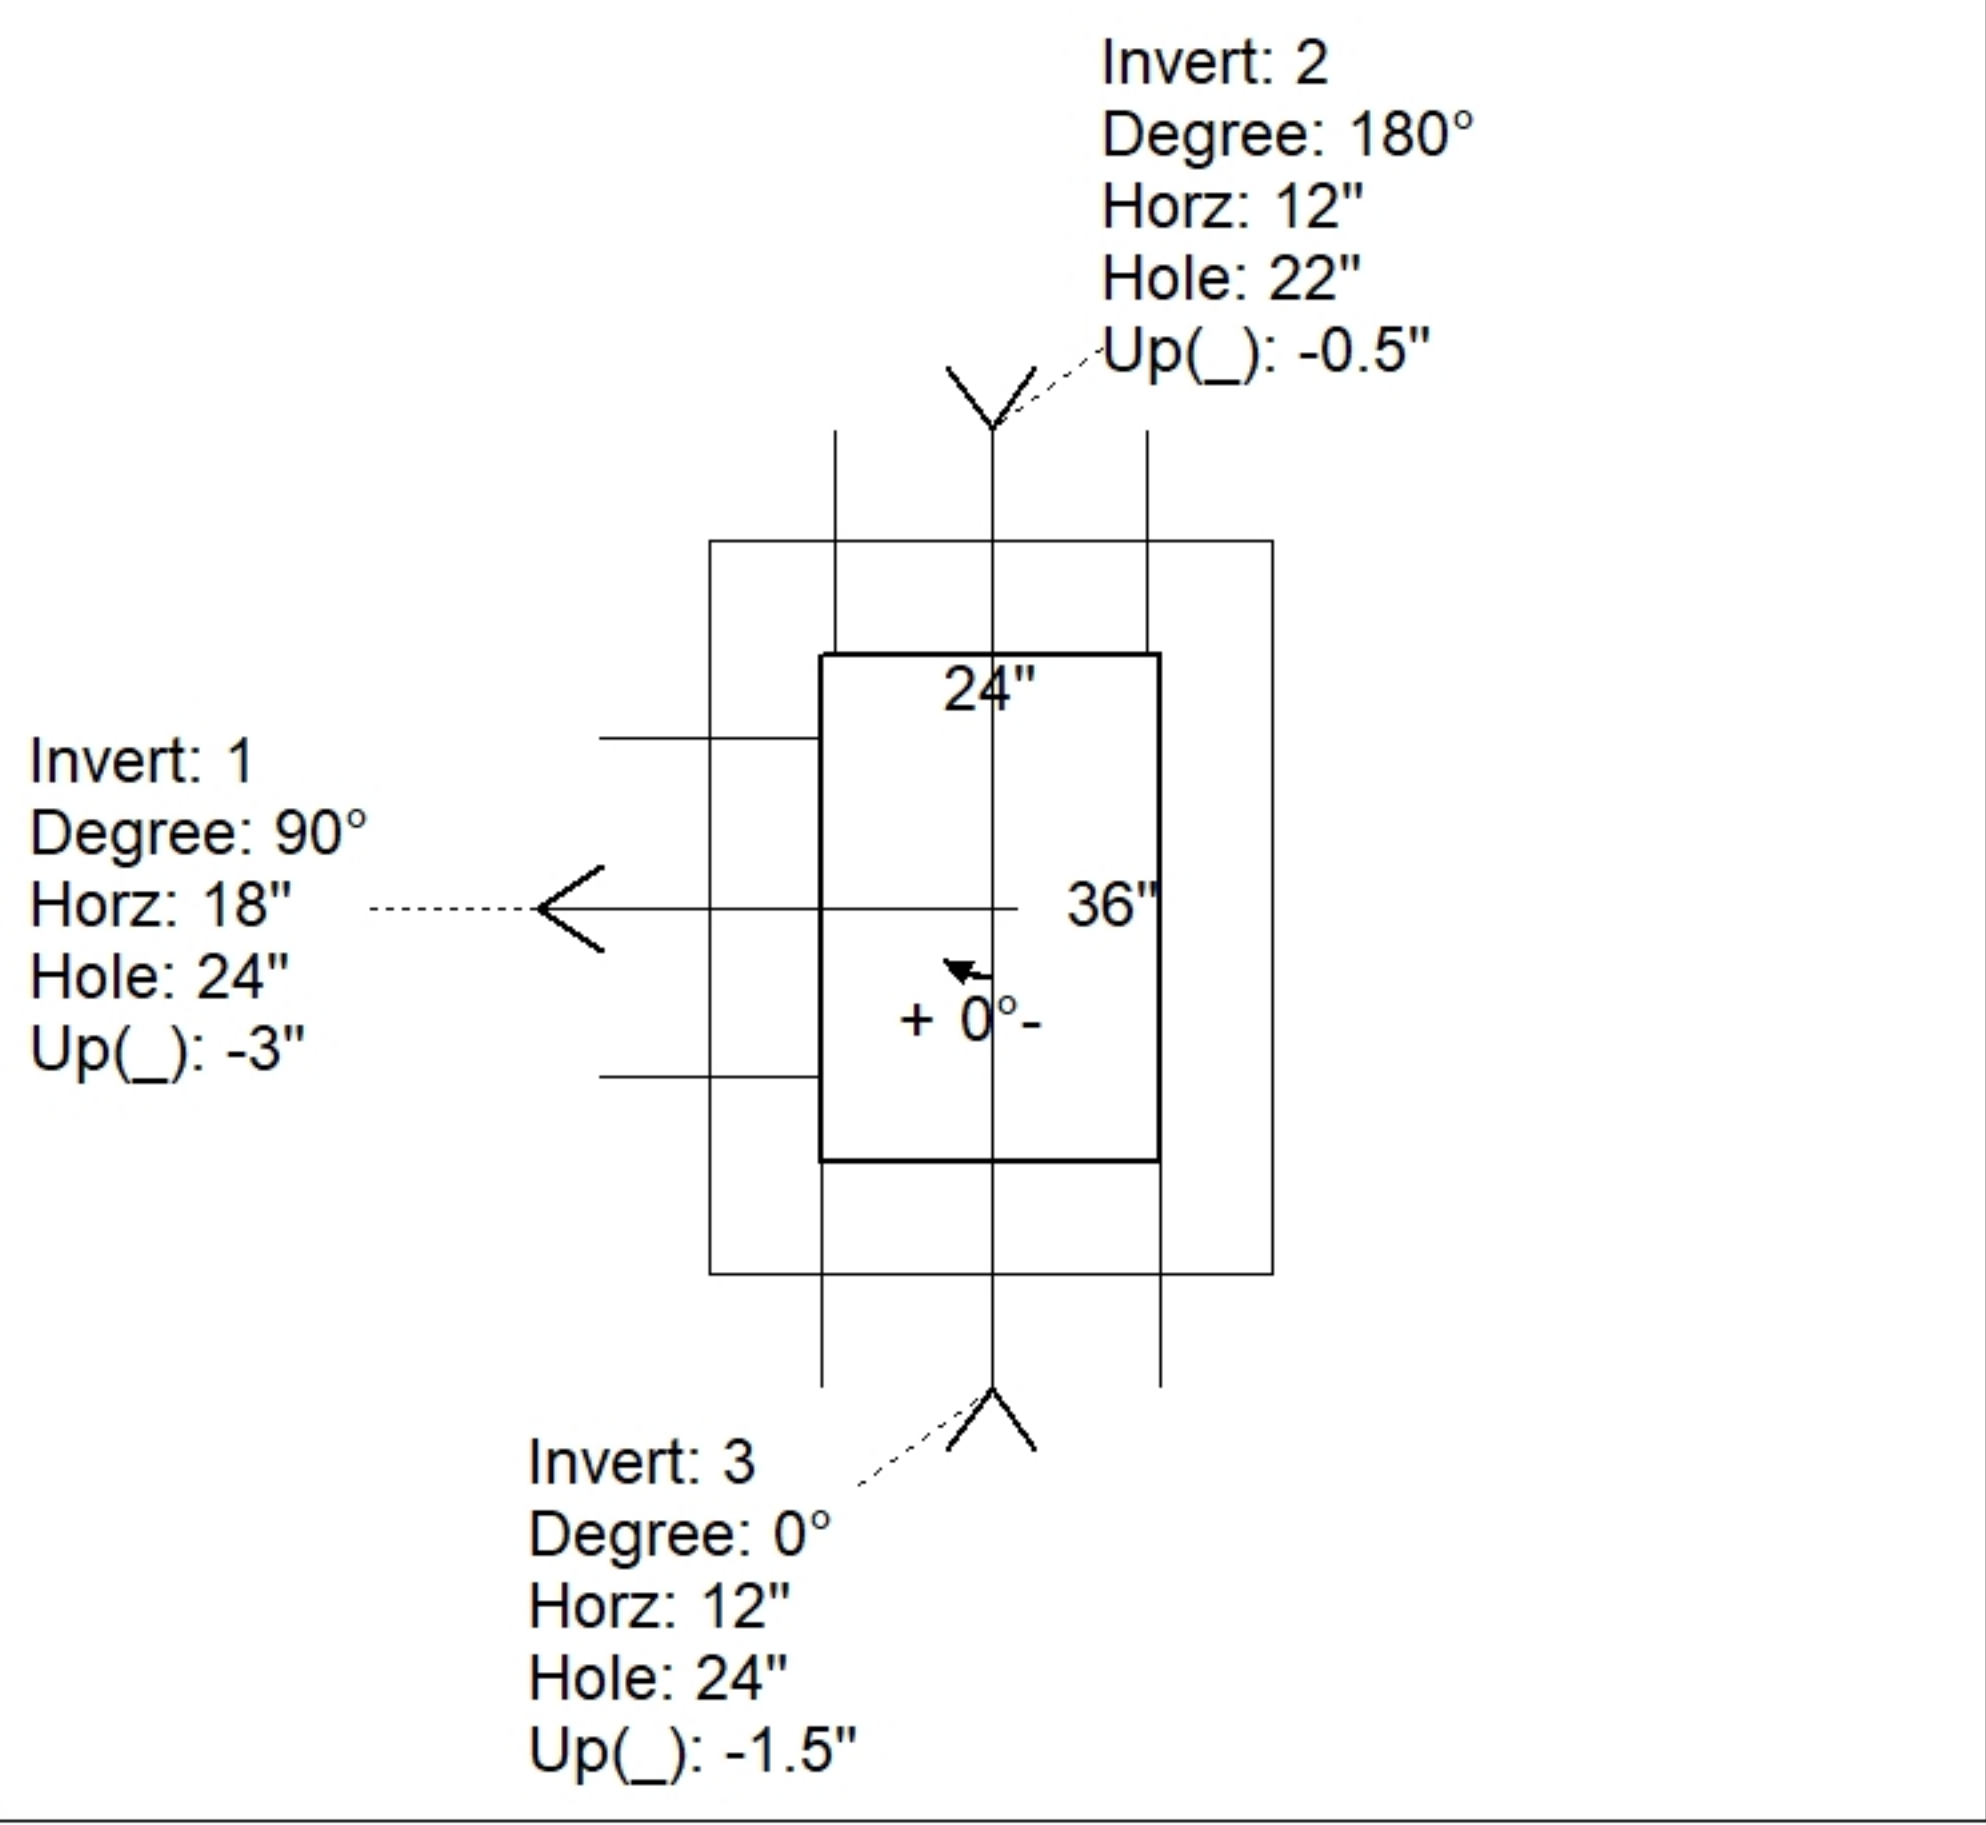
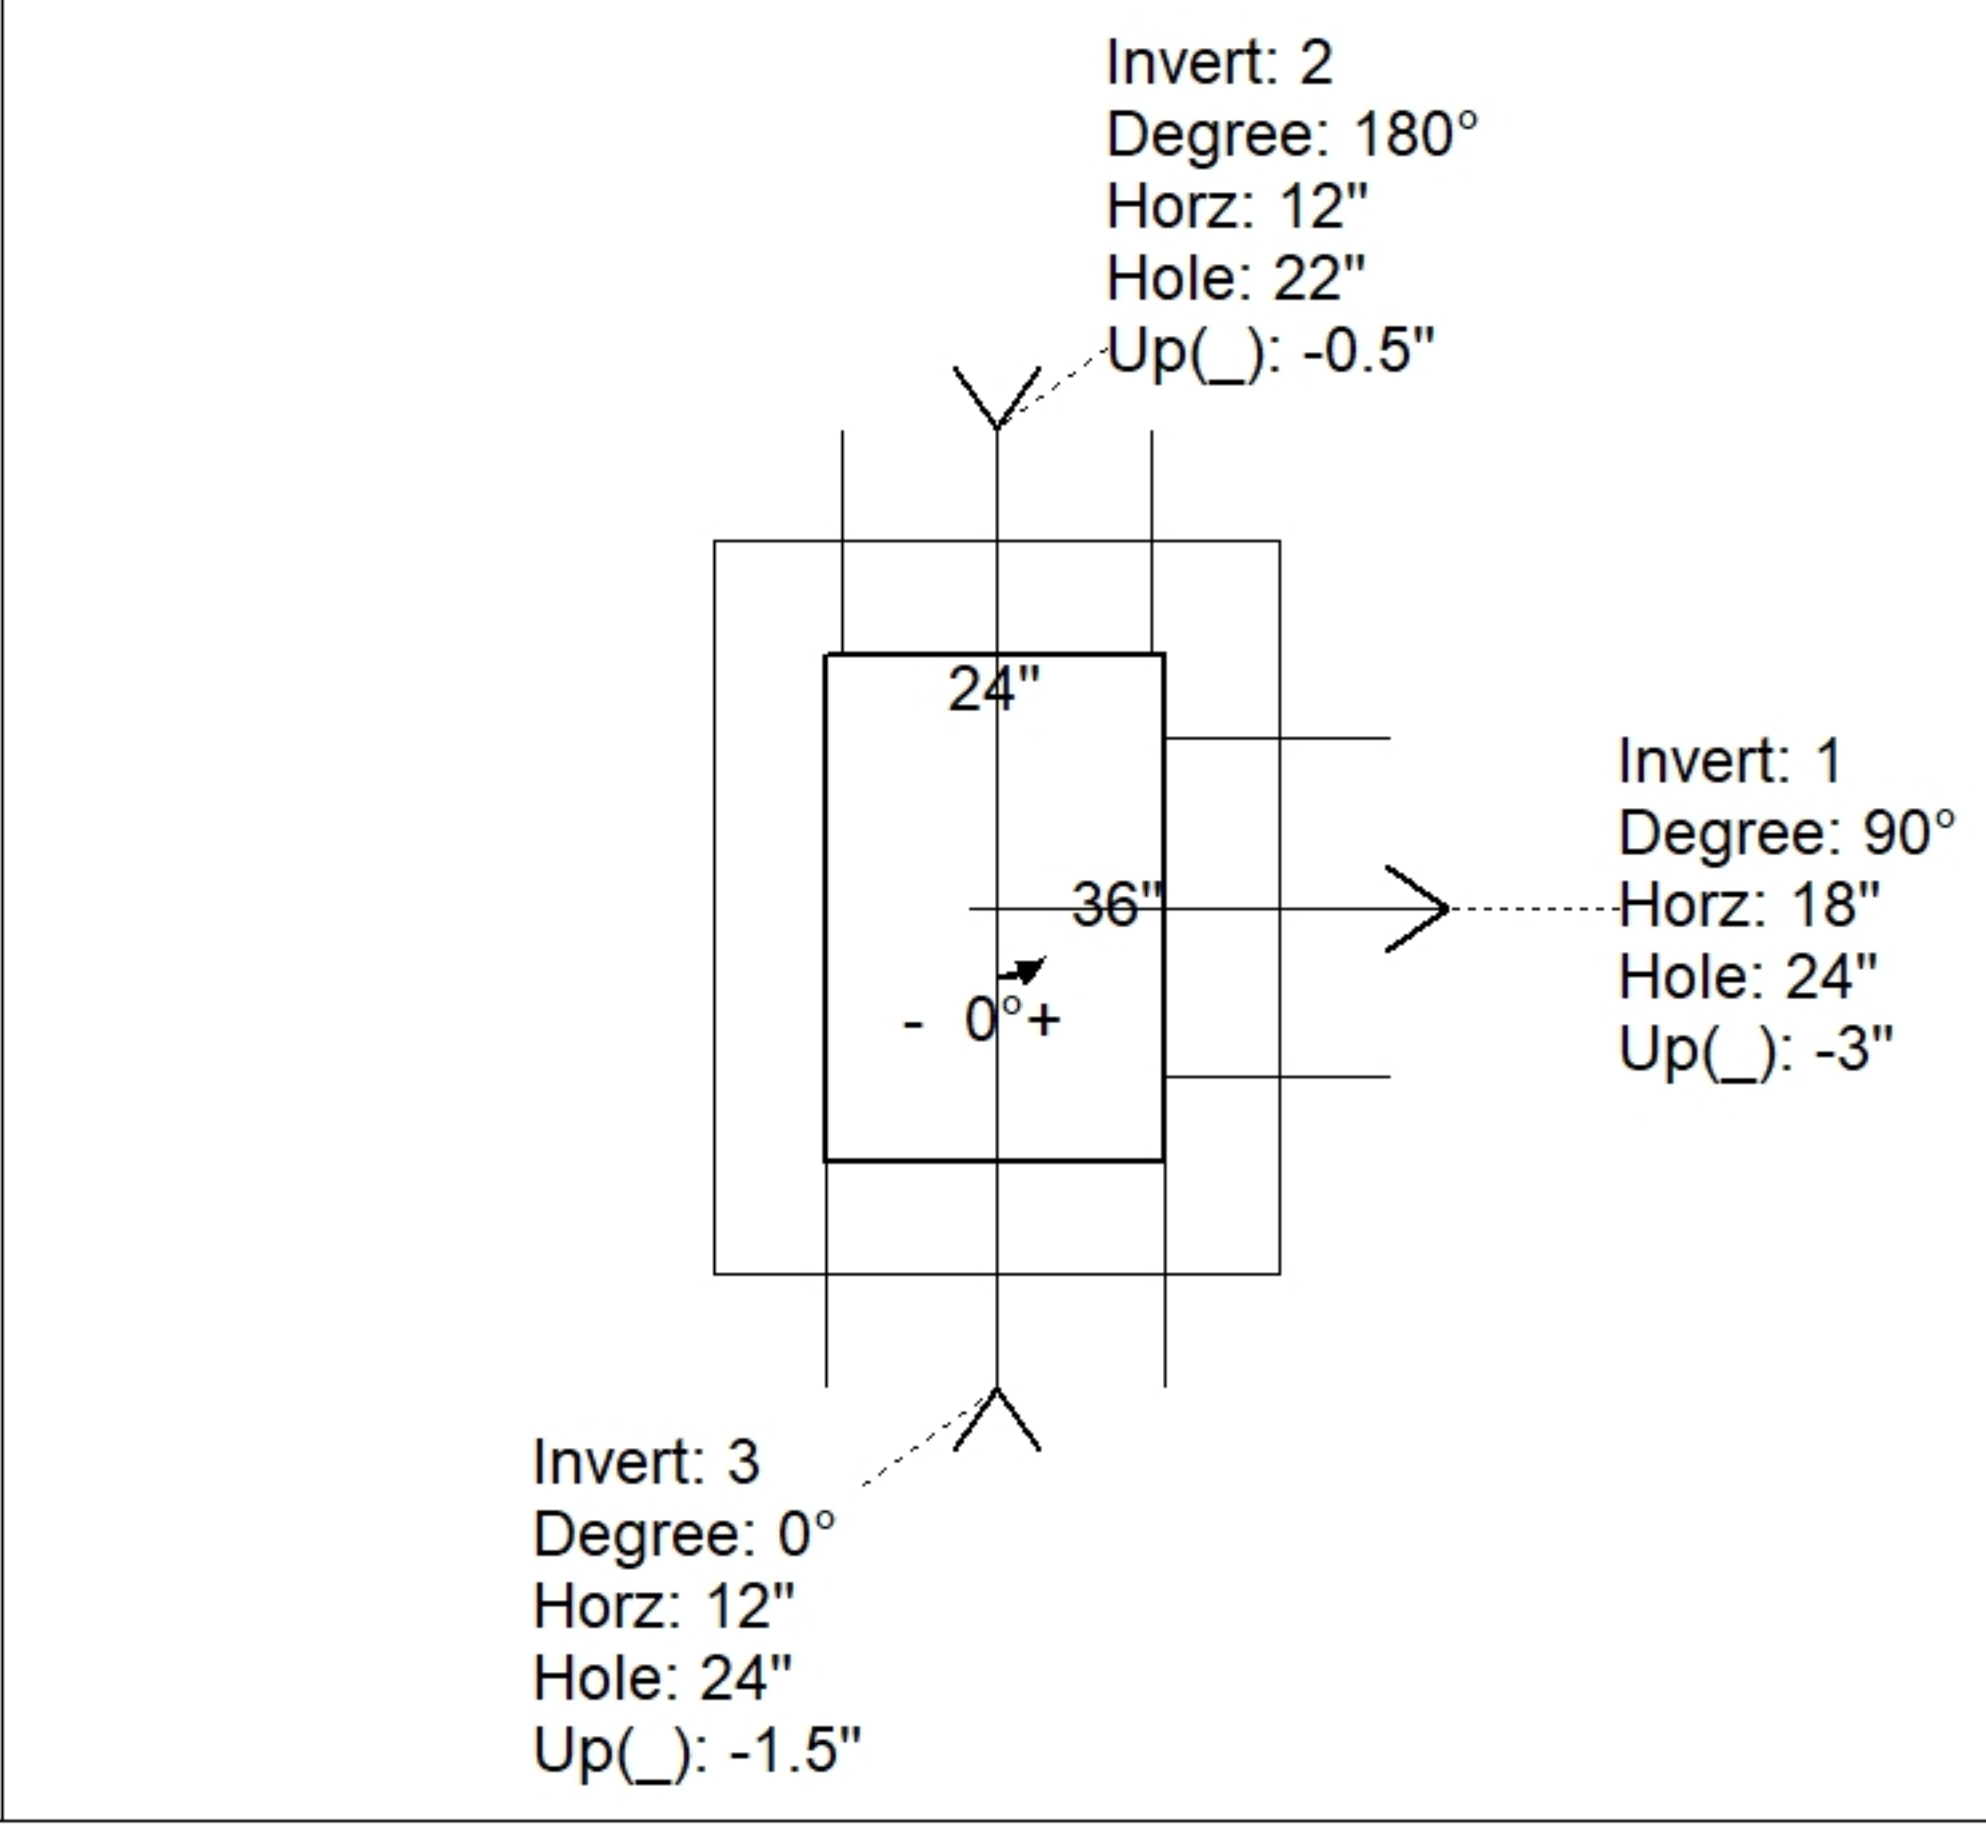
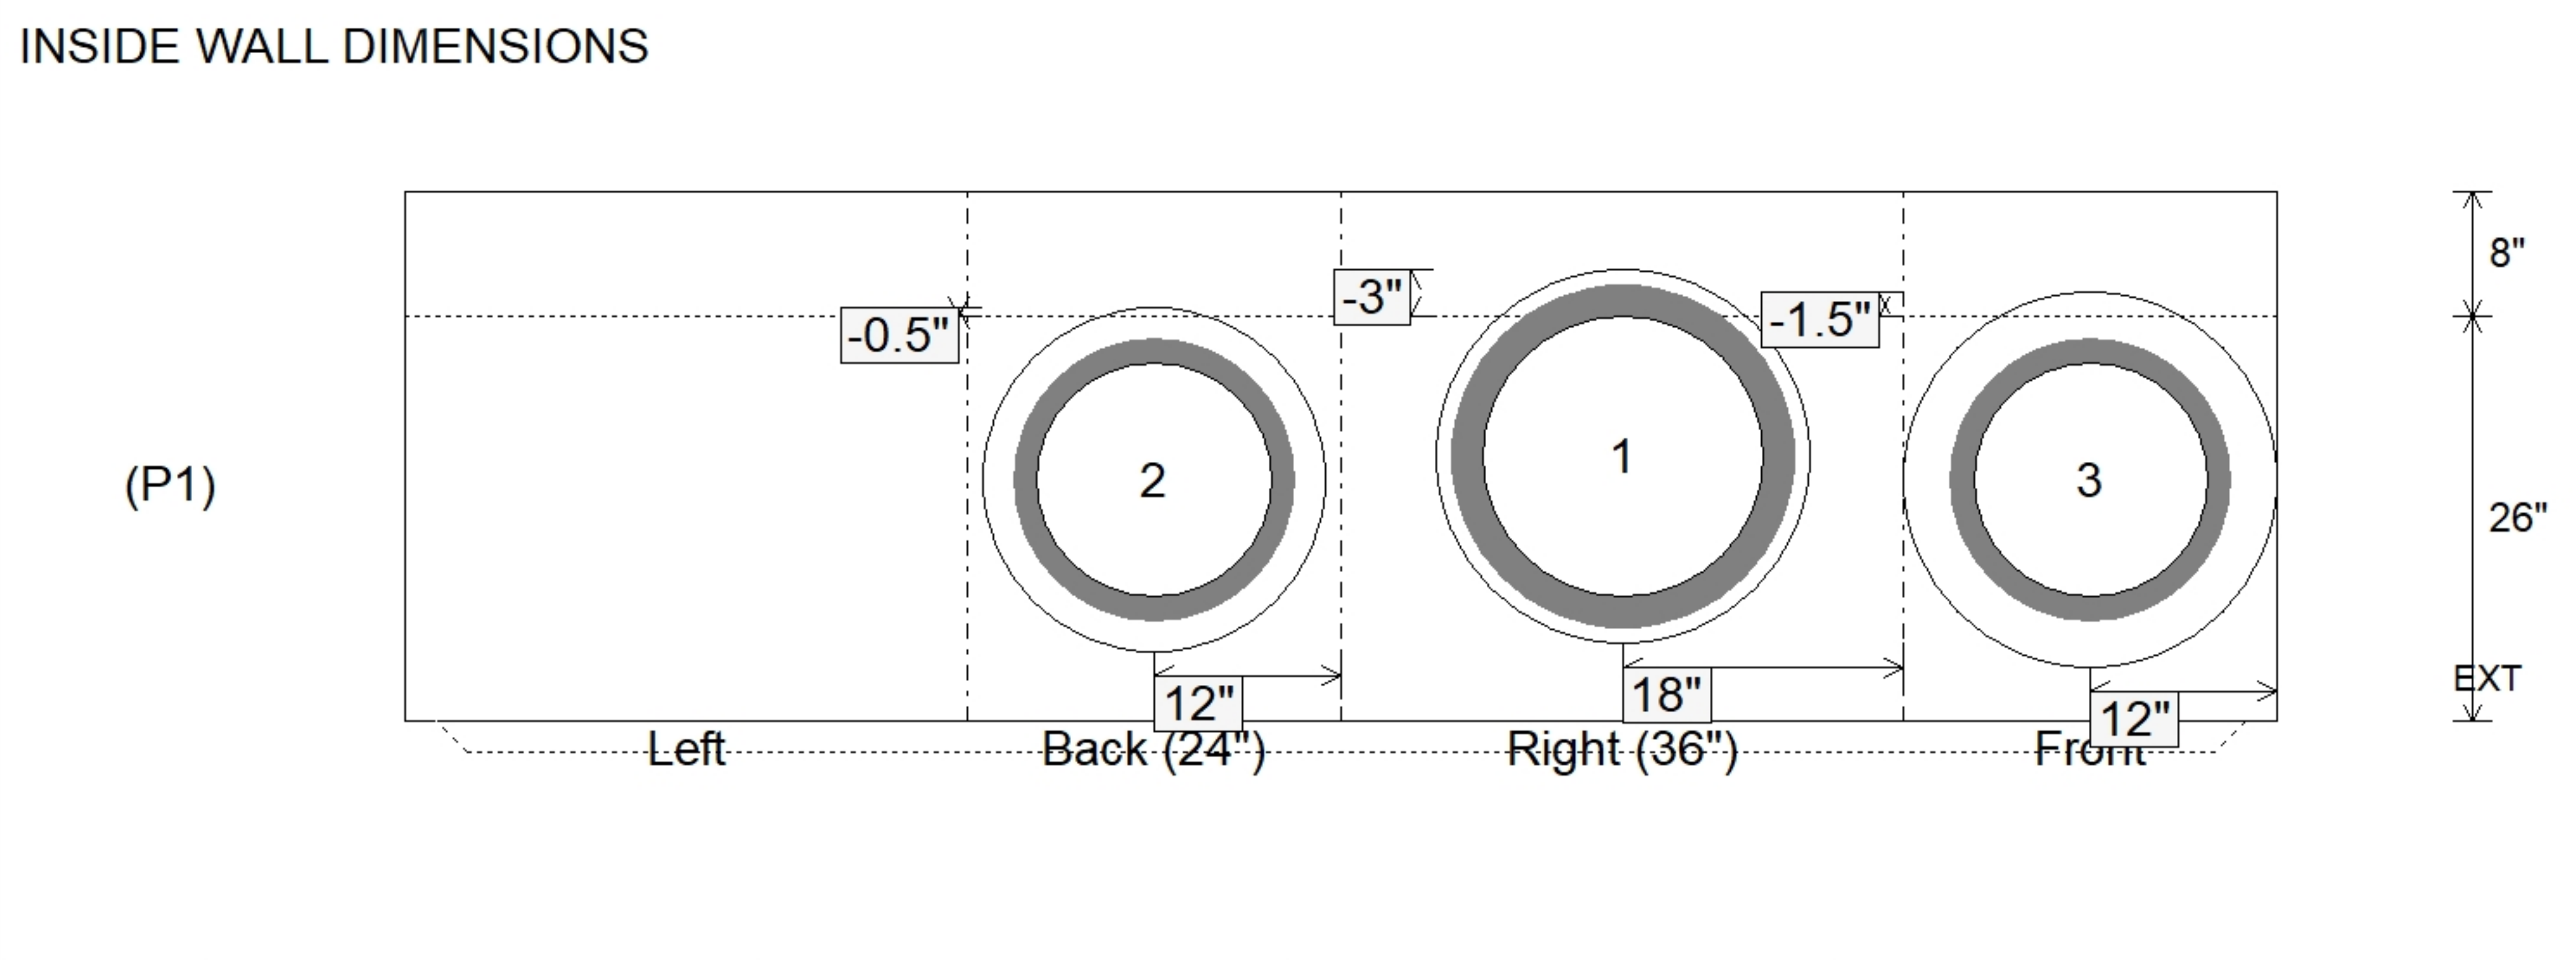


Job Name: 23-2404 Hampton Hills (Phase 1) Job Location: Richmond, KY Contractor: Seven Earthmovers LLC					Plant: 100 5/19/2026 12:59:22 PM		Tech: J. Horsley PC: C. Golf				
Structure ID: CBI-E3											
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht T/n							
P3) 24" x 120" - CB INLET KY A 10' TOP SAG F/G - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM SAG T/G - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 26" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 24 1) Hole - 22					3398 lb 5270 lb 3263 lb 206 lb 0 lb 0 lb 0 lb ----- Structure Total: 12136 lb		Structure Notes: 1. PER KYTC CBI A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING (HOE KY-206) TO BE CAST INTO TOP PHASE. REINFORCING PER ASTM AS615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - BASE WALLS (As .31) #5 BARS AT 12" C.C.E.W. - BASE FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 906.98'		Rim to Invert: 4.5'		Slack: 0"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	902.48'	90°	26"	18" ADS N-12	22"	Hole 24	24"	24"	-3"	0"	
Invert 2	902.73'	180°	20"	15" ADS N-12	18"	Hole 22	22"	22"	-0.5"	0"	
Invert 3	902.73'	0°	20"	15" ADS N-12	18"	Hole 24	24"	24"	-1.5"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)   											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 26" Height (Ext): 34"		Weight (Net): 3263 lb Volume (Net): 0.83cu.yd		
