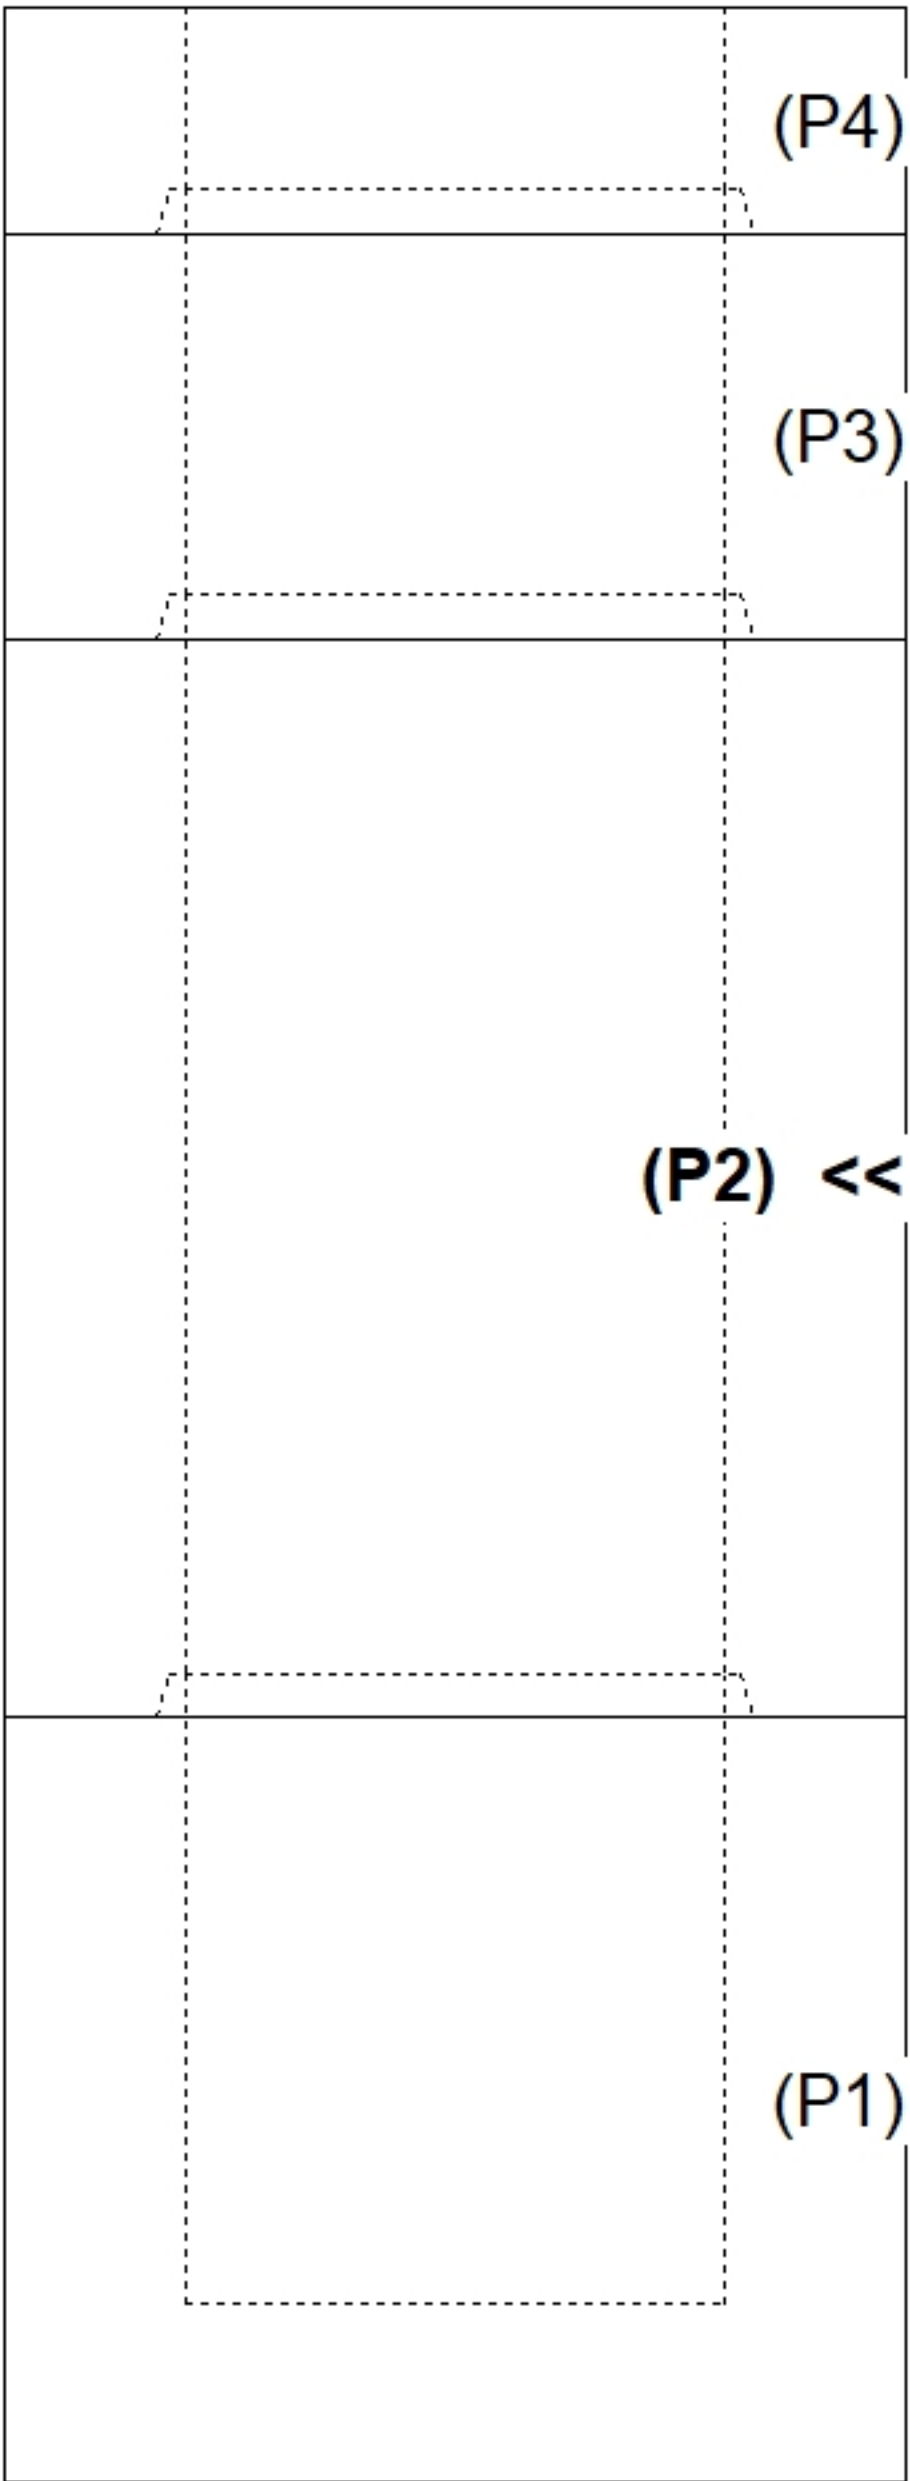
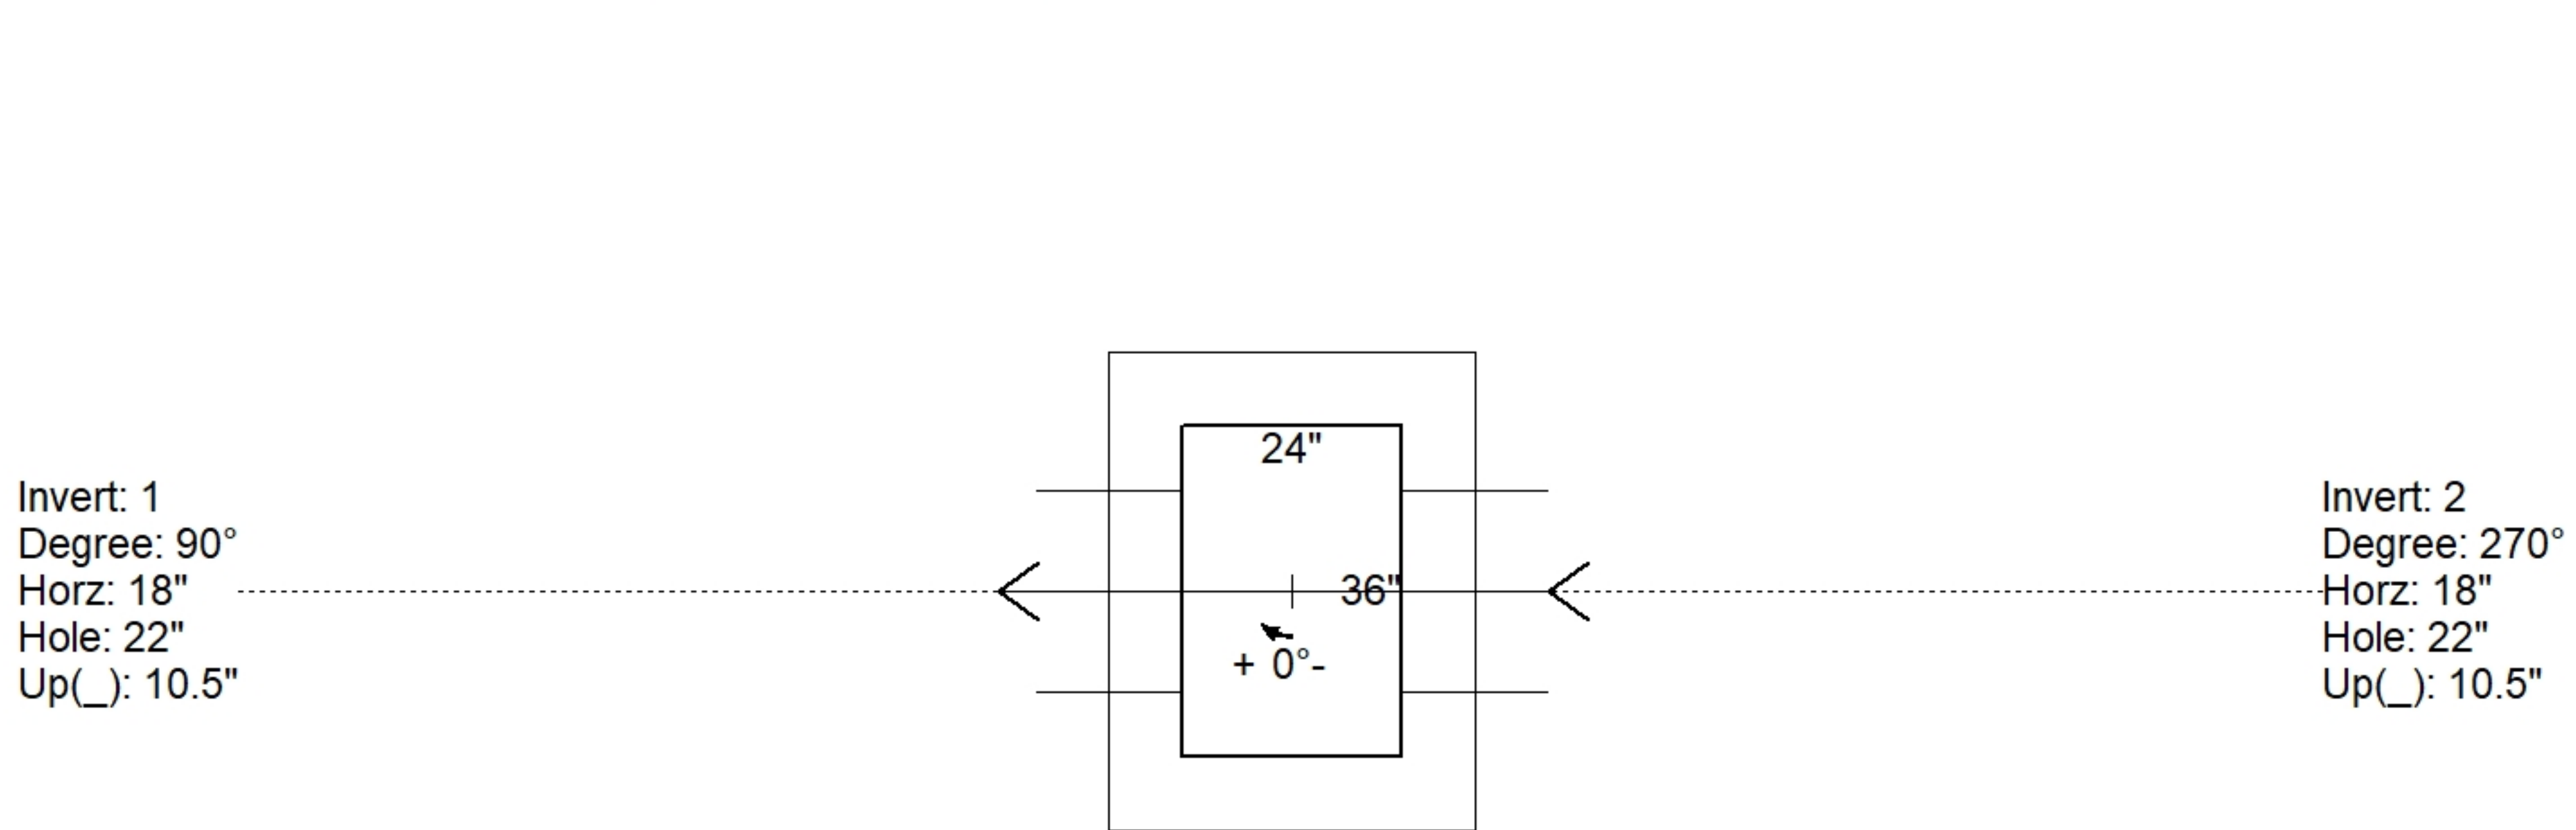
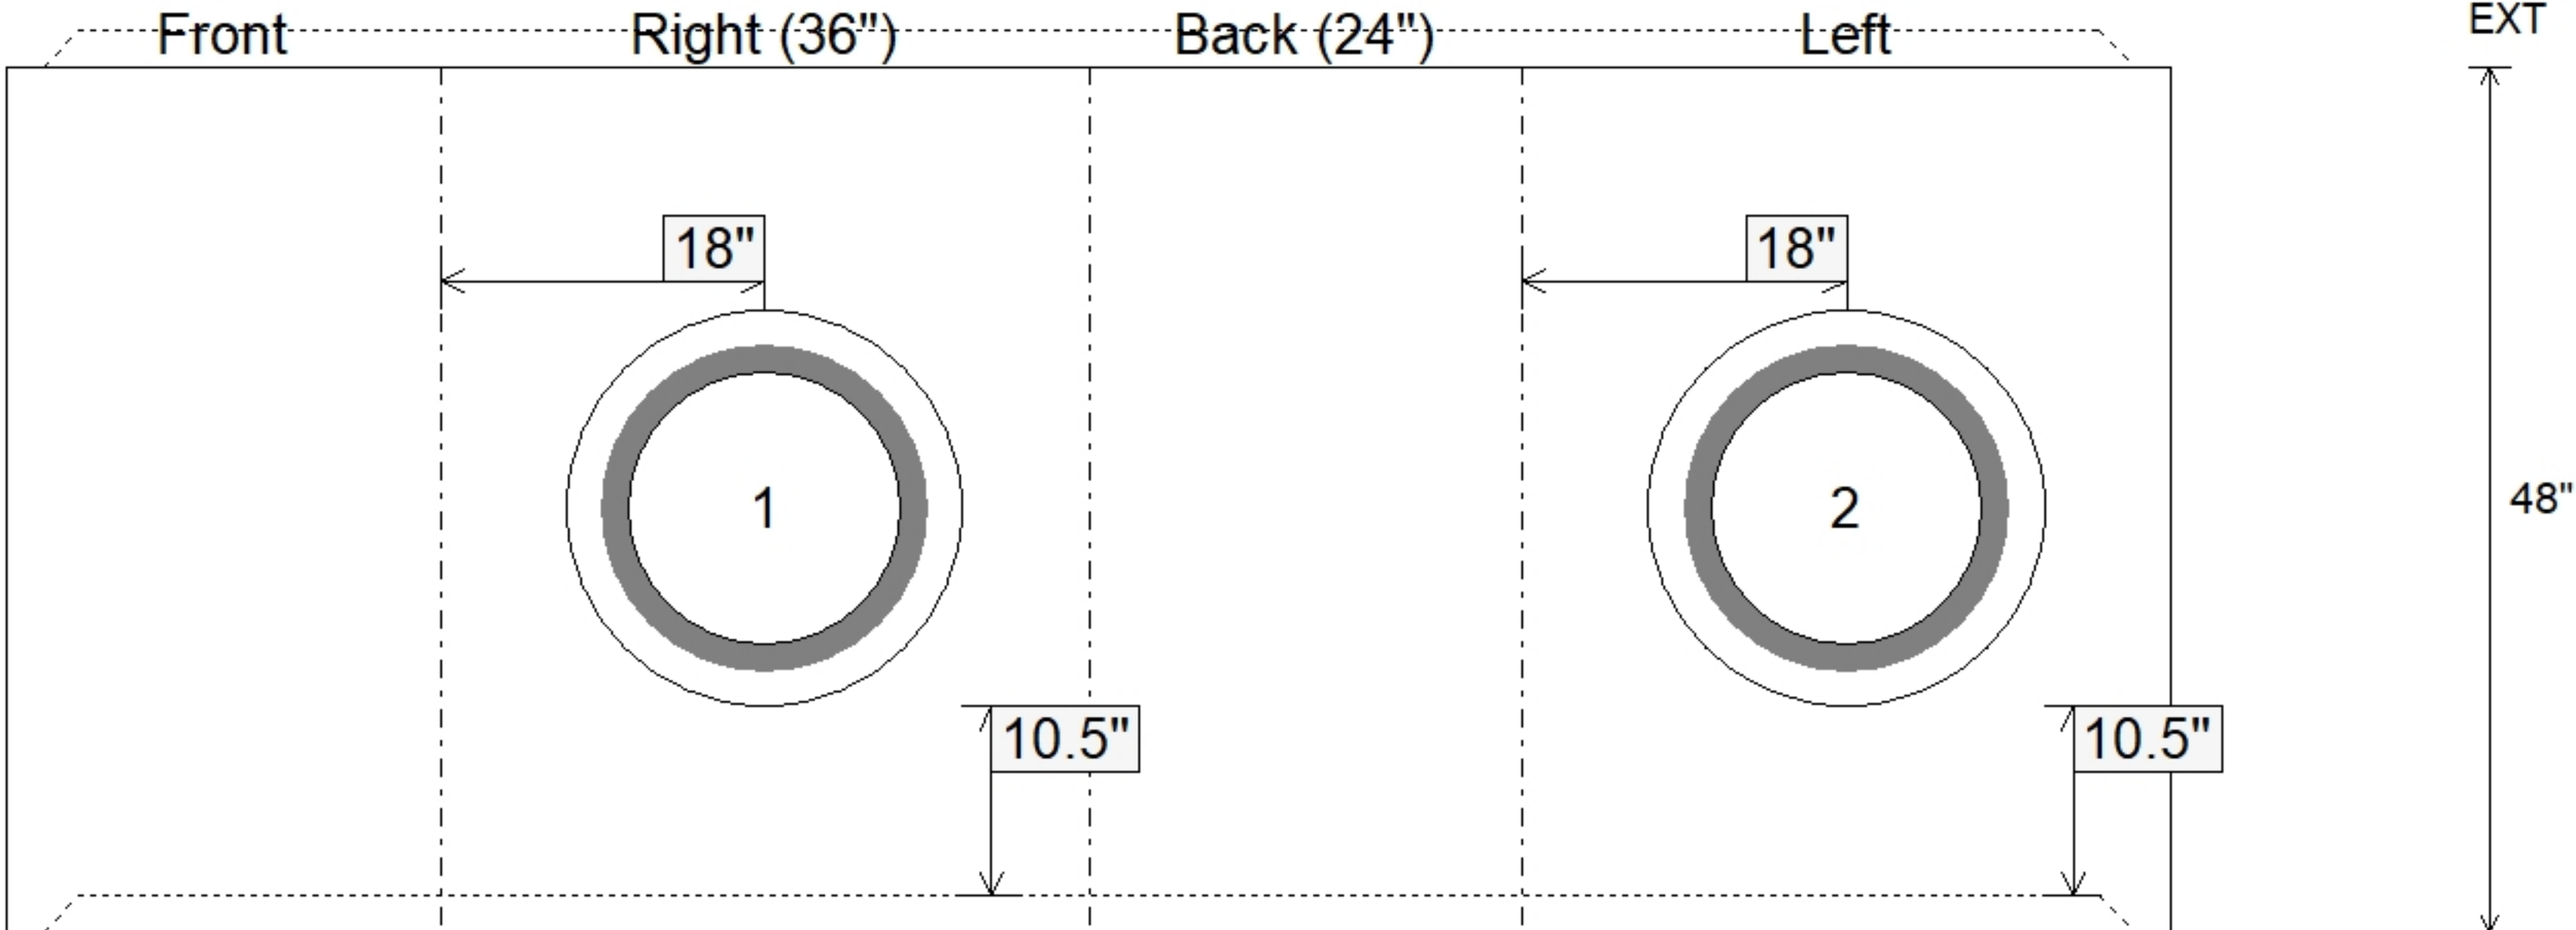


Job Name: 23-2404 Hampton Hills (Phase 1) Job Location: Richmond, KY Contractor: Seven Earthmovers LLC					Plant: 100 5/19/2026 1:01:04 PM		Tech: J. Horsley PC: C. Golf				
Structure ID: CBI-H2											
P2		BX2436-08R48			BOX RISER 8inW T/G						
P4) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P3) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18" P2) 24" x 36" - BOX RISER 8inW T/G - 48" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 26" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) SNOOT - BMP SNOOT 18F w/ KIT 2) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 22					3400 lb 5270 lb 4387 lb 4049 lb 206 lb 25 lb 0 lb 0 lb ----- Structure Total: 17337 lb		Structure Notes: 1. PER KYTC CBI A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING (HOE KY-206) TO BE CAST INTO TOP PHASE. 4. BMP SNOOT 18F w/KIT. REINFORCING PER ASTM AS615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - BASE WALLS (As .31) #5 BARS AT 12" C.C.E.W. - BASE FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 910.68'		Rim to Invert: 5'		Slack: 0"		Sump: 42"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	905.68'	90°	26"	15" ADS N-12	18"	Hole 22	22"	22"	10.5"	0"	
Invert 2	905.68'	270°	26"	15" ADS N-12	18"	Hole 22	22"	22"	10.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 8" Floor Height: 0"		Height (Int): 48" Height (Ext): 48"		Weight (Net): 4387 lb Volume (Net): 1.12cu.yd	
