

Contractor: Seven Earthmovers LLC

TECH: J. Horsley

Plant: 100



Spec: Sanitary
Type: SAN.MH
Size: 48"

Rim: 885.59'
Invert: 876.07'
Rim to Invert: 9.52'

Sump: 2"
Floor (Top): 875.903'
Floor Height: 6"

Floor (Bot): 875.403'
Overall Height: 10.083'
Slack: 1.24"


1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE MC-350 F/C) SHIPPED LOOSE.

- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


- P4) 24" - CASTING HEIGHT - 7"
- P3) 48" - ECC CONE w/ 24" HOLE F/G - 30"
- P2) 48" - MH RISER T/G - 48"
- P1) 48" - MH BASE Custom Ht T/n - 30"
- 1) 48" - MH INVERT CHANNEL - FULL HEIGHT
- 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
- 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
- 1) CASTING - HOE MC-350 F/C Sanitary
- 2) 48" - Conseal CS-102 1.00" (Double)
- 1) 24" - Conseal CS-102 1.00" (Double)
- 2) PSX - 12-08 NYLO
- 1) PSX - 12-06 NYLO
- 9) MH Step ML-10-TDS-NCR - 10"

0 lb
2050 lb
3353 lb
3282 lb
1440 lb
0 lb
0 lb
305 lb
0 lb
0 lb
16 lb
8 lb
0 lb


Structure Total: 10455 lb

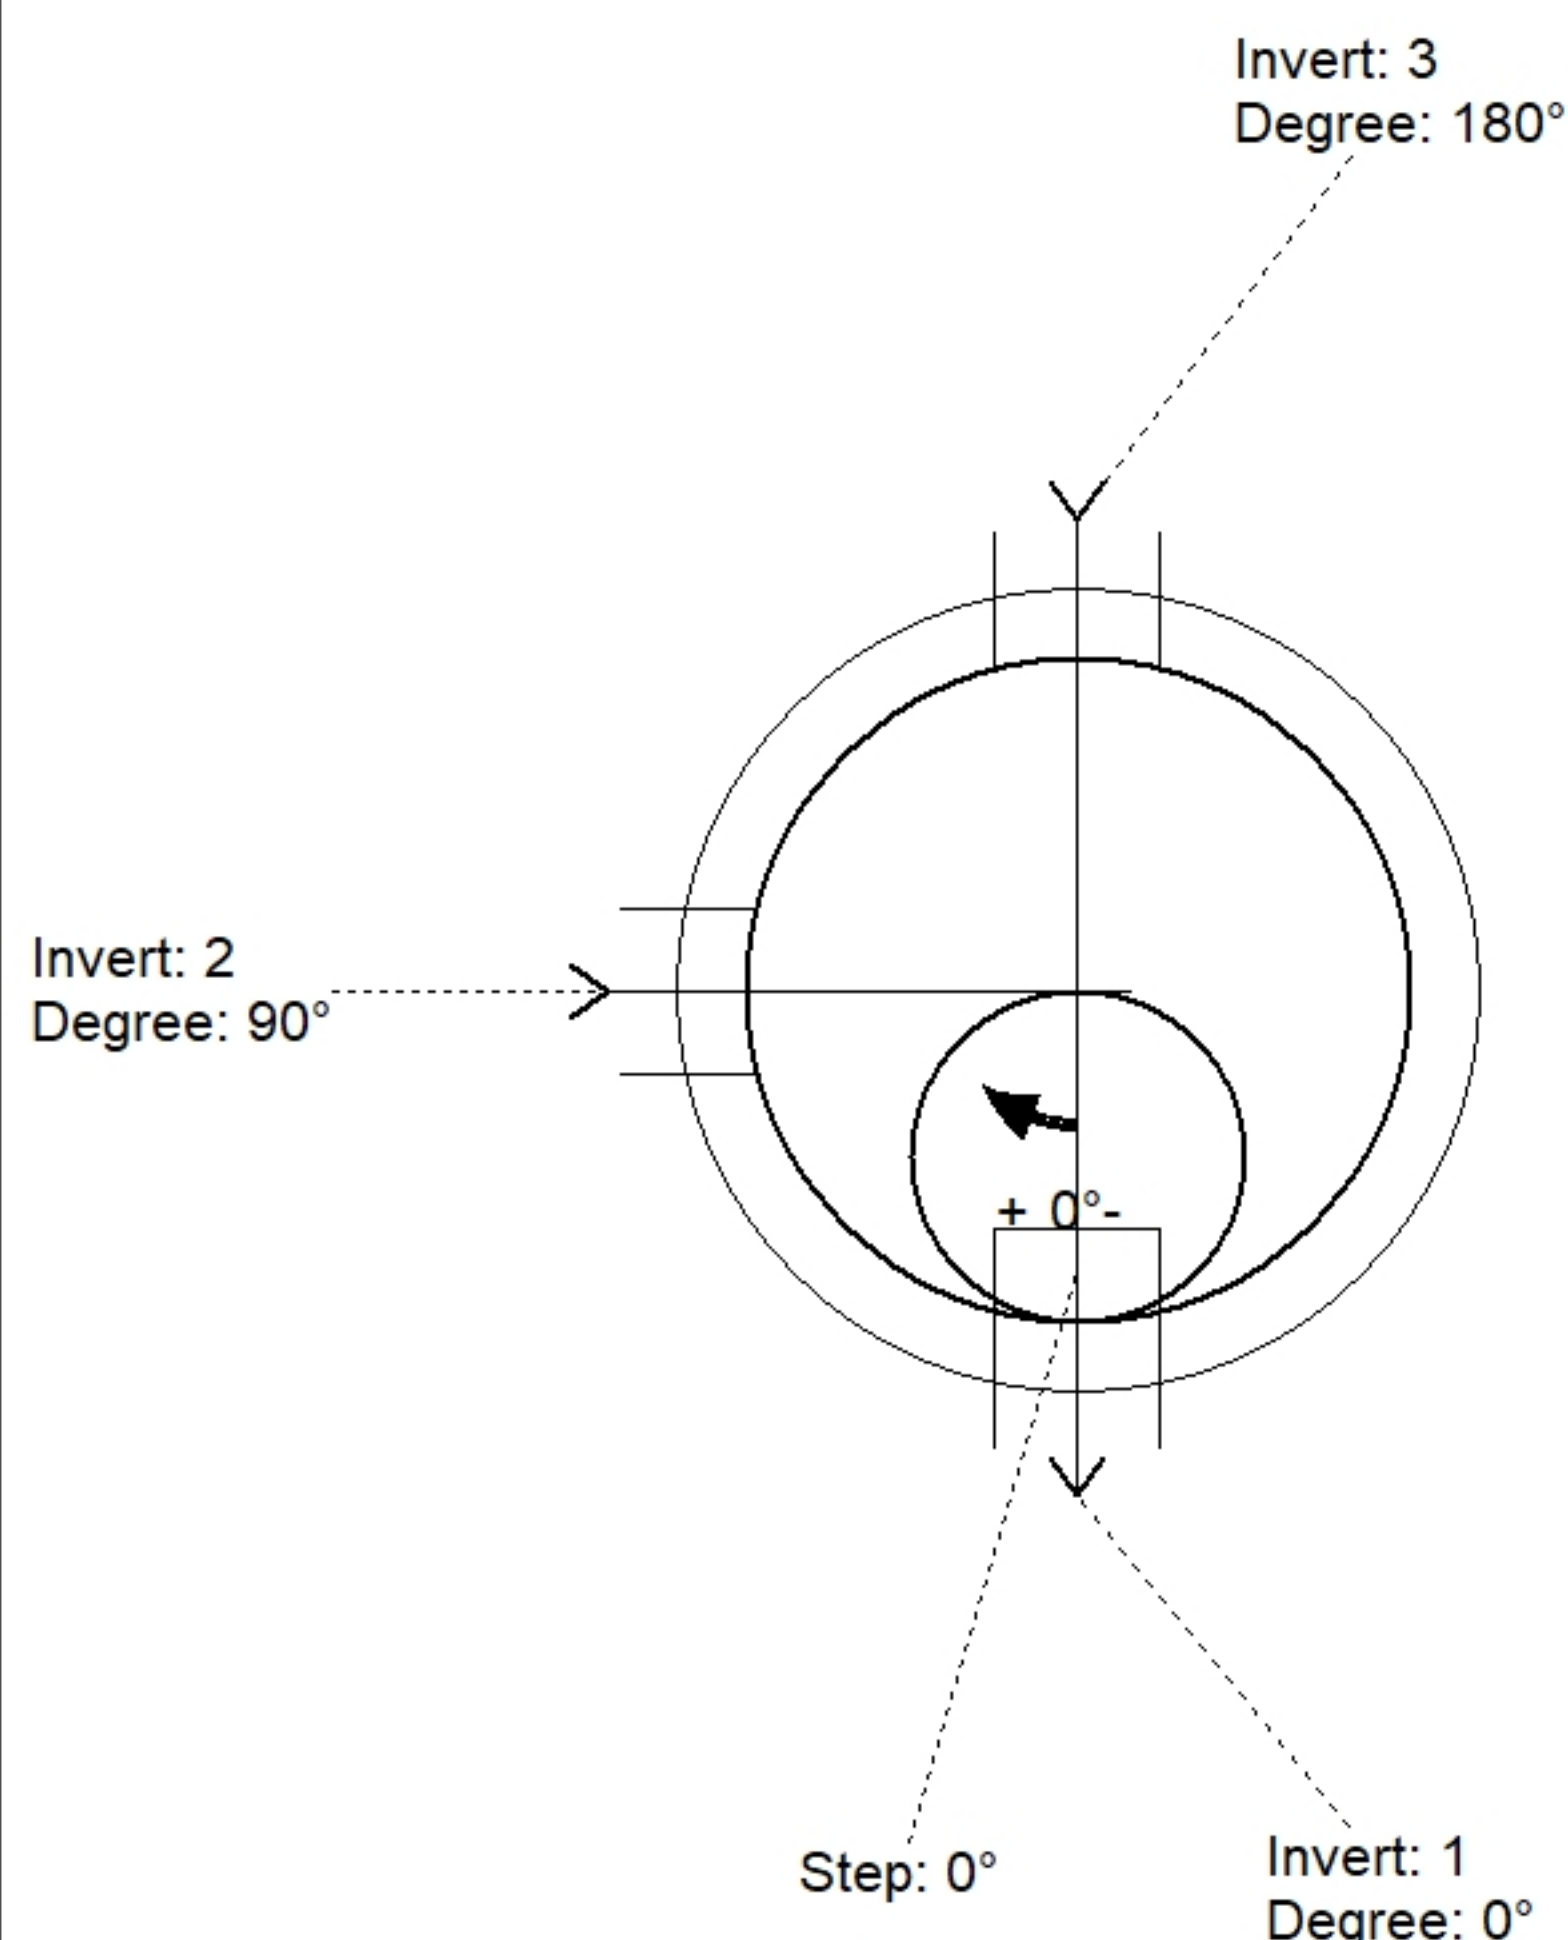

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	885.59'							
Reducer								
Invert 1	876.07'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	876.17'	90°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	1.25"	P1
Invert 3	876.17'	180°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	0.25"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

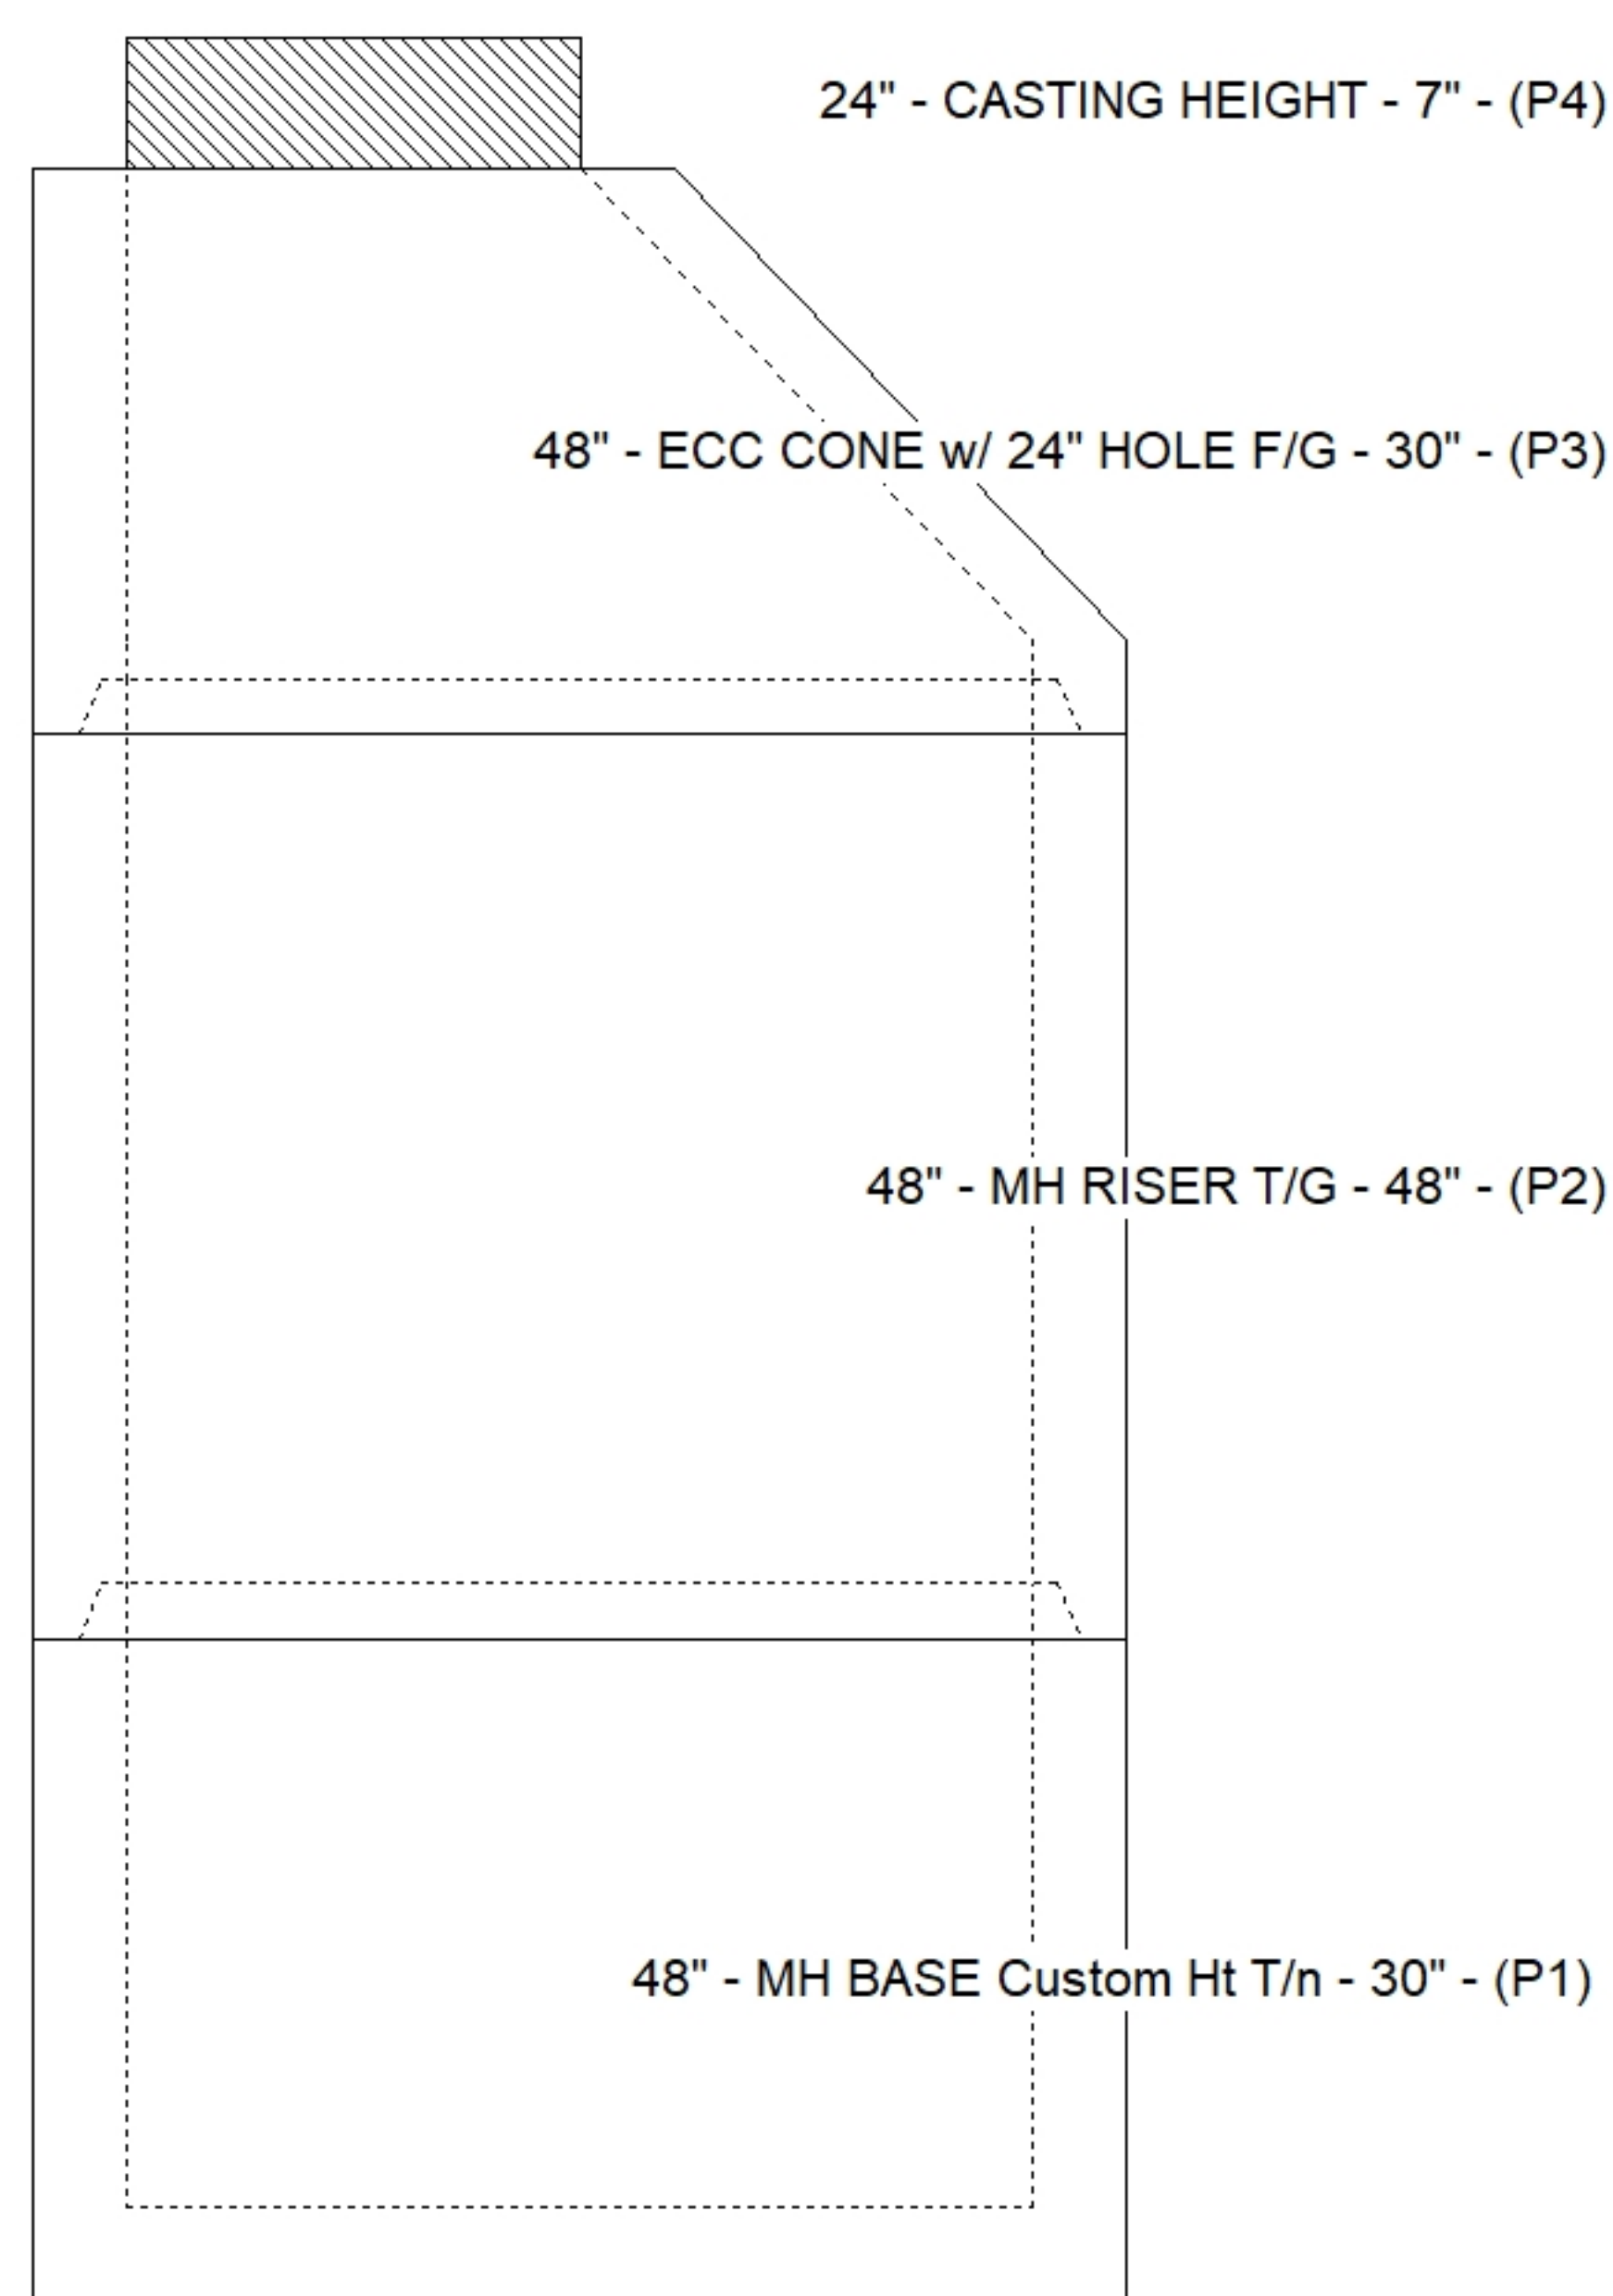

Cast (Int. Dim.) - Interior Dimensions

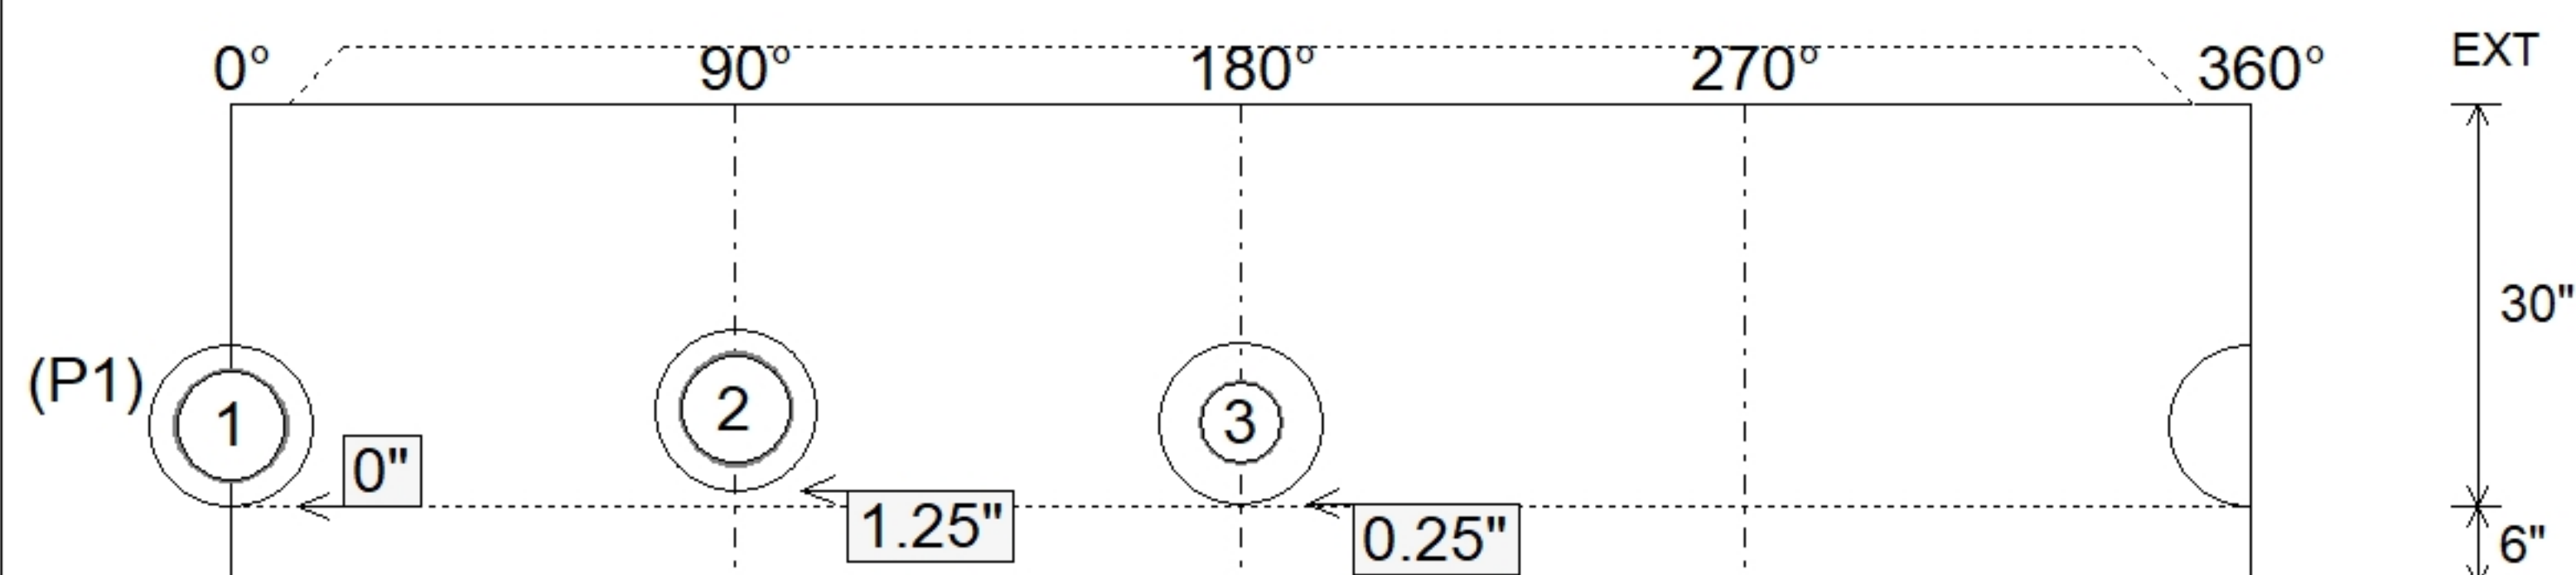

Submittal Drawing
5/19/2026 12:54:56 PM

SUBMITTAL
APPROVED BY:
