


Job Name: 23-2404 Hampton Hills (Phase 1) Job Location: Richmond, KY Contractor: Seven Earthmovers LLC					Plant: 100 5/19/2026 1:01:06 PM		Tech: J. Horsley PC: C. Golf				
Structure ID: SSMH BB-2-DROP											
P2		MH048RS60S-D		MH RISER w/DROP T/G							
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 30" P2) 48" - MH RISER w/DROP T/G - 60" P1) 48" - MH BASE w/DROP Custom Ht T/n - 20" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-350 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 1) Drop Tee - 8" PVC 1) Drop Elbow - 8" PVC 10) MH Step ML-10-TDS-NCR - 10"					0 lb 2050 lb 4168 lb 3774 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 8 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-350 F/C) SHIPPED LOOSE. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Structure Total:					11745 lb						
Rim: 862.85' Rim to Invert: 9.65' Slack: 0.8" Sump: 2" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2	858.2'	180°	91.125"	8" PVC SDR35	8.5"	Drop Tee 8" PVC	8.5"	8.545"	37.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

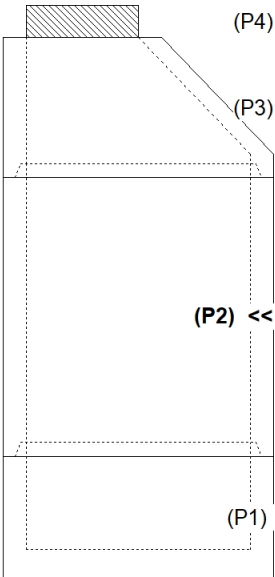


(P4)

(P3)

(P2) <<

(P1)

RIGHT-SIDE UP VIEW (int. dimensions)

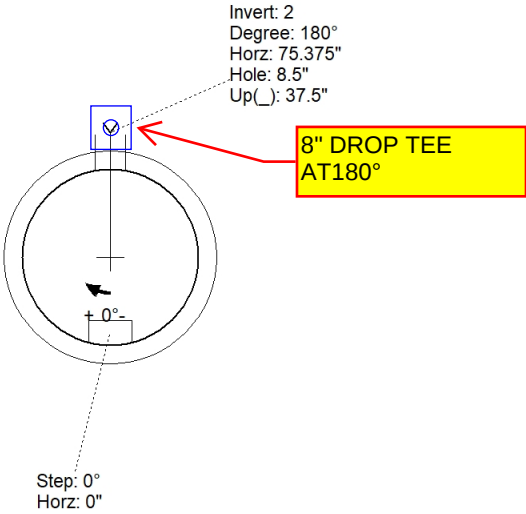


Invert: 2
Degree: 180°
Horz: 75.375"
Hole: 8.5"
Up(): 37.5"

8" DROP TEE AT180°

Step: 0°
Horz: 0°

INSIDE WALL DIMENSIONS

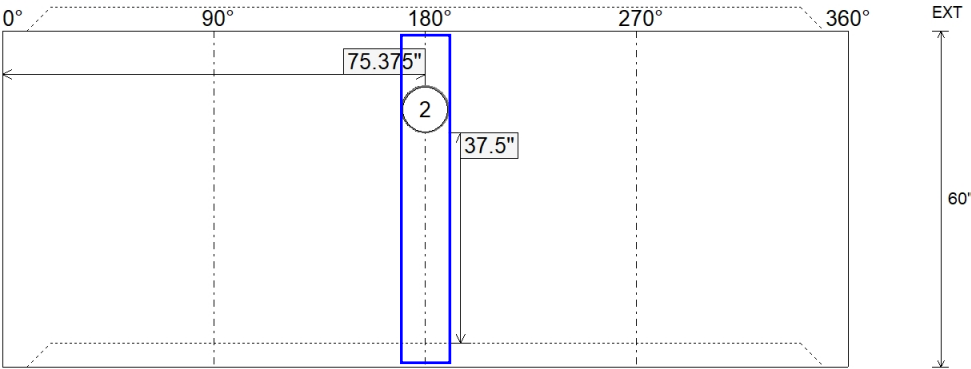

0° 90° 180° 270° 360°

75.375"

2

37.5"

60"

EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 60" Height (Ext): 60"	Weight (Net): 4168 lb Volume (Net): 1.06cu.yd
----------------------------------	------------------------------------	--	--	--
