



Job Name: 23-2404 Hampton Hills (Phase 1) Job Location: Richmond, KY Contractor: Seven Earthmovers LLC					Plant: 100 5/19/2026 12:59:29 PM		Tech: J. Horsley PC: C. Golf				
Structure ID: SSMH BB-3											
P1 MH048BAVF		MH BASE Custom Ht T/n									
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 36" P2) 48" - MH RISER T/G - 36" P1) 48" - MH BASE Custom Ht T/n - 43" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-350 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 2) Quik-Lok - QL-08-C 9) MH Step ML-10-TDS-NCR - 10"					0 lb 3000 lb 2515 lb 4257 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 2 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-350 F/C) SHIPPED LOOSE. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Structure Total: 11519 lb											
Rim: 876.1' Rim to Invert: 10' Slack: 0" Sump: 2" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	866.1'	0°	0"	8" PVC SDR35	8.5"	Quik-Lok QL-08-C	10.75"	10.842"	0.625"	0"	
Invert 2	868.2'	216°	109.375"	8" PVC SDR35	8.5"	Quik-Lok QL-08-C	10.75"	10.842"	25.875"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

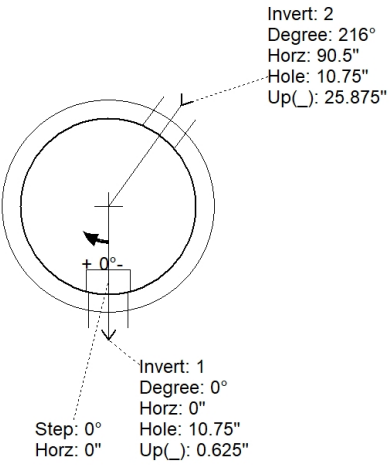

UPSIDE-DOWN VIEW (int. dimenions)

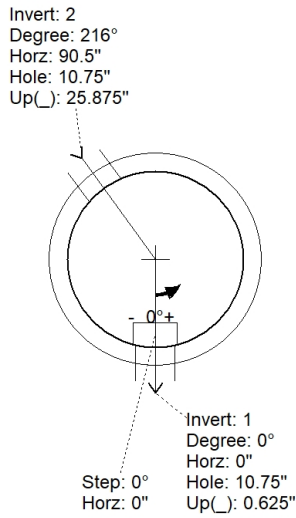

INSIDE WALL DIMENSIONS

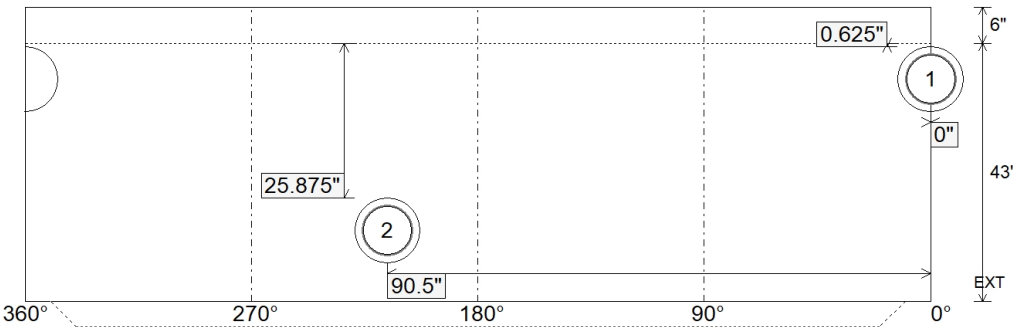

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 43" Height (Ext): 49"	Weight (Net): 4257 lb Volume (Net): 1.09cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 23-2404 Hampton Hills (Phase 1)
Job Location: Richmond, KY
Contractor: Seven Earthmovers LLC

Plant: 100

5/19/2026 12:59:29 PM

Tech: J. Horsley

PC: C. Golf



Structure ID: SSMH BB-3

P1A MH048BAVF

MH BASE Custom Ht T/n

- P4) 24" - CASTING HEIGHT - 7"
P3) 48" - ECC CONE w/ 24" HOLE F/G - 36"
P2) 48" - MH RISER T/G - 36"
P1) 48" - MH BASE Custom Ht T/n - 43"
1) 48" - MH INVERT CHANNEL - FULL HEIGHT
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) CASTING - HOE MC-350 F/C Sanitary
2) 48" - Conseal CS-102 1.00" (Double)
2) Quik-Lok - QL-08-C
9) MH Step ML-10-TDS-NCR - 10"

0 lb
3000 lb
2515 lb
4257 lb
1440 lb
0 lb
0 lb
305 lb
0 lb
2 lb
0 lb

Structure Total: 11519 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE MC-350 F/C) SHIPPED LOOSE.

REINFORCING PER ASTM A615 (GRADE 60).




- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 876.1' Rim to Invert: 10' Slack: 0" Sump: 2" Step Position: 0°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	866.1'	0°	0"	8" PVC SDR35	8.5"	Quik-Lok QL-08-C	10.75"	10.842"	0.625"	0"
Invert 2	868.2'	216°	109.375"	8" PVC SDR35	8.5"	Quik-Lok QL-08-C	10.75"	10.842"	25.875"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

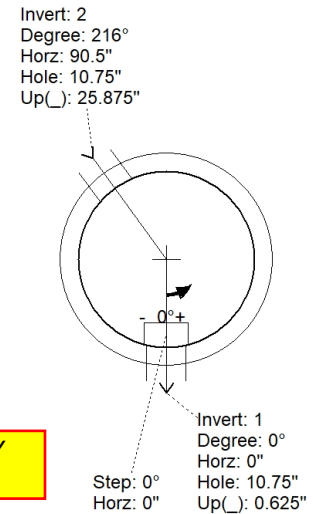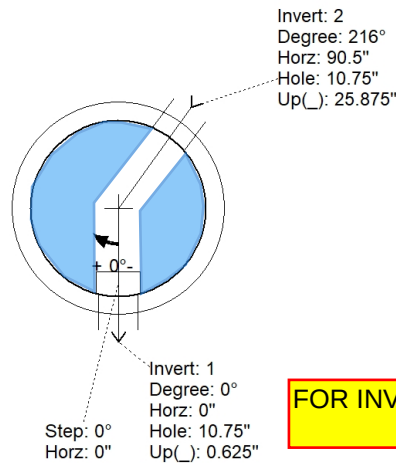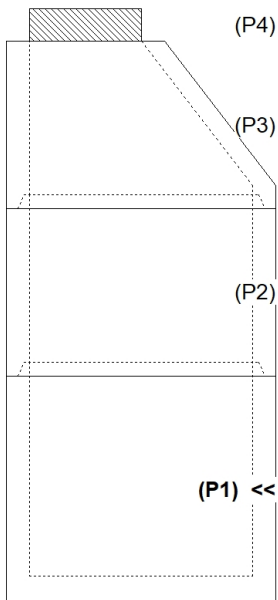

FOR INVERT ONLY

INSIDE WALL DIMENSIONS

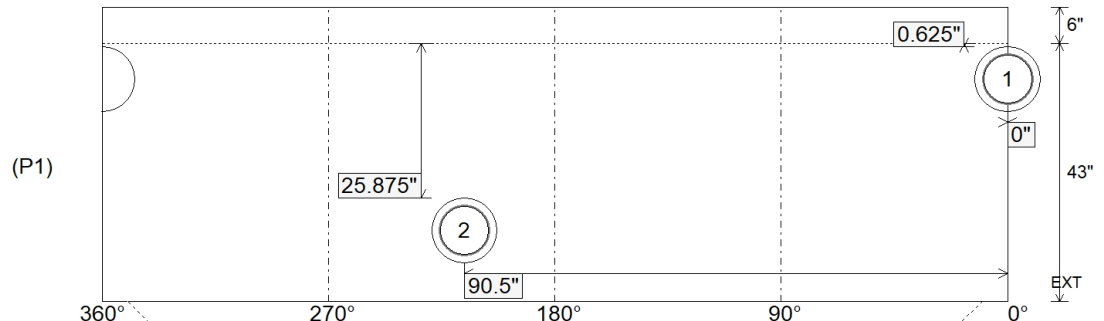

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 6"

Height (Int): 43"
Height (Ext): 49"

Weight (Net): 4257 lb
Volume (Net): 1.09cu.yd
