




Job Name: 23-2404 Hampton Hills (Phase 1) Job Location: Richmond, KY Contractor: Seven Earthmovers LLC					Plant: 100 5/19/2026 12:59:29 PM		Tech: J. Horsley PC: C. Golf				
Structure ID: SSMH BB-4											
P1 MH048BAVF		MH BASE Custom Ht T/n									
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 30" P1) 48" - MH BASE Custom Ht T/n - 19" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-350 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) Quik-Lok - QL-08-C 2) PSX - 12-06 NYLO 4) MH Step ML-10-TDS-NCR - 10"					0 lb 2050 lb 2523 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 1 lb 16 lb 0 lb ----- Structure Total: 6335 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-350 F/C) SHIPPED LOOSE. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 896' Rim to Invert: 4.5' Slack: 0" Sump: 2" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	891.5'	0°	0"	8" PVC SDR35	8.5"	Quik-Lok QL-08-C	10.75"	10.842"	0.625"	0"	
Invert 2	891.6'	115°	58.25"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	0.25"	0"	
Invert 3	891.6'	180°	91.125"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	0.25"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

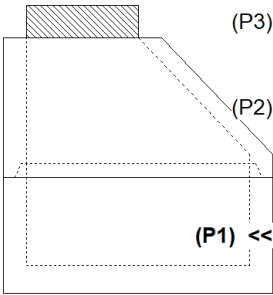


RIGHT-SIDE UP VIEW (int. dimensions)

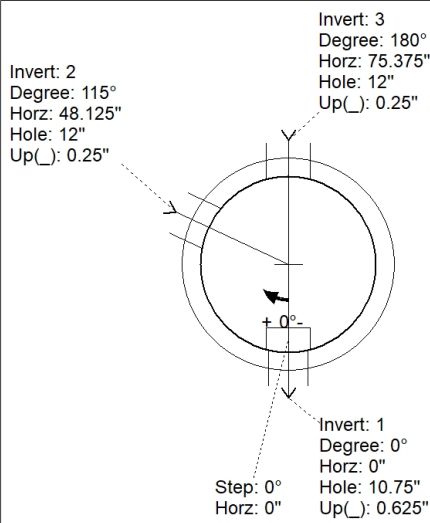

UPSIDE-DOWN VIEW (int. dimensions)

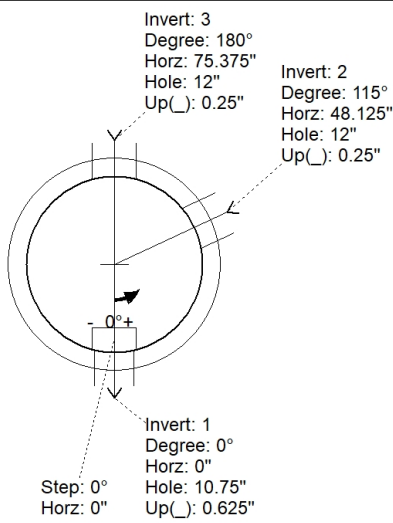

INSIDE WALL DIMENSIONS



Coating (Int):
Coating (Ext):


Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 6"


Height (Int): 19"
Height (Ext): 25"

Weight (Net): 2523 lb
Volume (Net): 0.64cu.yd


Job Name: 23-2404 Hampton Hills (Phase 1) Job Location: Richmond, KY Contractor: Seven Earthmovers LLC					Plant: 100 5/19/2026 12:59:29 PM		Tech: J. Horsley PC: C. Golf				
Structure ID: SSMH BB-4											
P1A MH048BAVF		MH BASE Custom Ht T/n									
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 30" P1) 48" - MH BASE Custom Ht T/n - 19" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-350 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) Quik-Lok - QL-08-C 2) PSX - 12-06 NYLO 4) MH Step ML-10-TDS-NCR - 10"					0 lb 2050 lb 2523 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 1 lb 16 lb 0 lb ----- Structure Total: 6335 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-350 F/C) SHIPPED LOOSE. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 896' Rim to Invert: 4.5' Slack: 0" Sump: 2" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	891.5'	0°	0"	8" PVC SDR35	8.5"	Quik-Lok QL-08-C	10.75"	10.842"	0.625"	0"	
Invert 2	891.6'	115°	58.25"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	0.25"	0"	
Invert 3	891.6'	180°	91.125"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	0.25"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

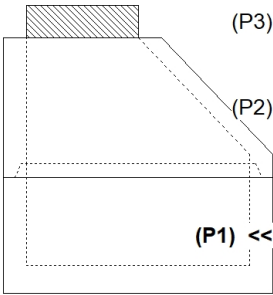

RIGHT-SIDE UP VIEW (int. dimensions)

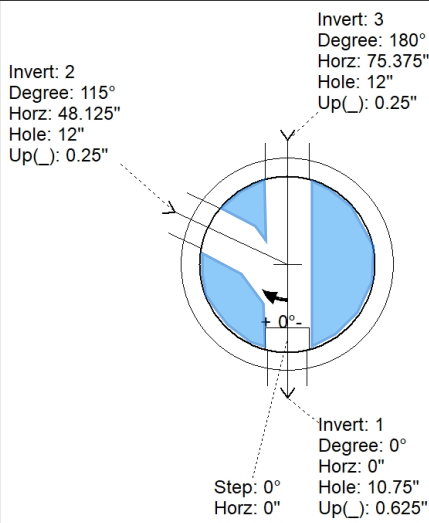


UPSIDE-DOWN VIEW (int. dimensions)

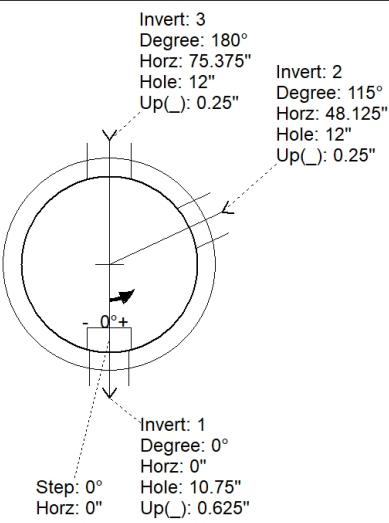

FOR INVERT ONLY

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 19" Height (Ext): 25"	Weight (Net): 2523 lb Volume (Net): 0.64cu.yd
----------------------------------	---------------------------------	--	--	--
