

Job Name: 23-2404 Hampton Hills (Phase 1) Job Location: Richmond, KY Contractor: Seven Earthmovers LLC					Plant: 100		Tech: J. Horsley			
					5/19/2026 12:59:31 PM		PC: C. Golf			
Structure ID: SSMH CC-2-DROP										
P1 MH048BAVF-D			MH BASE w/DROP Custom Ht T/n							
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 30" P2) 48" - MH RISER w/DROP T/G - 60" P1) 48" - MH BASE w/DROP Custom Ht T/n - 20" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-350 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 1) Drop Tee - 8" PVC 1) Drop Elbow - 8" PVC 10) MH Step ML-10-TDS-NCR - 10"					0 lb 2050 lb 4168 lb 3774 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 8 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 11745 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-350 F/C) SHIPPED LOOSE. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 859.5' Rim to Invert: 9.65' Slack: 0.8" Sump: 2" Step Position: 0°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	849.85'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2										
Invert 3	849.95'	180°	91.125"	8" PVC SDR35	8.5"	Drop Elbow 8" PVC	8.5"	8.545"	3"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 20" Height (Ext): 26"	Weight (Net): 3774 lb Volume (Net): 0.96cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 23-2404 Hampton Hills (Phase 1)
 Job Location: Richmond, KY
 Contractor: Seven Earthmovers LLC

Plant: 100

5/19/2026 12:59:31 PM

Tech: J. Horsley

PC: C. Golf



Structure ID: SSMH CC-2-DROP

P1A MH048BAVF-D

MH BASE w/DROP Custom Ht T/n

- P4) 24" - CASTING HEIGHT - 7"
 P3) 48" - ECC CONE w/ 24" HOLE F/G - 30"
 P2) 48" - MH RISER w/DROP T/G - 60"
 P1) 48" - MH BASE w/DROP Custom Ht T/n - 20"
 1) 48" - MH INVERT CHANNEL - FULL HEIGHT
 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
 1) CASTING - HOE MC-350 F/C Sanitary
 2) 48" - Conseal CS-102 1.00" (Double)
 1) PSX - 12-08 NYLO
 1) Drop Tee - 8" PVC
 1) Drop Elbow - 8" PVC
 10) MH Step ML-10-TDS-NCR - 10"

0 lb
 2050 lb
 4168 lb
 3774 lb
 1440 lb
 0 lb
 0 lb
 305 lb
 0 lb
 8 lb
 0 lb
 0 lb
 0 lb
 0 lb

Structure Total: 11745 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE MC-350 F/C) SHIPPED LOOSE.

REINFORCING PER ASTM A615 (GRADE 60).



- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 859.5' Rim to Invert: 9.65' Slack: 0.8" Sump: 2" Step Position: 0°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	849.85'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2										
Invert 3	849.95'	180°	91.125"	8" PVC SDR35	8.5"	Drop Elbow 8" PVC	8.5"	8.545"	3"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

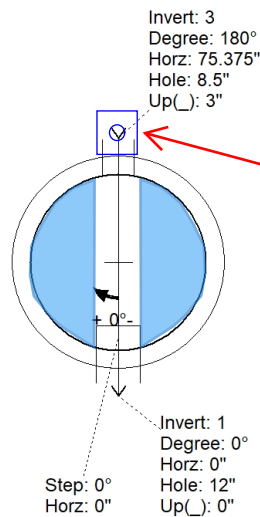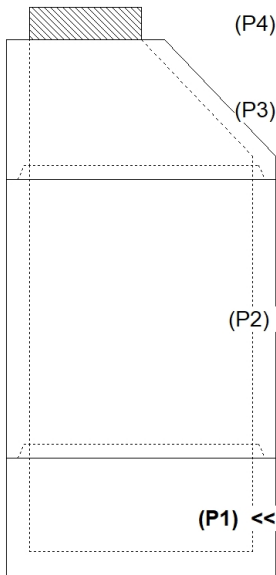


8" DROP ELBOW
AT 180°

FOR INVERT ONLY

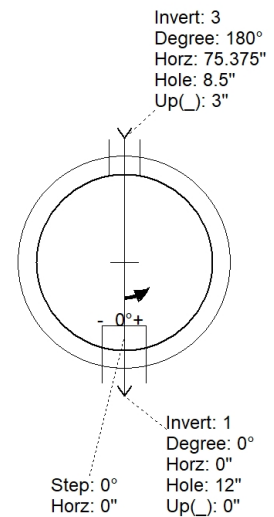

INSIDE WALL DIMENSIONS



Coating (Int):
 Coating (Ext):

Seam Up: Tongue
 Seam Dn: n/a

Wall Thickness: 5"
 Floor Height: 6"

Height (Int): 20"
 Height (Ext): 26"

Weight (Net): 3774 lb
 Volume (Net): 0.96cu.yd
