

Contractor: Seven Earthmovers LLC

TECH: J. Horsley

Plant: 100



Size: 48"

Rim to Invert: 6.16'

Floor Height: 6"


Slack: 0.92"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

5) MH Step ML-10-TDS-NCR - 10"


0 lb

Structure Total: 8012 lb

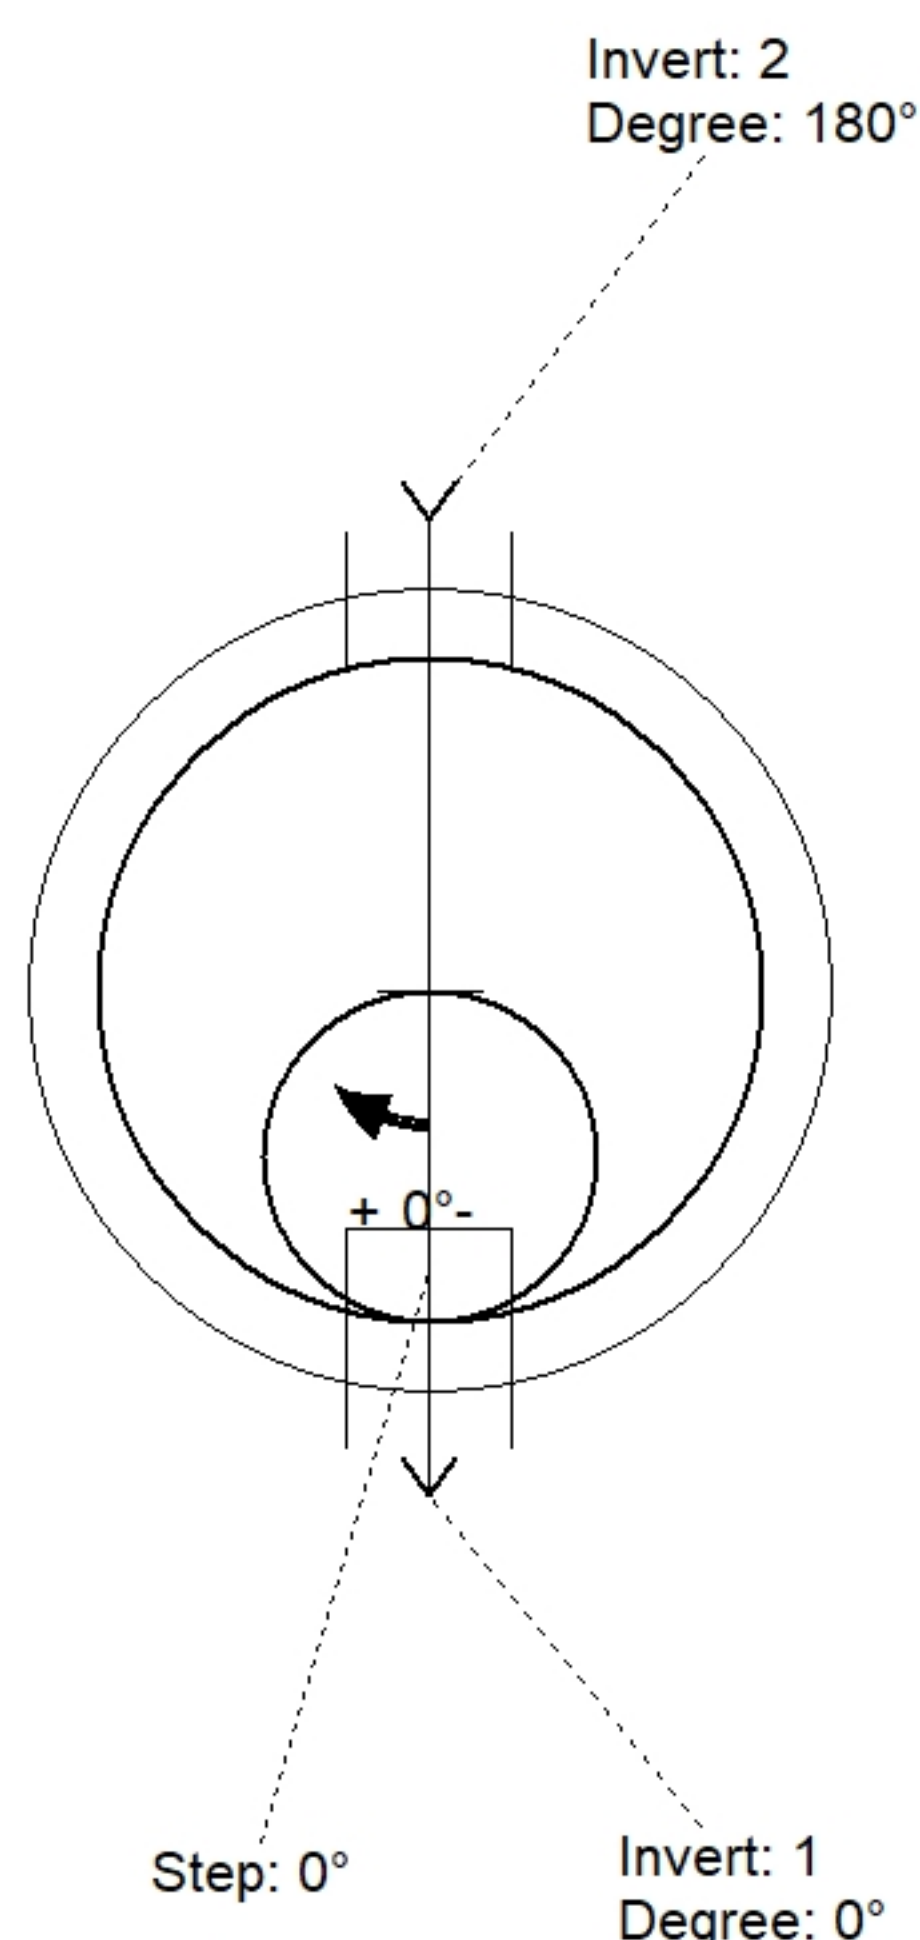

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	892.3'							
Reducer								
Invert 1	886.14'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	886.24'	180°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	1.25"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Cast (Int. Dim.) - Interior Dimensions

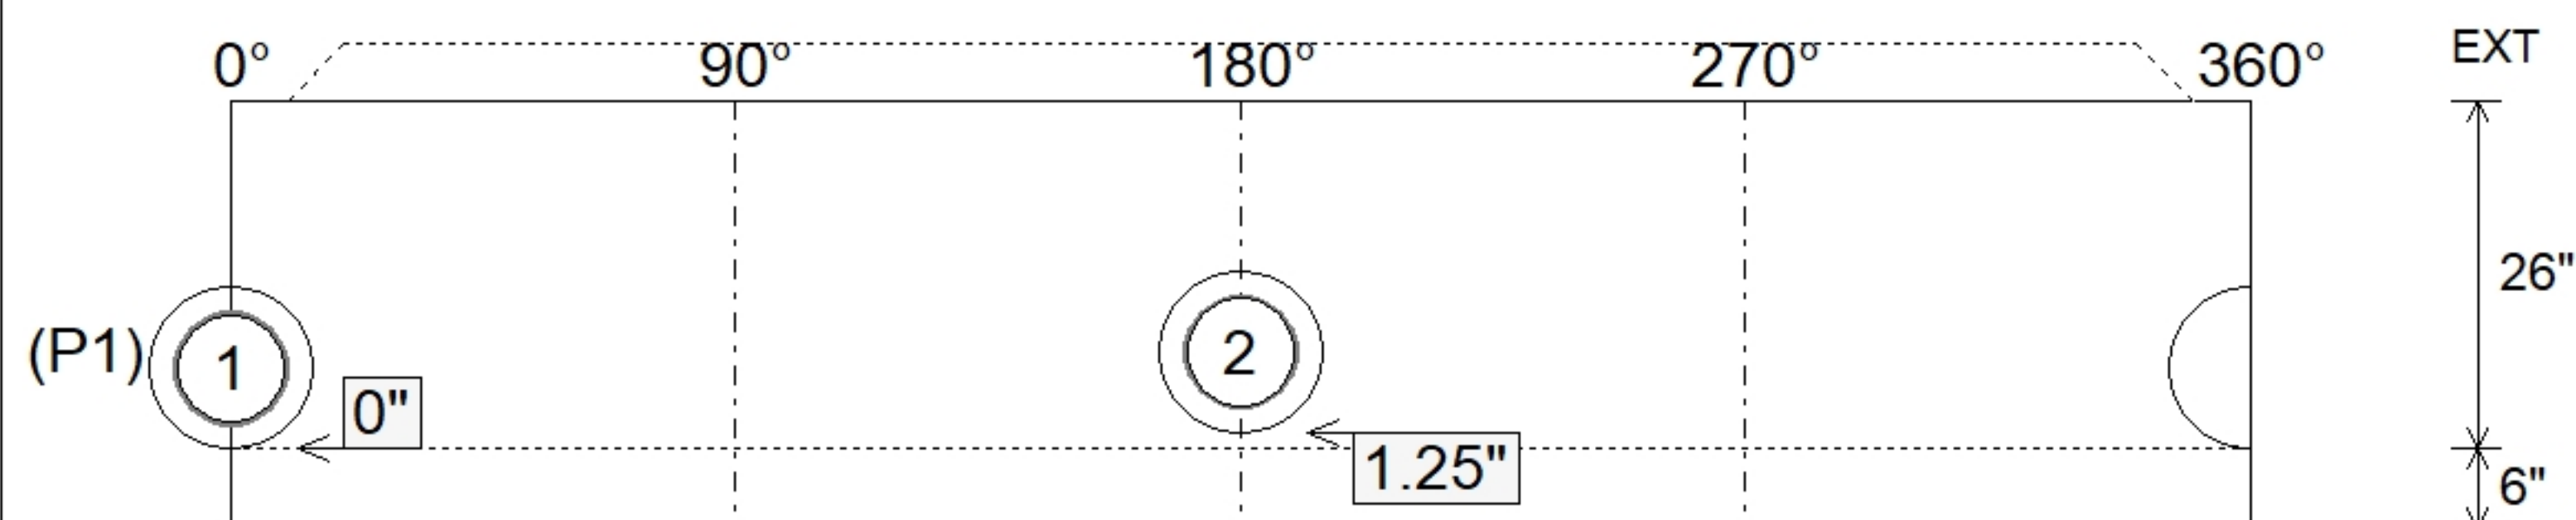

24" - CASTING HEIGHT - 7" - (P3)

48" - ECC CONE w/ 24" HOLE F/G - 42" - (P2)

48" - MH BASE Custom Ht T/n - 26" - (P1)

Submittal Drawing
5/19/2026 12:54:59 PM

SUBMITTAL
APPROVED BY:
