

Contractor: Core & Main LP (Lou)

Plant: Beaver Dam, Ky.




Slack: 0.04"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


3) PSX - 12-06 NYLO

24 lb

Structure Total: 16490 lb

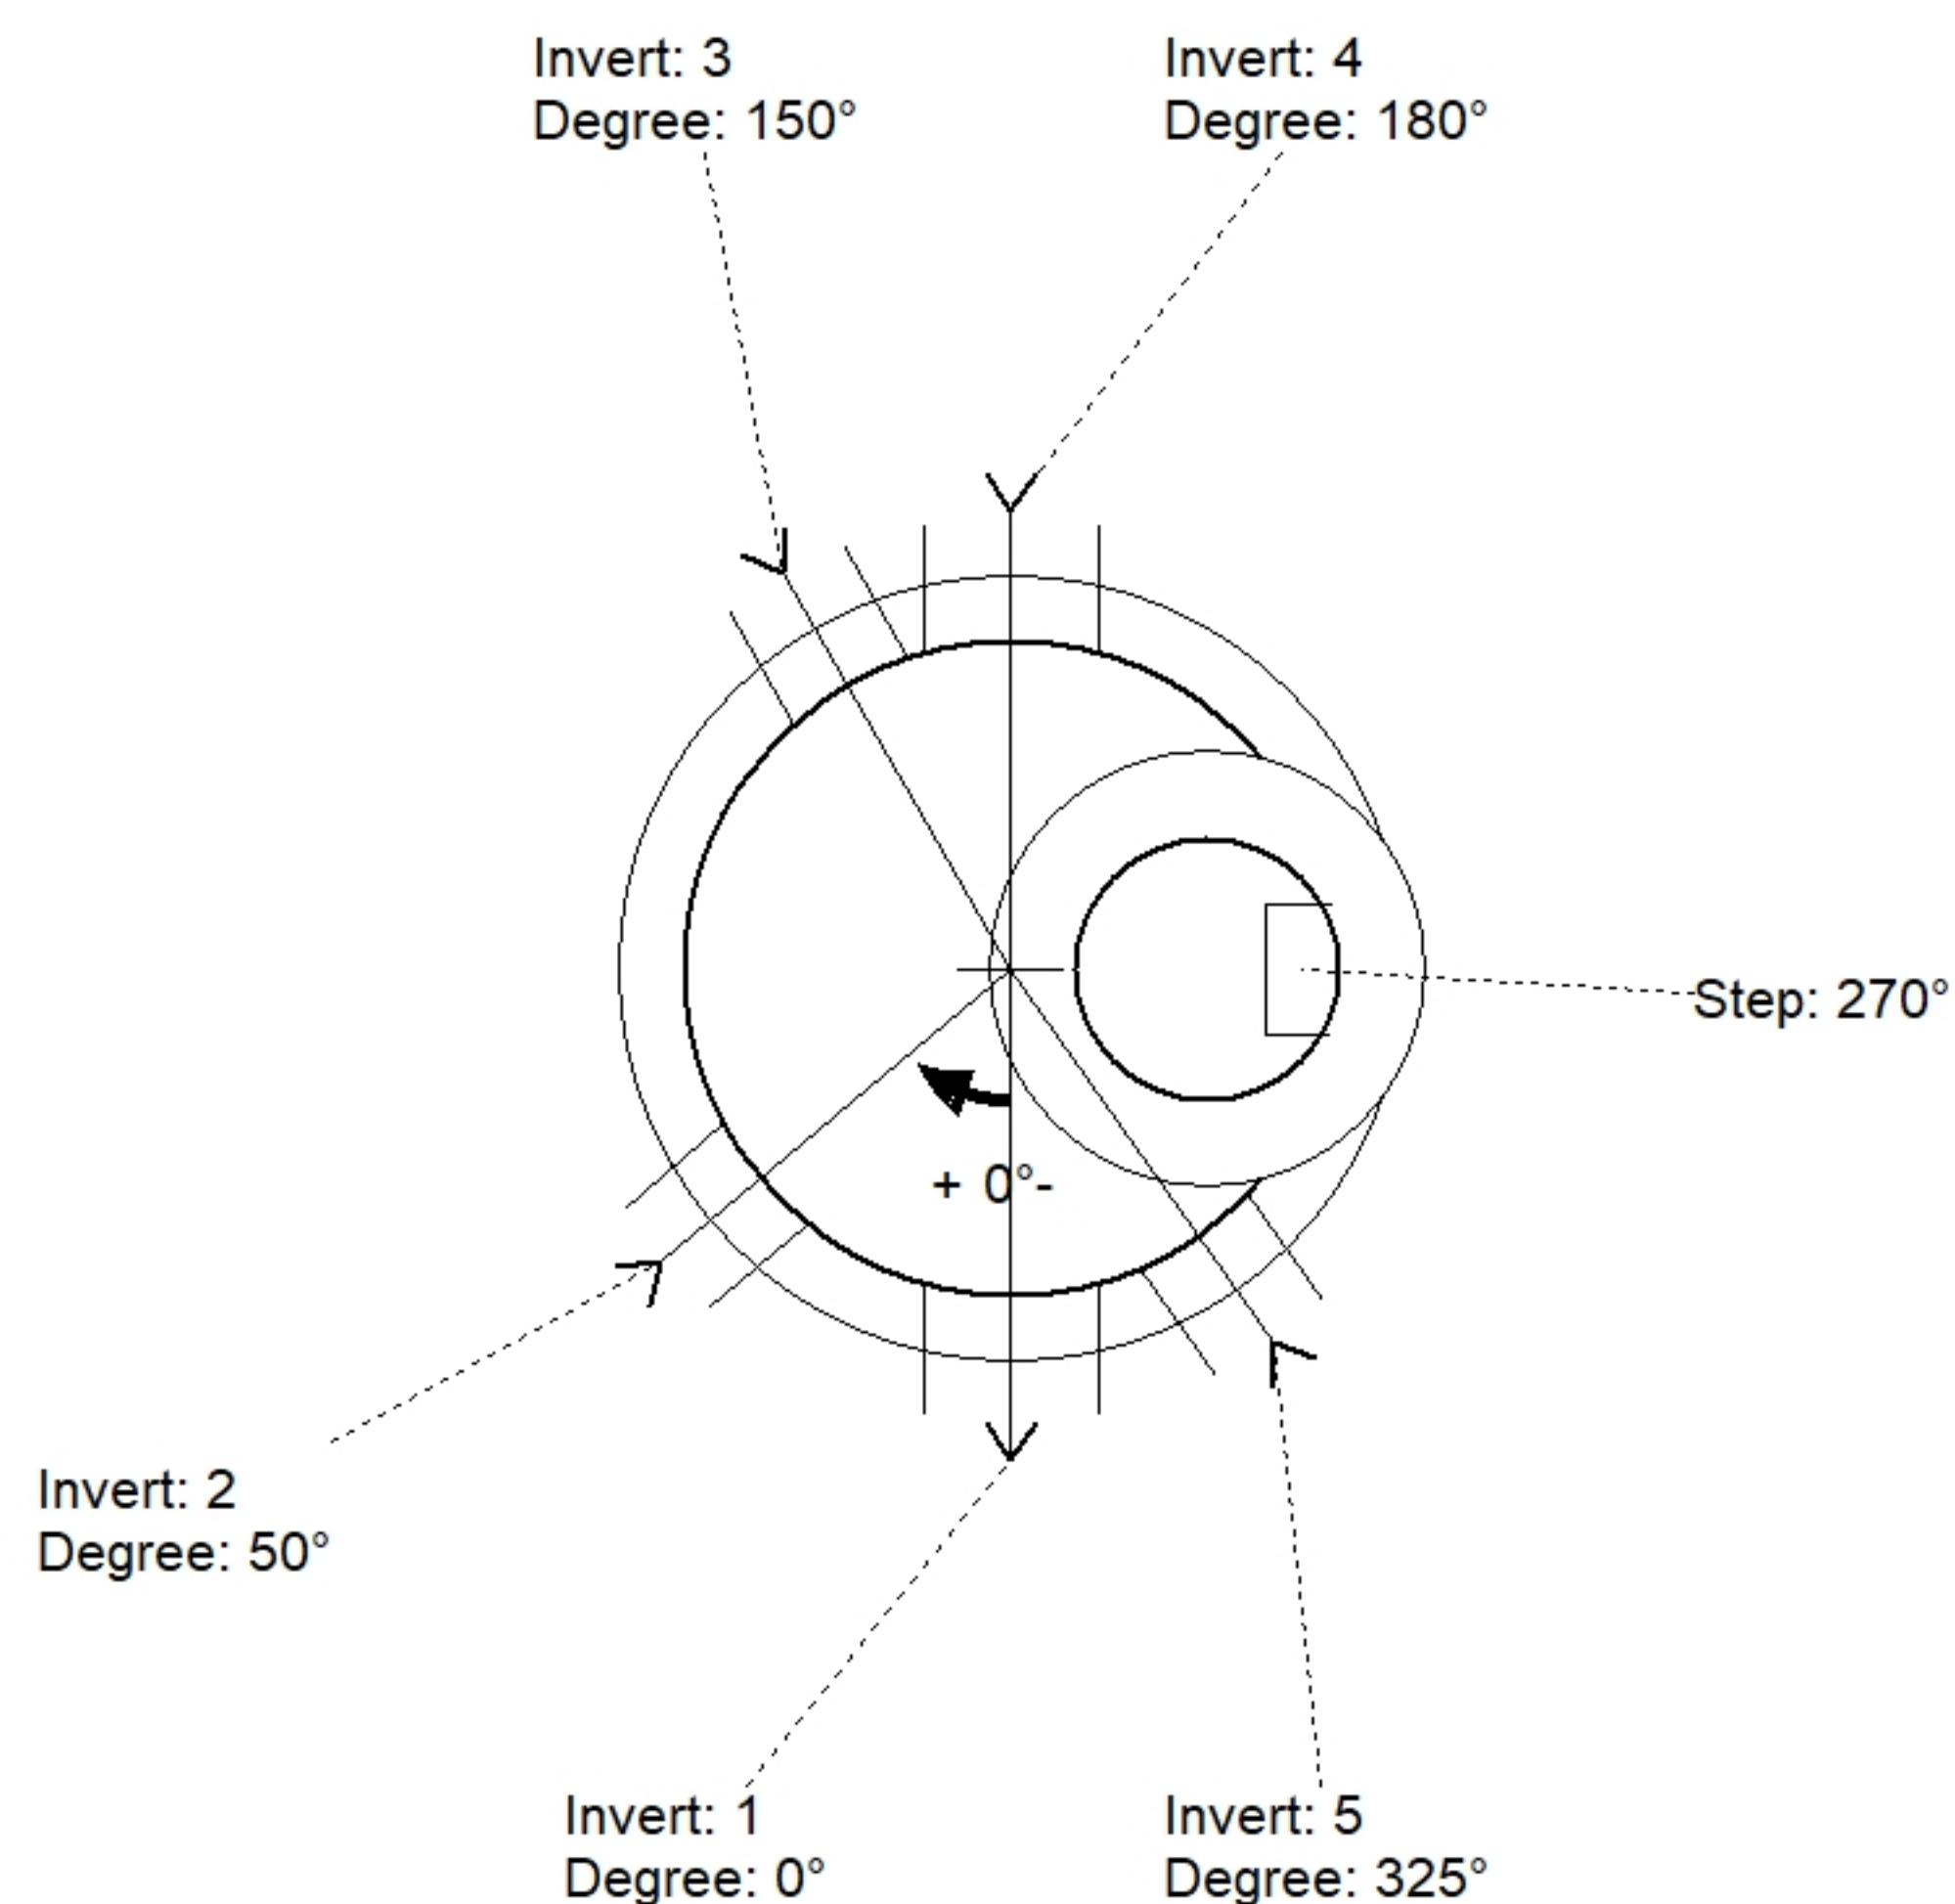

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	414.13'							
Reducer								
Invert 1	405.21'	0°	12" PVC SDR35	12.5"	16"	PSX 16L NYLO	1"	P1
Invert 2	406.3'	50°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	13.08"	P1
Invert 3	406.3'	150°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	13.08"	P1
Invert 4	409.91'	180°	12" PVC SDR35	12.5"	16"	PSX 16L NYLO	16.65"	P2
Invert 5	406.3'	325°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	13.08"	P1
Invert 6								
Invert 7								
Invert 8								

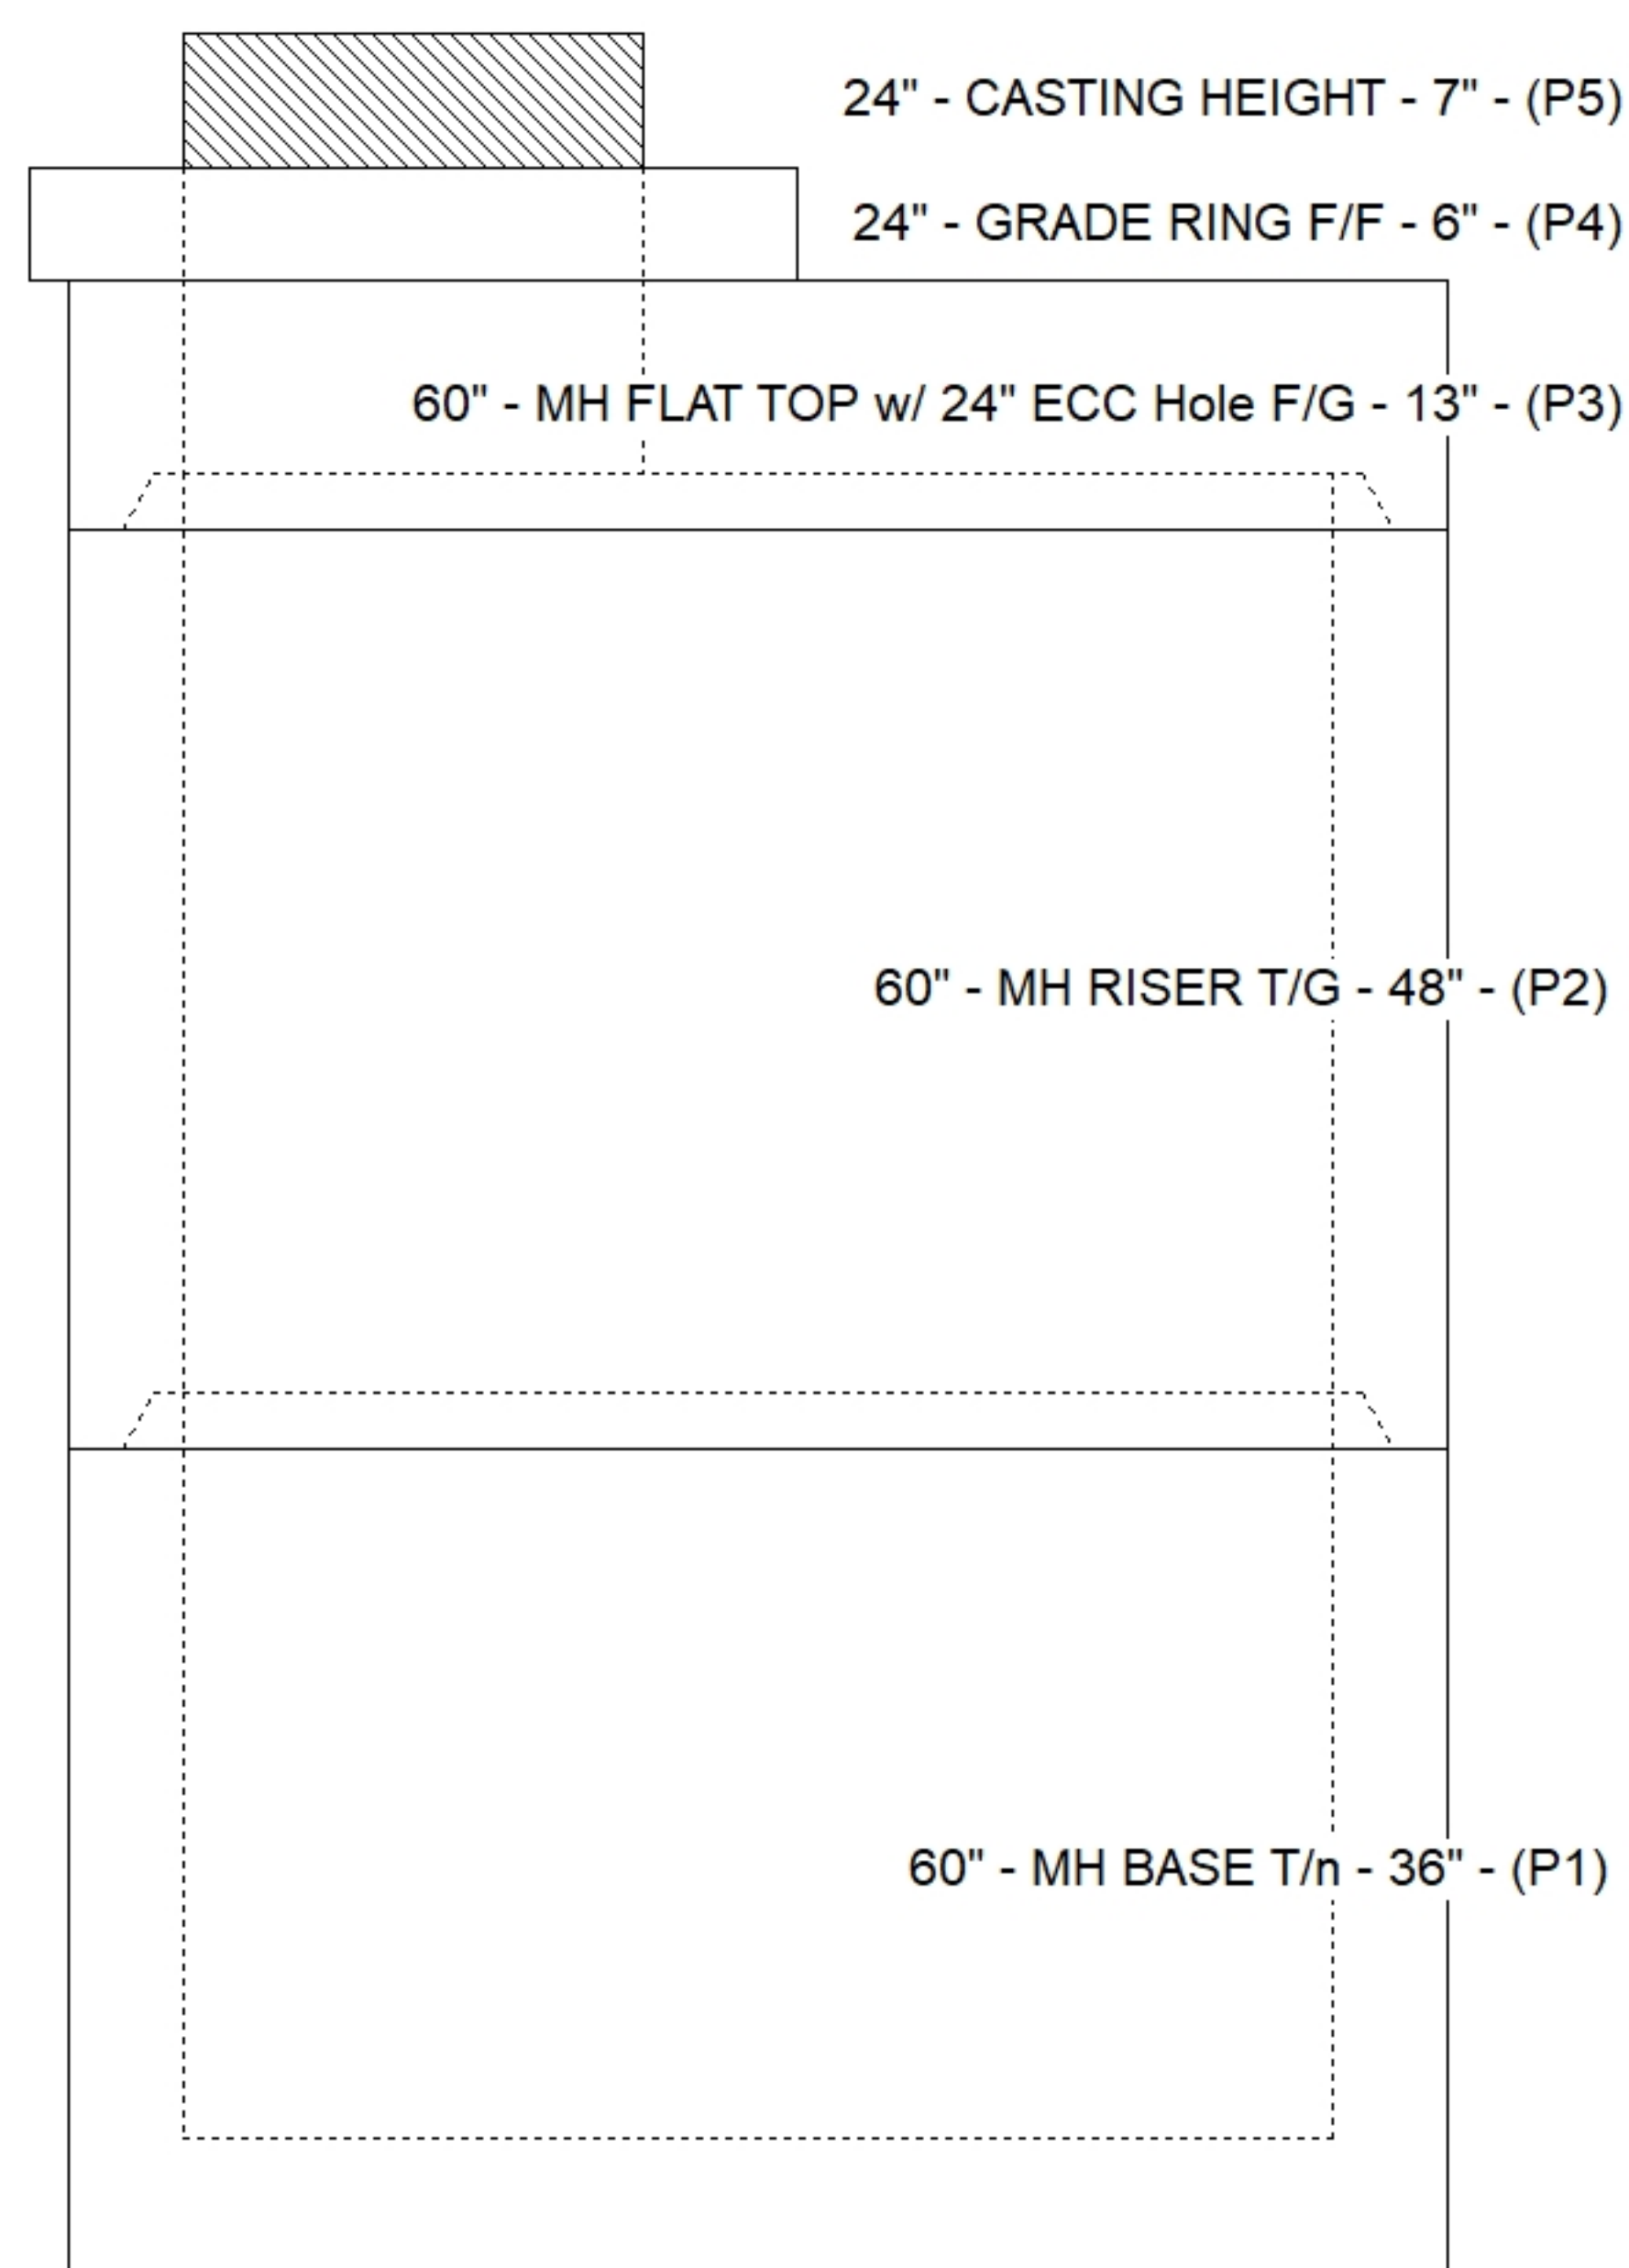

SUBMITTAL
APPROVED BY:
