

Job Name: 24-1632B KYTC Breathitt Co. Call 100-241306
Job Location: Breathitt Co., Ky.
Contractor: Triton Construction, Inc.

Plant: Beaver Dam

Tech: N. Richards

9/1/2026 9:43:30 AM

PC: C. Goff



Structure ID: 50+71 LT JB-A, JETT DR.

P1 BX2436-08BA36

BOX BASE 8inW, 8inF

P2) 24" x 36" - BX FLAT LID 8inW SOLID - 8"

P1) 24" x 36" - BOX BASE 8inW, 8inF - 36"

1) 24" x 36" - SGL 1"x14.5' Butyl

2) Hole - 32

1) Hole - 20

1396 lb

3779 lb

0 lb

0 lb

0 lb

Structure Total:

5175 lb

Structure Notes:

-KYTC STATE PROJECT 241306

-MANUFACTURED PER KYTC SPECIFICATIONS.

-REINFORCING: #5 BAR @ 12" C/C E.W.

-KYTC CERTIFICATIONS REQUIRED.

-SOLID TOP SLAB REQUIRED.

Rim: 732.84'

Rim to Invert: 3.69'

Slack: 0.28"



Sump: 0"

Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	729.15'	90°	26"	24" HDPE	27.8"	Hole 32	32"	32"	-4"	0"
Invert 2	729.15'	270°	26"	24" HDPE	27.8"	Hole 32	32"	32"	-4"	0"
Invert 3	729.15'	0°	20"	15" HDPE	17.6"	Hole 20	20"	20"	-2.5"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

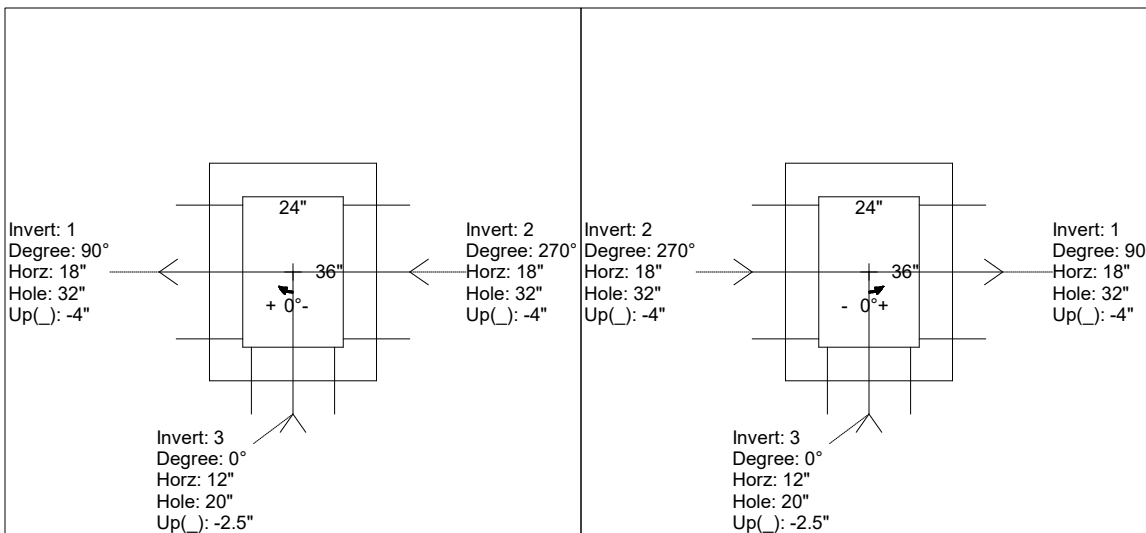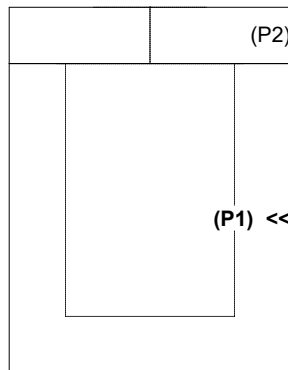

INSIDE WALL DIMENSIONS

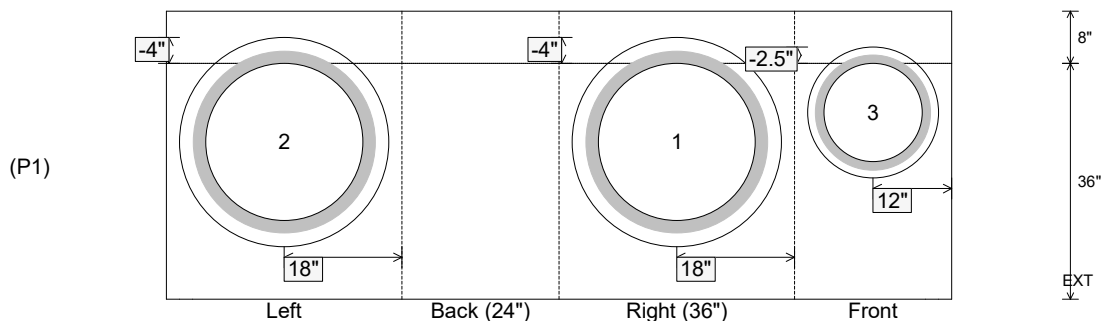

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 36"
Height (Ext): 44"

Weight (Net): 3779 lb
Volume (Net): 0.96cu.yd
