




Job Name: 24-2716B - 905 E Trinity Job Location: Nashville, TN Contractor: Hayes Pipe Supply					Plant: 100 6/5/2026 12:26:15 PM		Tech: Jared - F PC: A. Chambers				
Structure ID: SSMH-A1											
P1 MH048BA60CDARED			MH BASE w/ConBlock-CDA Red T/n								
P3) 24" - CASTING HEIGHT - 7" P2) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 24" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 60" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) ADMIXTURE CONBLOCK CDA RED 1) 48" - Conseal CS-102 1.00" (Double) 1) PSX - 12M NYLO 1) Drop Tee - 6" PVC 1) PSX - 12-08 NYLO 1) Drop Elbow - 6" PVC 7) MH Step ML-10-TDS-NCR - 10"					0 lb 1297 lb 5398 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 8 lb 0 lb 8 lb 0 lb 0 lb 0 lb		<u>Structure Notes:</u> 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY OTHERS. (JBS 1150 "SANITARY"). 5. EXTERIOR DROP ASSEMBLY FROM INVERT 2 TO INVERT 4 SUPPLIED BY ICAST. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 562.65' Rim to Invert: 7.47' Slack: 0.64" Sump: 2" Step Position: 180					Structure Total: 8151 lb						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	555.18'	0°	0"	8" DI	9"	PSX 12M NYLO	12"	12.129"	0"	0"	
Invert 2	558.5'	91°	46"	6" PVC SDR35	6.25"	Drop Tee 6" PVC	6.5"	6.52"	41.625"	0"	
Invert 3	555.38'	254°	128.5"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	2.375"	0"	
Invert 4	555.48'	91°	46"	6" PVC SDR35	6.25"	Drop Elbow 6" PVC	6.5"	6.52"	5.375"	0"	
Invert 5											
Invert 6											
Invert 7											
Invert 8											

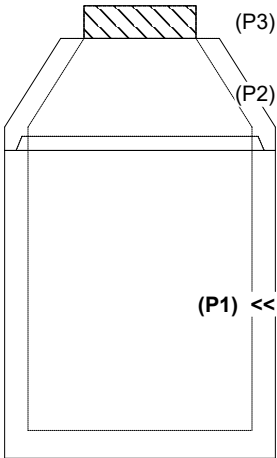


RIGHT-SIDE UP VIEW (int. dimensions)

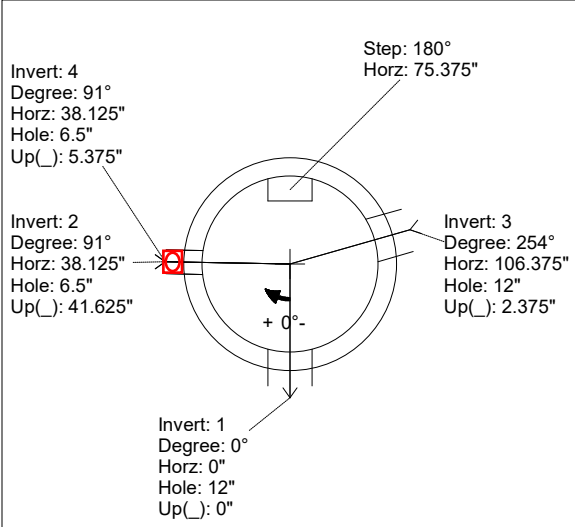

UPSIDE-DOWN VIEW (int. dimensions)

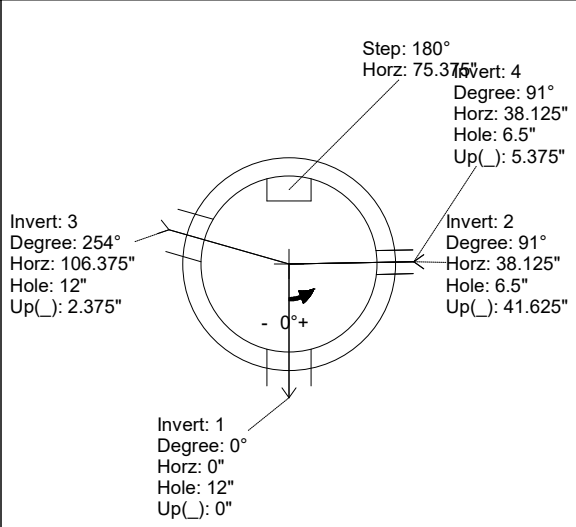


INSIDE WALL DIMENSIONS

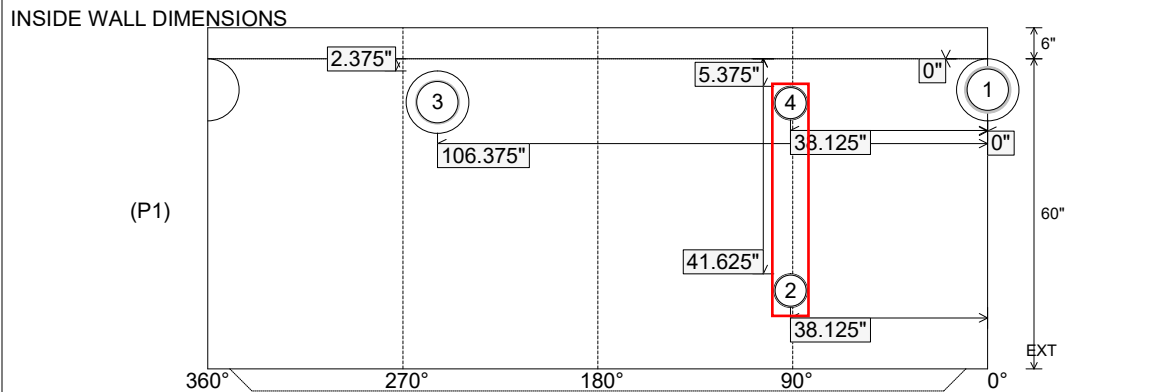


Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 60" Height (Ext): 66"	Weight (Net): 5398 lb Volume (Net): 1.38cu.yd
----------------------------------	---------------------------------	--	--	--


Job Name: 24-2716B - 905 E Trinity Job Location: Nashville, TN Contractor: Hayes Pipe Supply					Plant: 100 6/5/2026 12:26:15 PM		Tech: Jared - F PC: A. Chambers			
Structure ID: SSMH-A1										
P1 MH048BA60CDARED			MH BASE w/ConBlock-CDA Red T/n							
P3) 24" - CASTING HEIGHT - 7" P2) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 24" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 60" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) ADMIXTURE CONBLOCK CDA RED 1) 48" - Conseal CS-102 1.00" (Double) 1) PSX - 12M NYLO 1) Drop Tee - 6" PVC 1) PSX - 12-08 NYLO 1) Drop Elbow - 6" PVC 7) MH Step ML-10-TDS-NCR - 10"					0 lb 1297 lb 5398 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 8 lb 0 lb 8 lb 0 lb 0 lb ----- Structure Total: 8151 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY OTHERS. (JBS 1150 "SANITARY"). 5. EXTERIOR DROP ASSEMBLY FROM INVERT 2 TO INVERT 4 SUPPLIED BY ICAST. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 562.65' Rim to Invert: 7.47' Slack: 0.64" Sump: 2" Step Position: 180										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (↓)	Offset
Invert 1	555.18'	0°	0"	8" DI	9"	PSX 12M NYLO	12"	12.129"	0"	0"
Invert 2	558.5'	91°	46"	6" PVC SDR35	6.25"	Drop Tee 6" PVC	6.5"	6.52"	41.625"	0"
Invert 3	555.38'	254°	128.5"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	2.375"	0"
Invert 4	555.48'	91°	46"	6" PVC SDR35	6.25"	Drop Elbow 6" PVC	6.5"	6.52"	5.375"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										

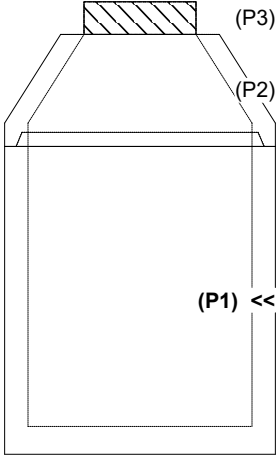


RIGHT-SIDE UP VIEW (int. dimensions)

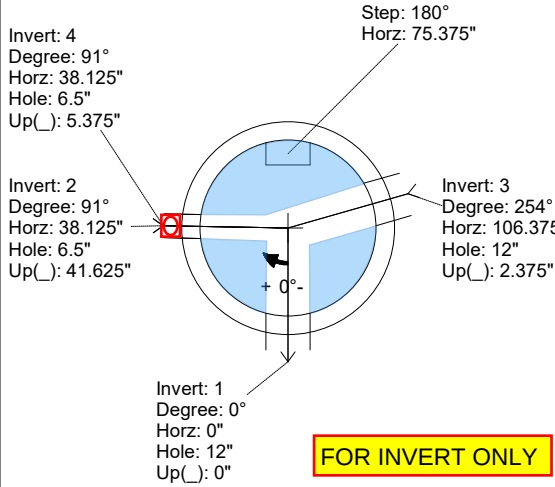

UPSIDE-DOWN VIEW (int. dimensions)

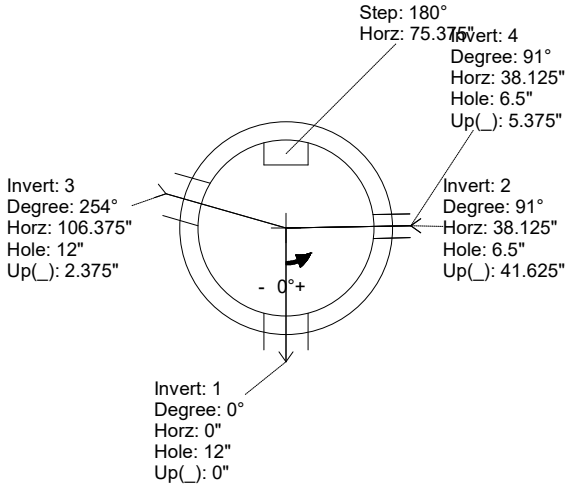

INSIDE WALL DIMENSIONS

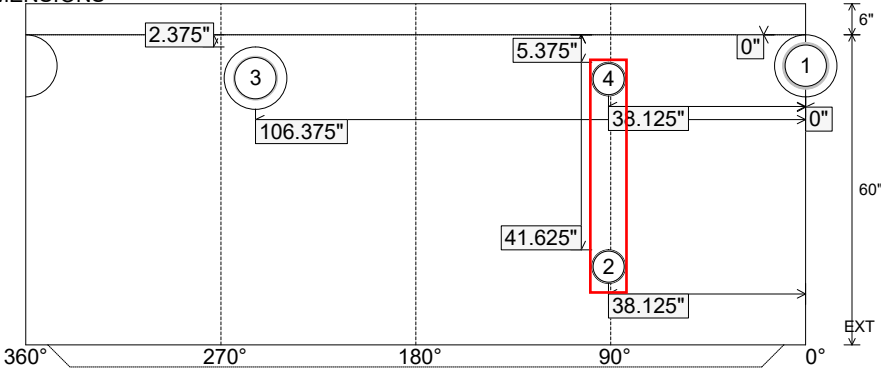

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 60" Height (Ext): 66"	Weight (Net): 5398 lb Volume (Net): 1.38cu.yd
----------------------------------	---------------------------------	--	--	--
