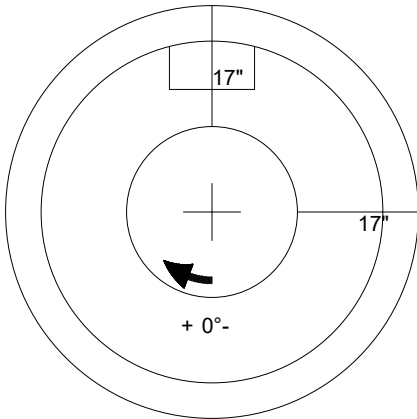



Job Name: 24-2716B - 905 E Trinity		Plant: 100	Tech: Jared - F		
Job Location: Nashville, TN		6/5/2026 12:26:27 PM	PC: A. Chambers		
Contractor: Hayes Pipe Supply					
Structure ID: SSMH-A1					
P2 MH048CCN24CDARED		CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G			
P3) 24" - CASTING HEIGHT - 7" P2) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 24" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 60" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) ADMIXTURE CONBLOCK CDA RED 1) 48" - Conseal CS-102 1.00" (Double) 1) PSX - 12M NYLO 1) Drop Tee - 6" PVC 1) PSX - 12-08 NYLO 1) Drop Elbow - 6" PVC 7) MH Step ML-10-TDS-NCR - 10"		0 lb 1297 lb 5398 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 8 lb 0 lb 8 lb 0 lb 0 lb ----- 8151 lb	Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY OTHERS. (JBS 1150 "SANITARY"). 5. EXTERIOR DROP ASSEMBLY FROM INVERT 2 TO INVERT 4 SUPPLIED BY ICAST. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
					
48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 24" - (P2) 					
Coating (Int): Coating (Ext):		Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 24"	Weight (Net): 1297 lb Volume (Net): 0.33cu.yd
