
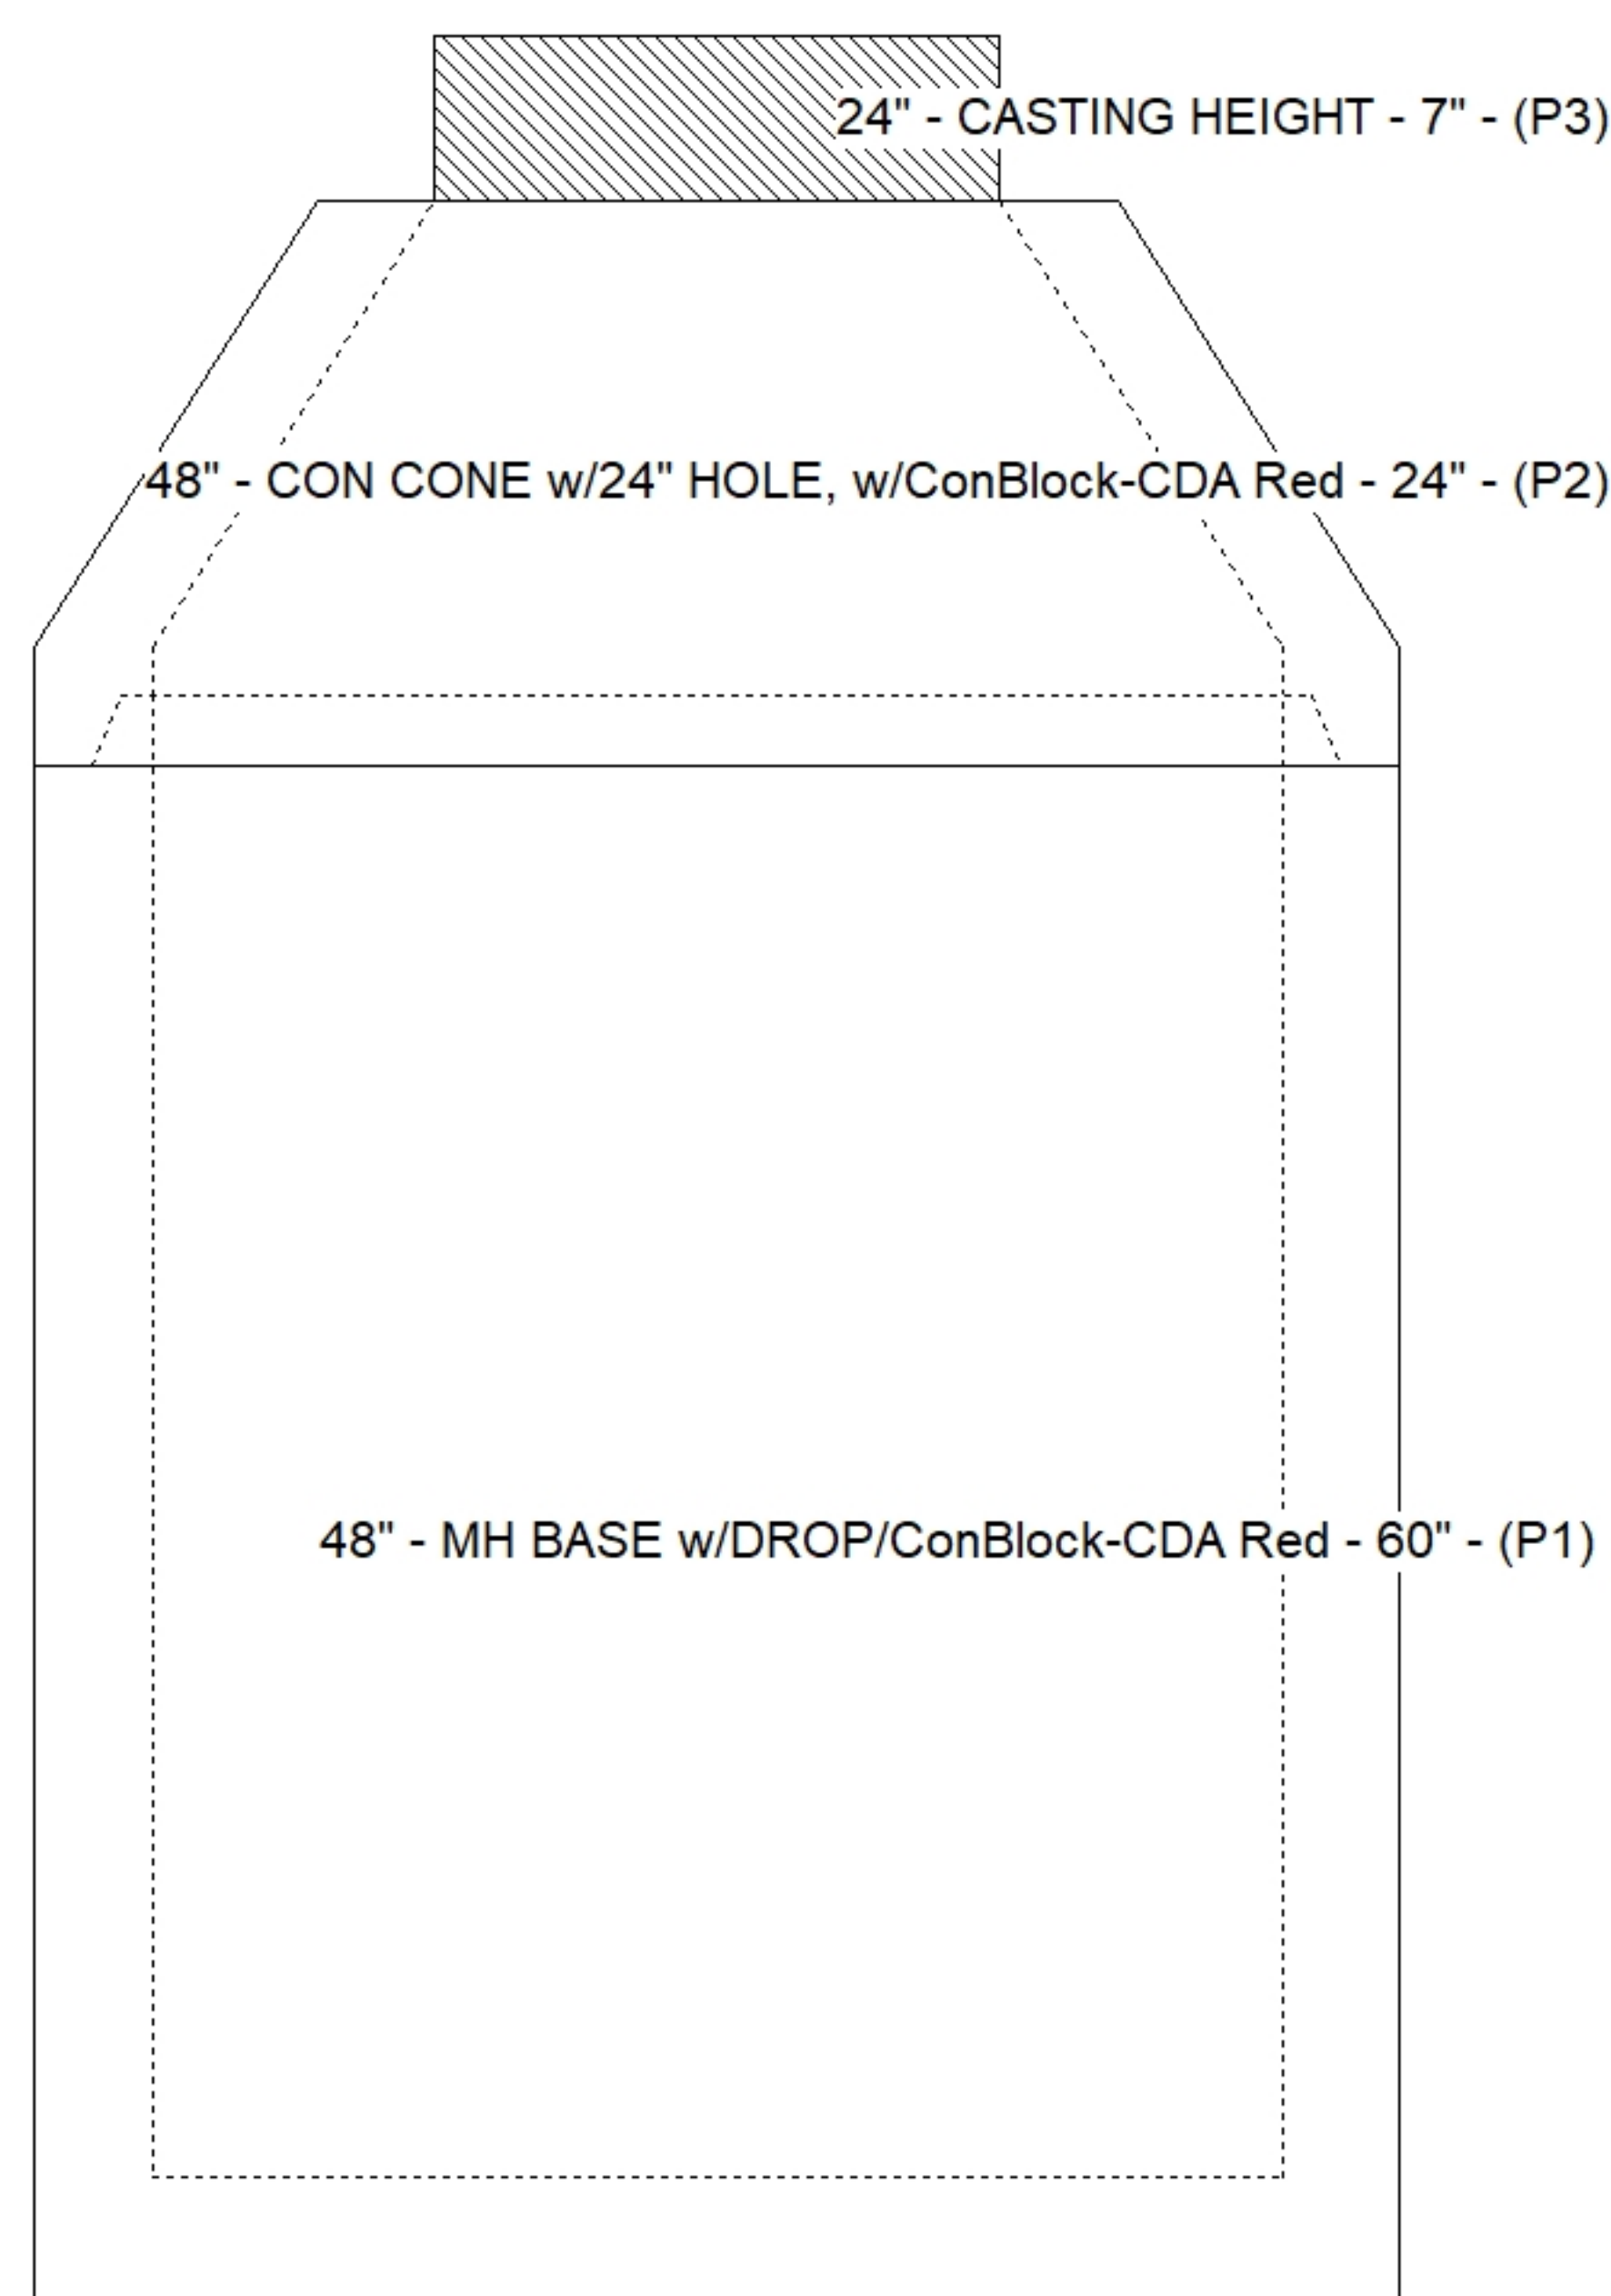


Rim: 562.65'	Sump: 2"	Floor (Bot): 554.513'
Invert: 555.18'	Floor (Top): 555.013'	Overall Height: 8.083'
Rim to Invert: 7.47'	Floor Height: 6"	Slack: 0.64"

P3) 24" - CASTING HEIGHT - 7"	0 lb
P2) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red - 24"	1297 lb
P1) 48" - MH BASE w/DROP/ConBlock-CDA Red - 60"	5398 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT	1440 lb
1) ADMIXTURE CONBLOCK CDA RED	0 lb
1) 48" - Conseal CS-102 1.00" (Double)	0 lb
1) 24" - Conseal CS-102 1.00" (Double)	0 lb
1) PSX - 12M NYLO	8 lb
1) Drop Tee - 6" PVC	0 lb
1) PSX - 12-08 NYLO	8 lb
1) Drop Elbow - 6" PVC	0 lb
7) MH Step ML-10-TDS-NCR - 10"	0 lb

Structure Total:	8151 lb

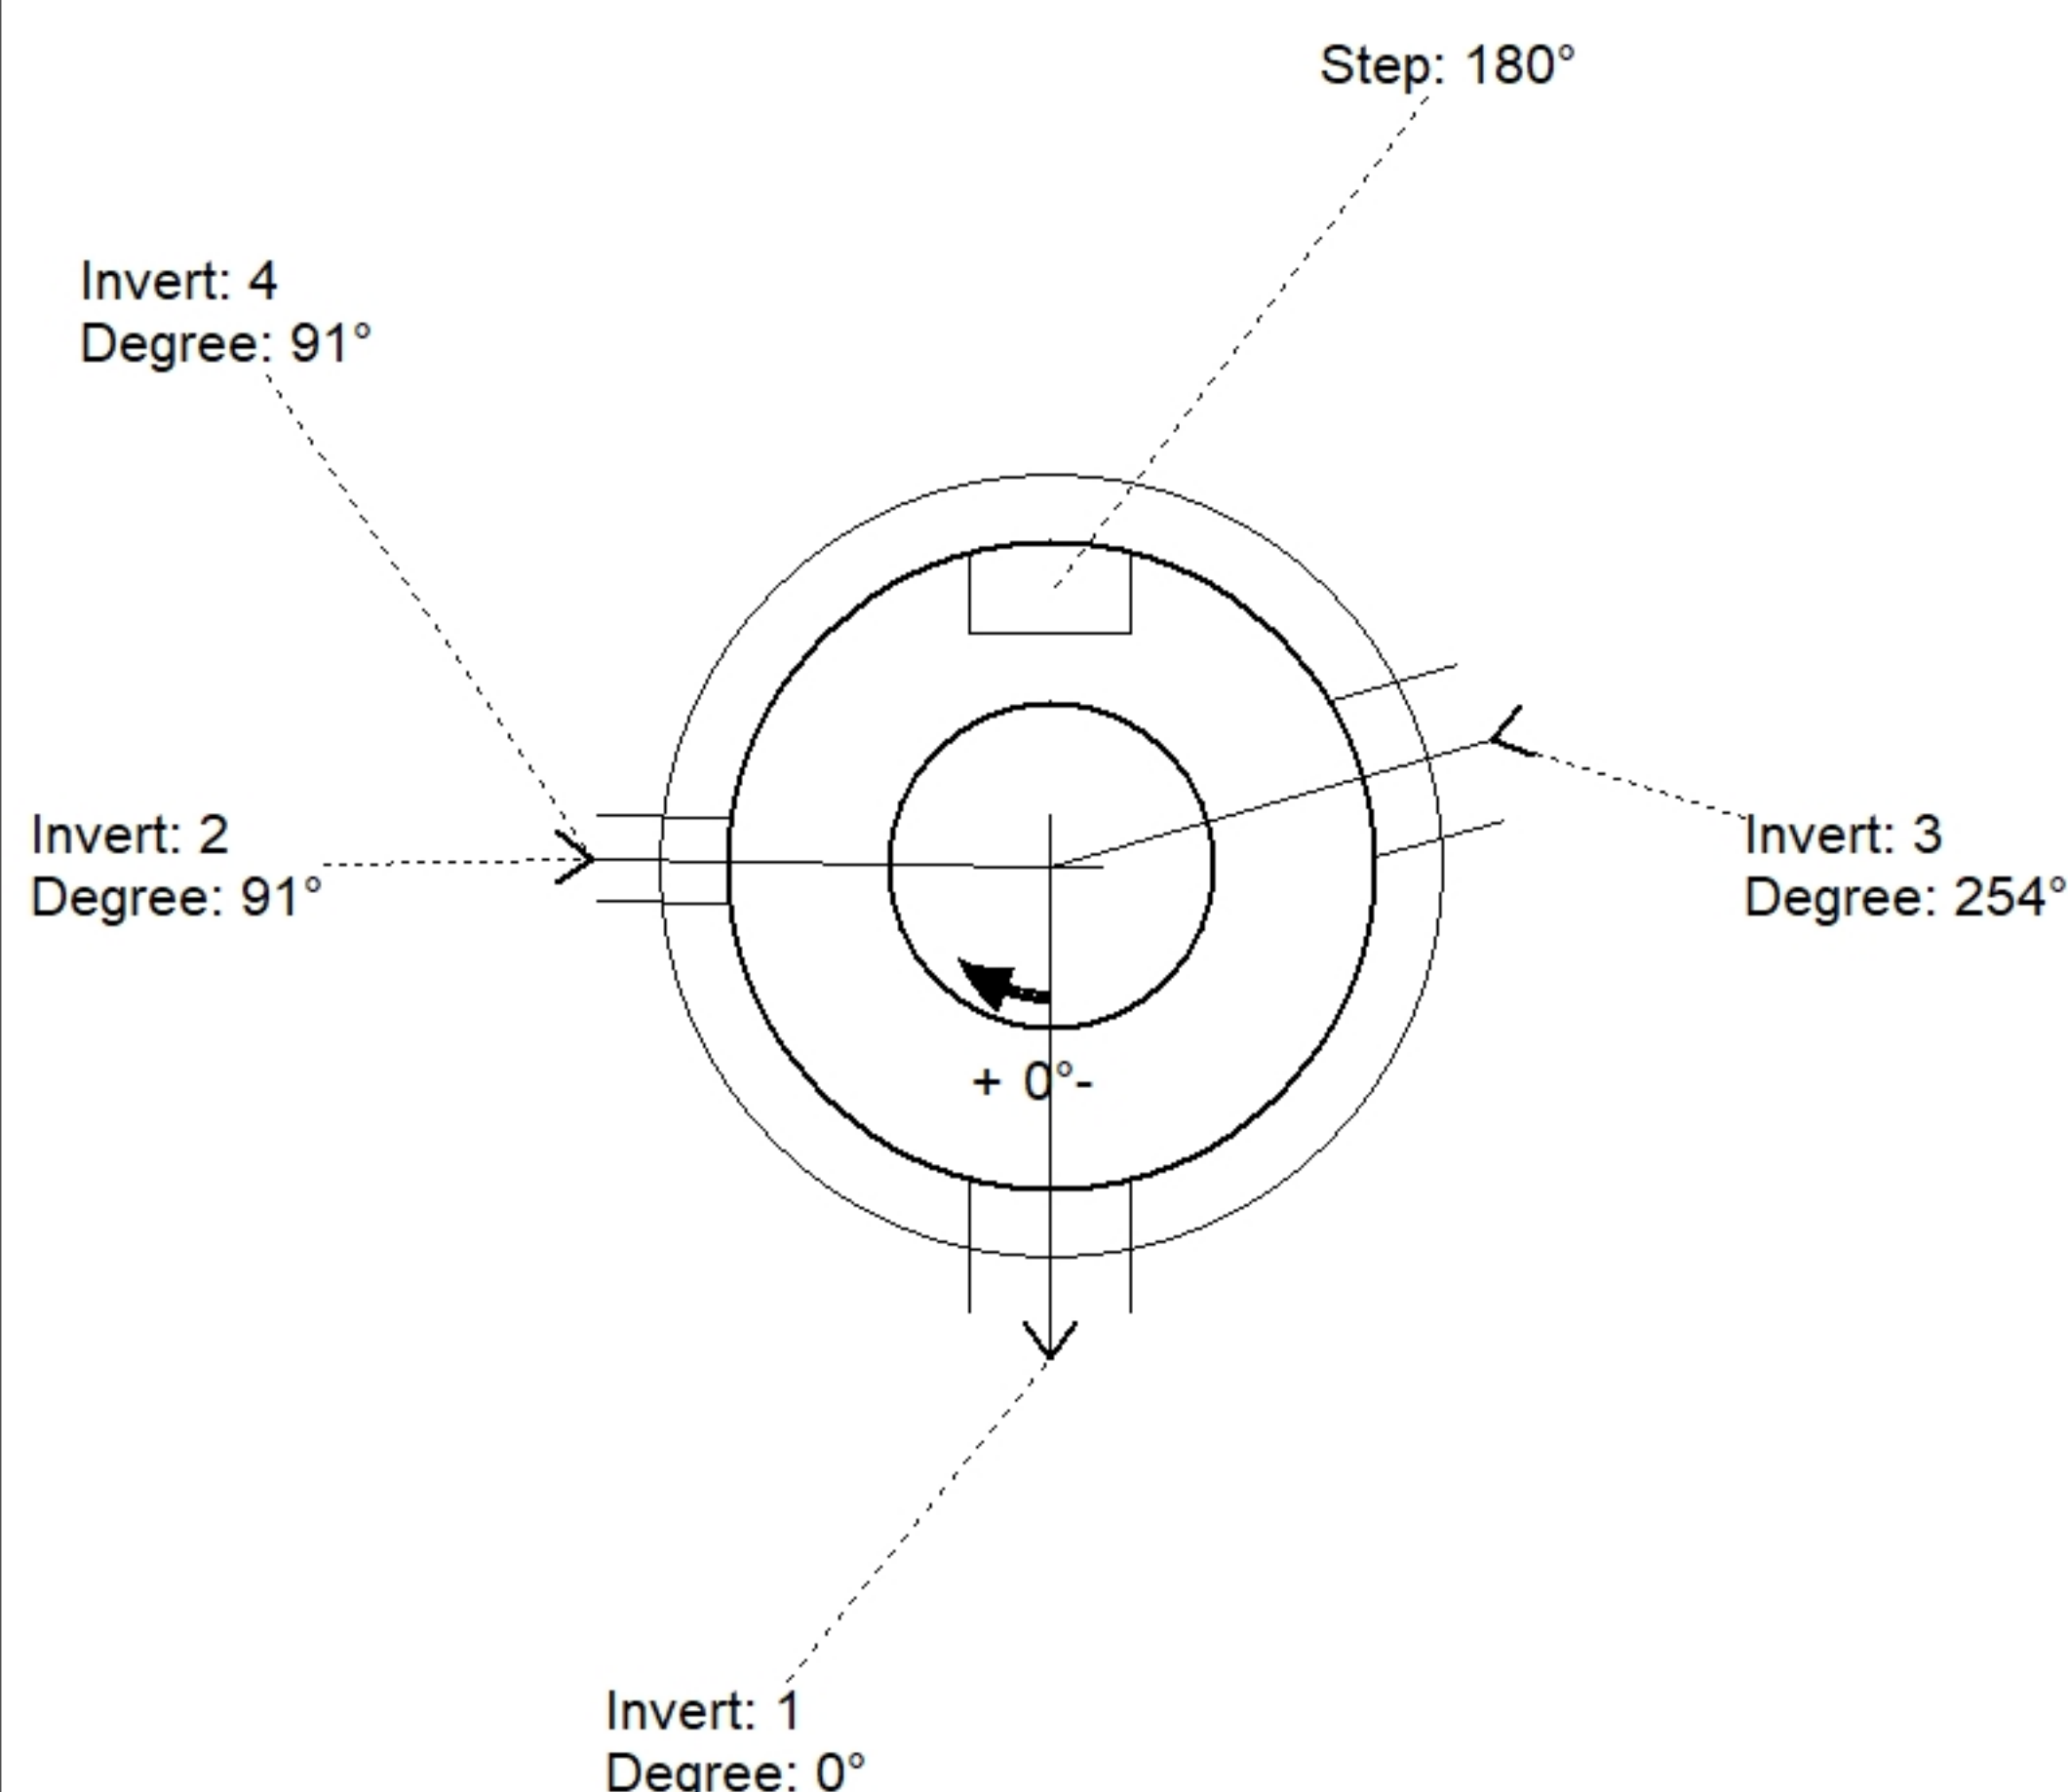

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	562.65'							
Reducer								
Invert 1	555.18'	0°	8" DI	9"	12"	PSX 12M NYLO	0"	P1
Invert 2	558.5'	91°	6" PVC SDR35	6.25"	6.5"	Drop Tee 6" PVC	41.59"	P1
Invert 3	555.38'	254°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	2.4"	P1
Invert 4	555.48'	91°	6" PVC SDR35	6.25"	6.5"	Drop Elbow 6" PVC	5.35"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

SUBMITTAL
APPROVED BY:
