


Contractor: Tim Klenck Demolition LLC

Plant: Beaver Dam, KY



Slack: 0.97"

Structure Total: 4733 lb

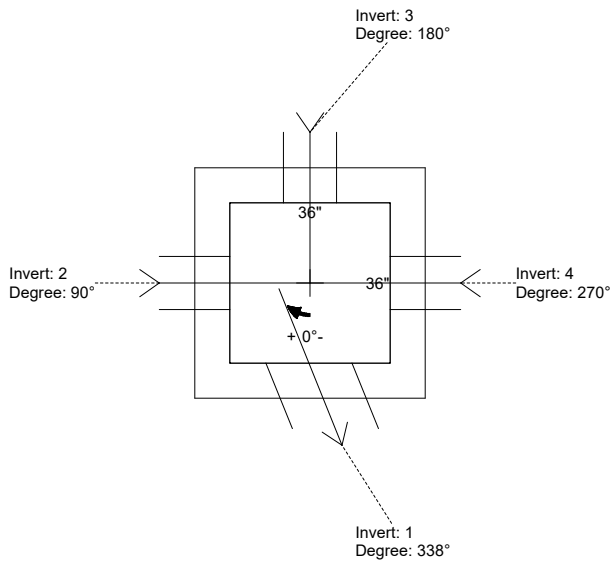


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	404.94'							
Reducer								
Invert 1	402.63'	338°	12" ADS N-12	14.5"	18"	Hole 18	0"	P1
Invert 2	402.97'	90°	8" ADS N-12	9.1"	12"	Hole 12	4.75"	P1
Invert 3	403.36'	180°	8" ADS N-12	9.1"	12"	Hole 12	9.5"	P1
Invert 4	402.97'	270°	8" ADS N-12	9.1"	12"	Hole 12	4.75"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

36" x 36" - CASTING HEIGHT - 3" - (P2)

36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/- 25" - (P1)

The diagram illustrates a cross-section of a casting mold. It features a rectangular casting height of 3 inches, labeled '36" x 36" - CASTING HEIGHT - 3" - (P2)', which is shaded with diagonal lines. Below this is a larger rectangular box base, labeled '36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/- 25" - (P1)', outlined with a dashed line. The entire assembly is contained within a larger rectangular frame.



SUBMITTAL
APPROVED BY:
