
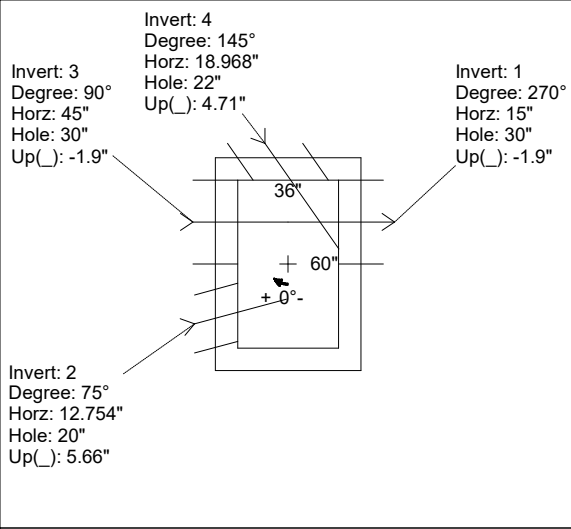
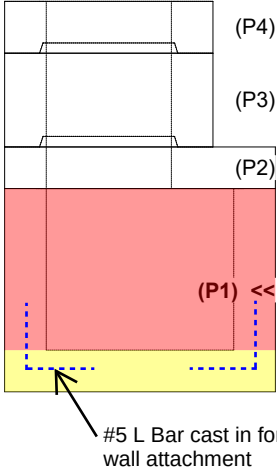



Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC					Plant: Beaver Dam 7/30/2026 8:55:19 AM		Tech: J. Horsley PC: C. Goff				
Structure ID: 234 (425+20 RT)											
P1		BX3660-08BAVF		BOX BASE 8inW, 8inF, Variable Ht F/n							
P4) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P3) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18" P2) 36" x 60" - CB FT REDUCER 24"X36" HOLE T/F - 8" P1) 36" x 60" - BOX BASE 8inW, 8inF, Variable Ht F/n - 31" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) 36" x 60" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 30 1) Hole - 20 1) Hole - 22						3400 lb 5270 lb 2073 lb 6310 lb 206 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 17259 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. HOE KY-206 F/C CAST INTO TOP SLAB. REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - TRANS. SLAB (As .62) #5 BARS AT 6" C.C.E.W (DBL MAT) - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 546.53'		Rim to Invert: 5.59'		Slack: 0.08"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	540.94'	270°	23"	24" HDPE	27.8"	Hole 30	30"	30"	-1.9"	-15"	
Invert 2	541.52'	75°	18.61"	15" HDPE	17.6"	Hole 20	20"	20.706"	5.66"	-12"	
Invert 3	540.94'	90°	53"	24" HDPE	27.8"	Hole 30	30"	30"	-1.9"	15"	
Invert 4	541.52'	145°	21.366"	15" RCP B WALL	19.5"	Hole 22	22"	26.857"	4.71"	18"	
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)						UPSIDE-DOWN VIEW (int. dimensions)					
						2-Stage Pour Required First pour drawing First pour weight = 2,653 LBS Second pour weight = 3,657 LBS					
						INSIDE WALL DIMENSIONS					
											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 31" Height (Ext): 39"		Weight (Net): 6310 lb Volume (Net): 1.61cu.yd		



Weight (Net): 6310 lb
Volume (Net): 1.61cu.yd
