

Contractor: Scotty's Contracting & Stone, LLC

TECH: J. Horsley

Plant: Beaver Dam



Size: 24" x 24"

Rim to Invert: 4.34'

Floor Height: 8"


Slack: 0.08"

- FLOOR (As .31) #5 BARS AT 12: C.C.E.W.

2) Hole - 20

0 lb


Structure Total: 5409 lb

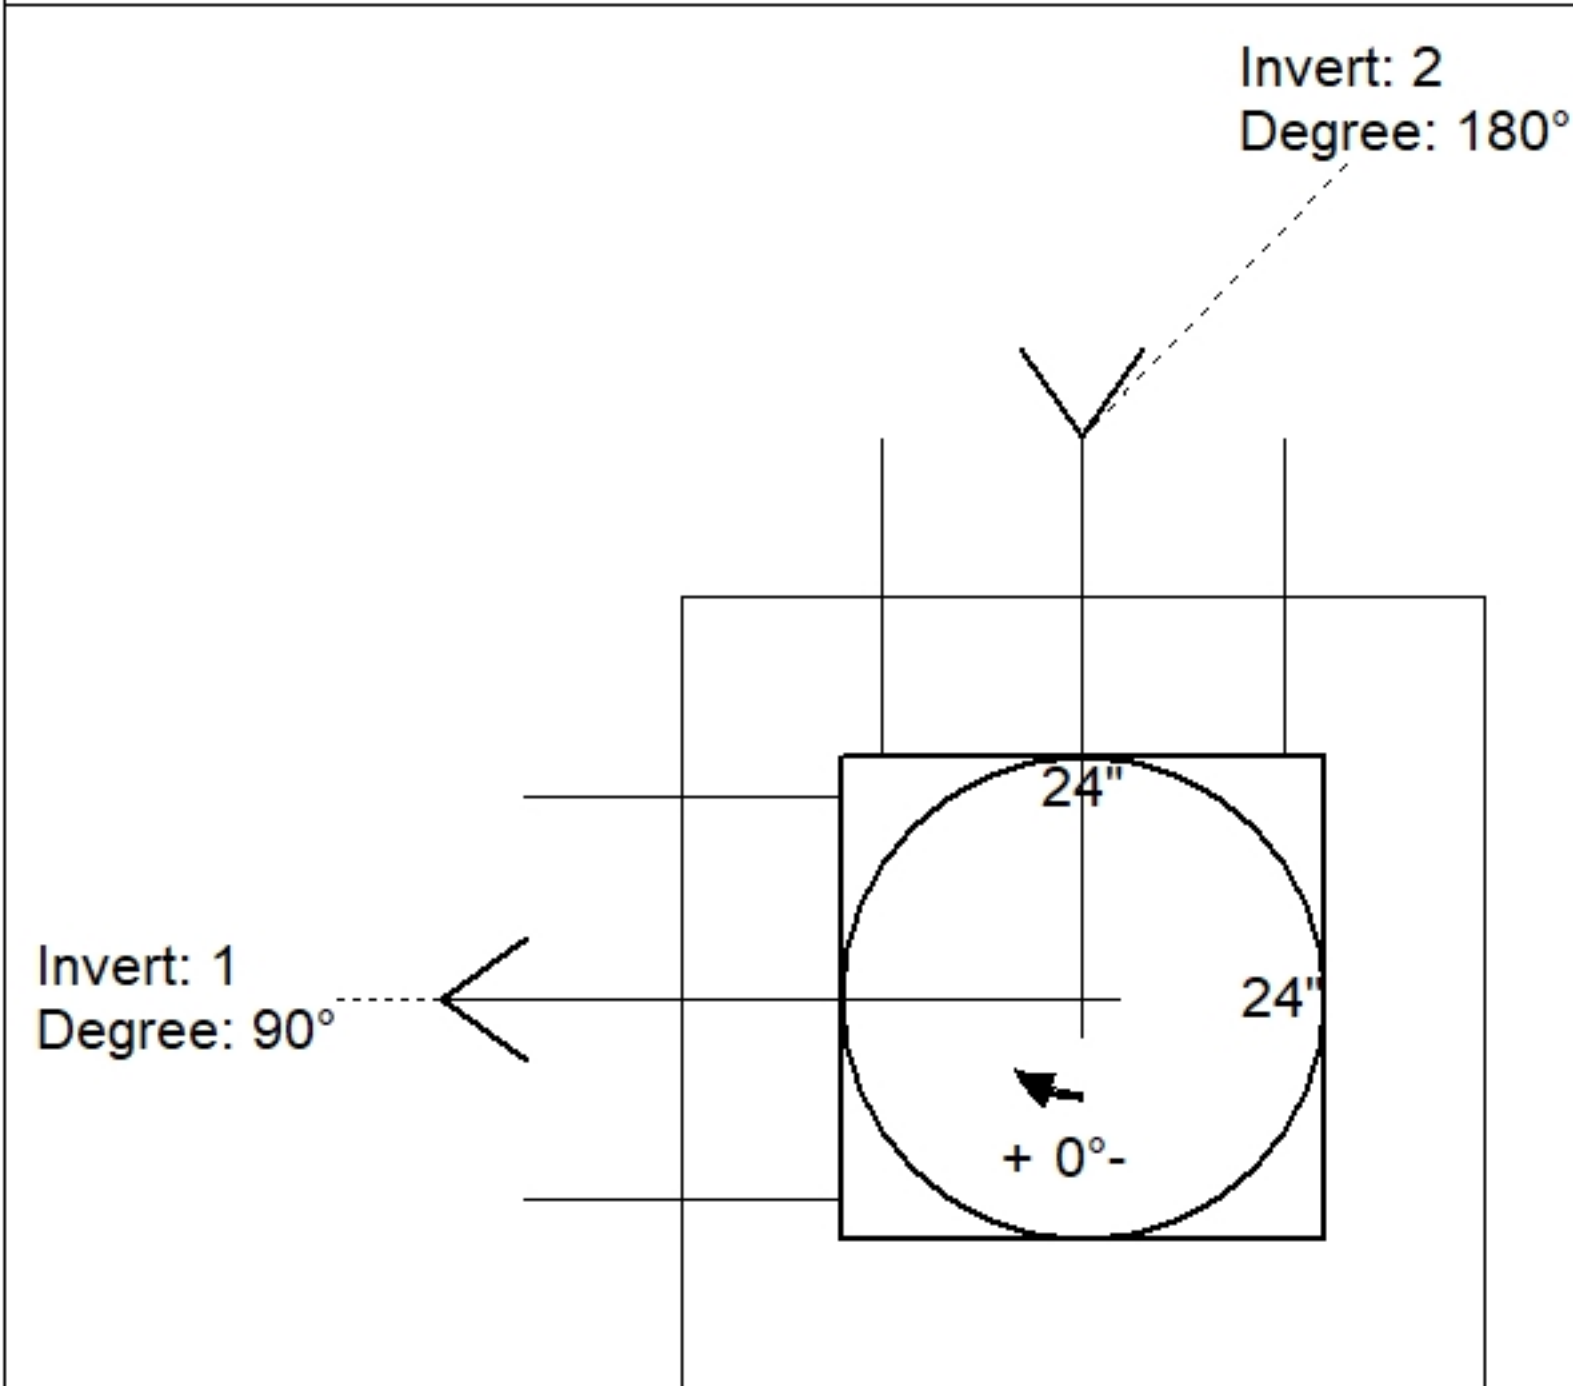

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	542'							
Reducer								
Invert 1	537.66'	90°	15" HDPE	17.6"	20"	Hole 20	-1.3"	P1
Invert 2	537.66'	180°	15" HDPE	17.6"	20"	Hole 20	-1.3"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 44" - (P1)

Default - Interior Dimensions

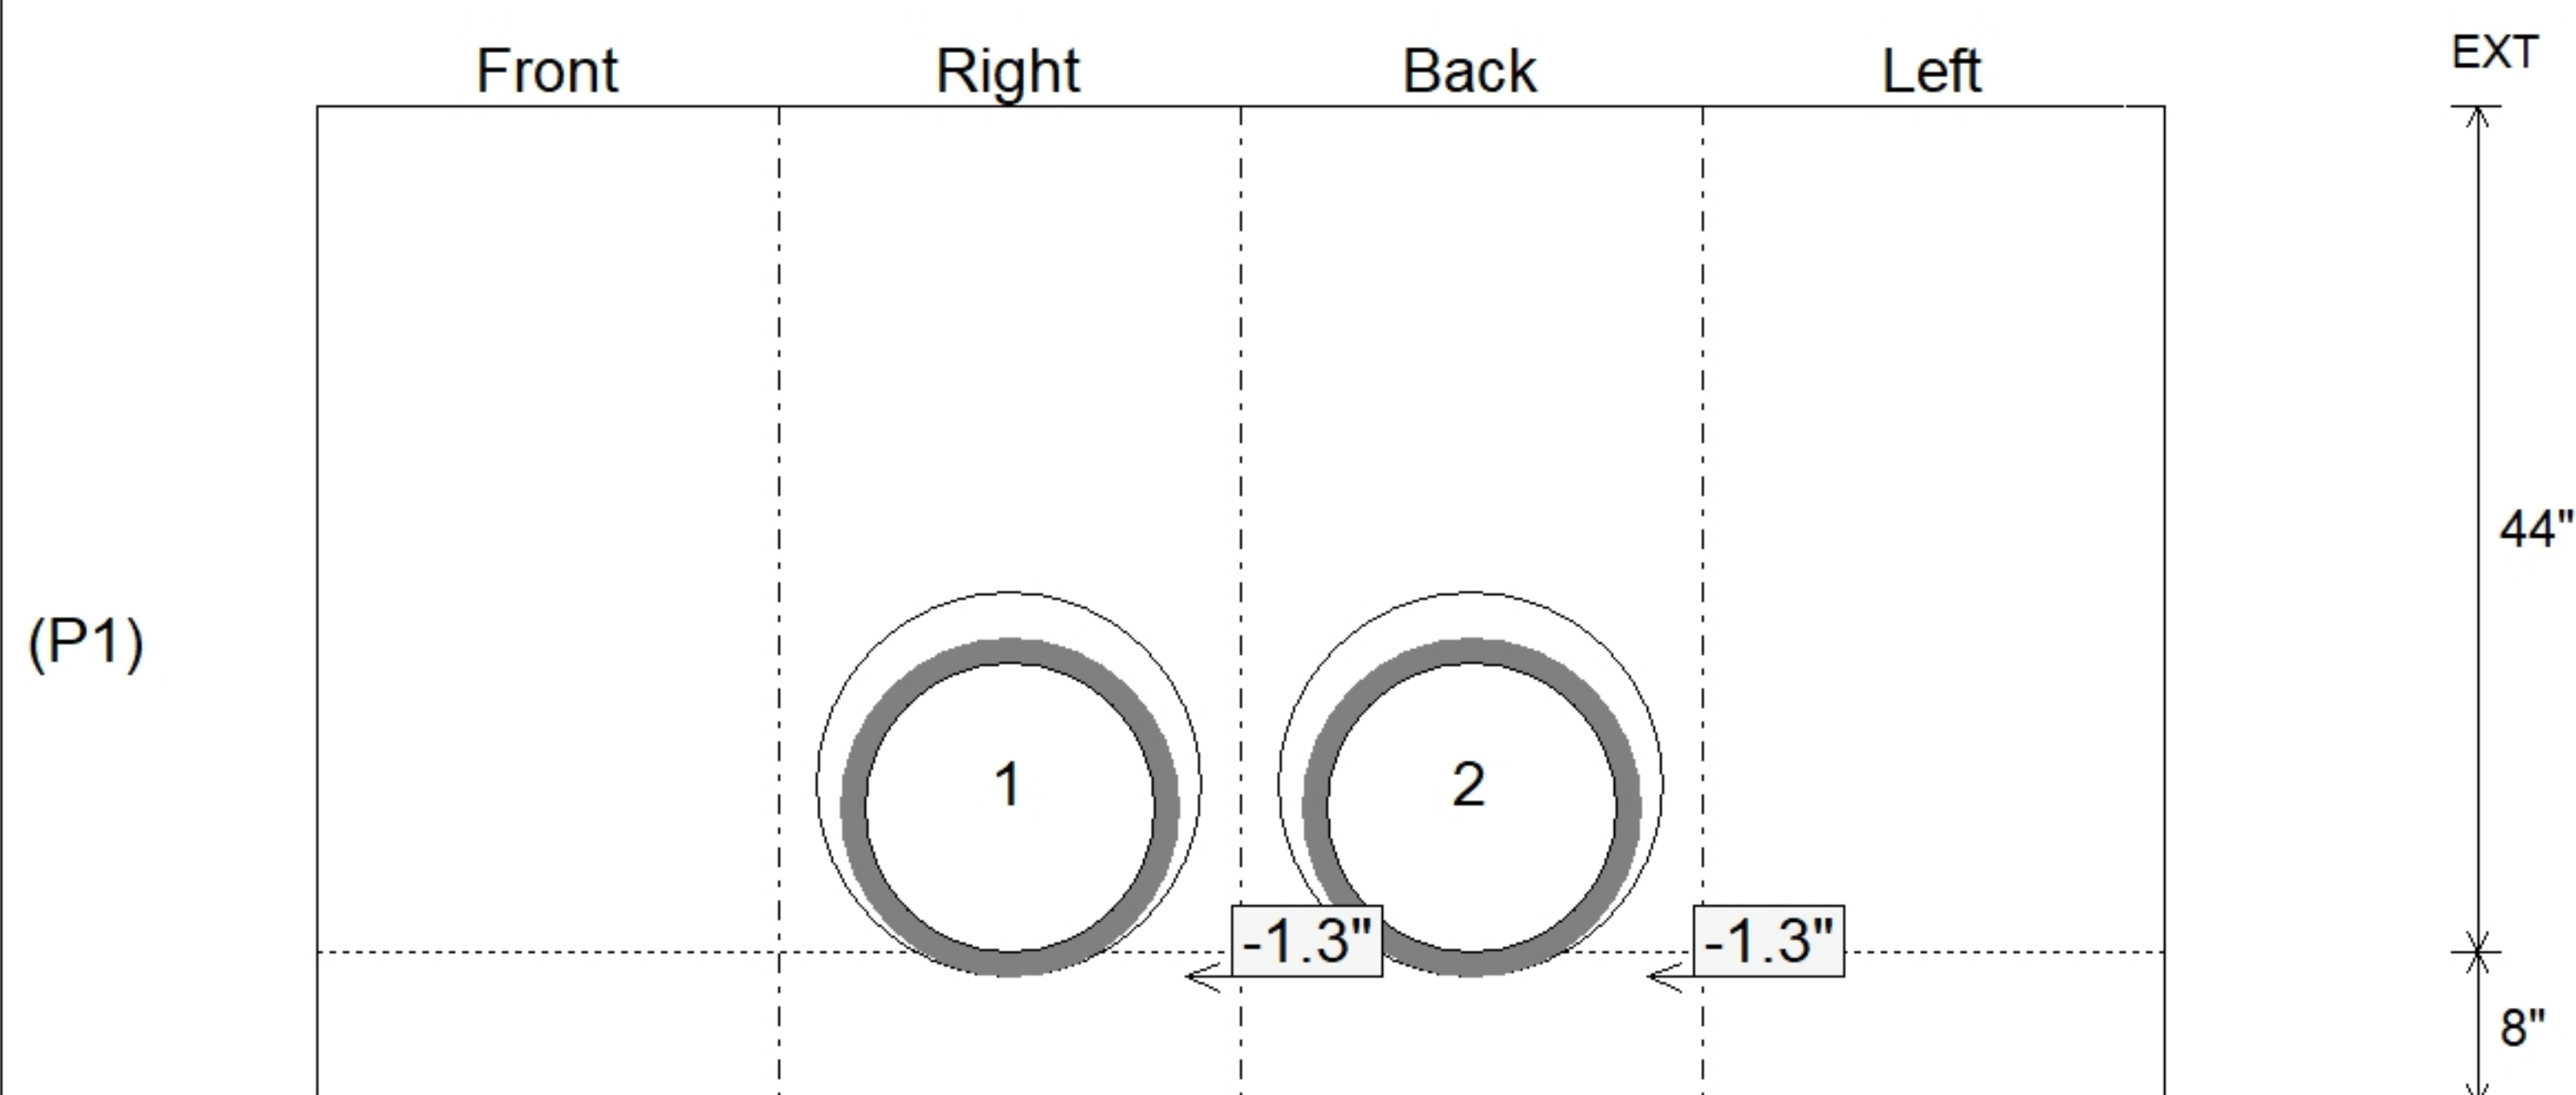

SUBMITTAL
APPROVED BY:
