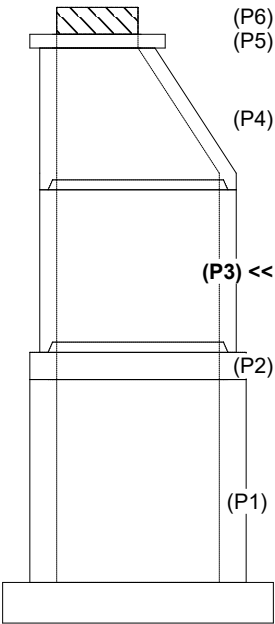

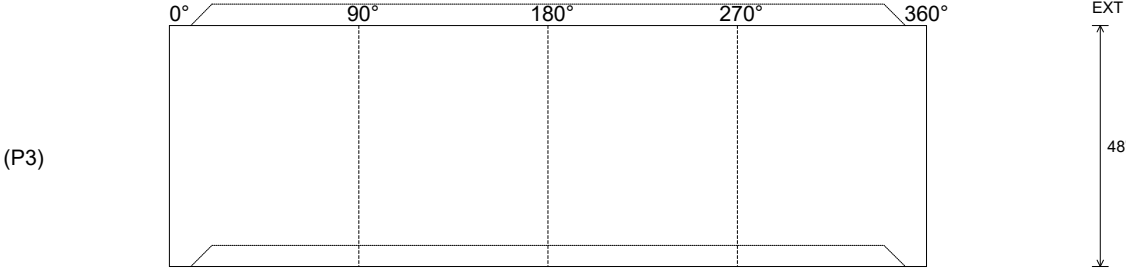


Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC					Plant: Beaver Dam 7/30/2026 8:59:19 AM		Tech: J. Horsley PC: C. Goff						
Structure ID: 267 (435+52 RT)													
P3 MH048RS48			MH RISER T/G										
P6) 24" - CASTING HEIGHT - 8" P5) 24" - GRADE RING F/F - 4" P4) 48" - ECC CONE w/ 24" HOLE F/G - 42" P3) 48" - MH RISER T/G - 48" P2) 48" x 48" - CB FT REDUCER 48" HOLE T/F - 8" P1) 48" x 48" - BX BASE w/FLANGE 08W/12F/08EF F/n - 60" 1) CASTING - HOE KY-510 F/C (KY TY.2) 1) 48" x 48" - Conseal CS-102 1.00" 2) 48" - Conseal CS-102 1.00" 2) Hole - 44						0 lb 270 lb 3200 lb 3353 lb 1535 lb 13425 lb 510 lb 0 lb 0 lb 0 lb ----- 22293 lb		Structure Notes: . ** KYTC STATE PROJECT** 1. PER KYTC MANHOLE TYPE C / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-510 F/C) 4. SECONDARY POUR REQ'D FOR EXTENDED FLANGE (8"WD x 12" THICK). . REINFORCING PER ASTM A615 (GRADE 60). - TRANS. SLAB #5's AT 6" C.C.E.W (DBL MAT). - WALLS #5's AT 6" C.C.E.W. - FLOOR #5's AT 12" C.C.E.W..					
Rim: 546.75' Rim to Invert: 14.32' Slack: 1.84" Sump: 0" Step Position: 90°													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
INSIDE WALL DIMENSIONS													
													
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 48" Height (Ext): 48"		Weight (Net): 3353 lb Volume (Net): 0.86cu.yd			
