

Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam



Size: 24" x 30"

Rim to Invert: 3'

Floor Height: 8"


Slack: 0.25"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W..
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

1) Hole - 22

0 lb


Structure Total: 4408 lb

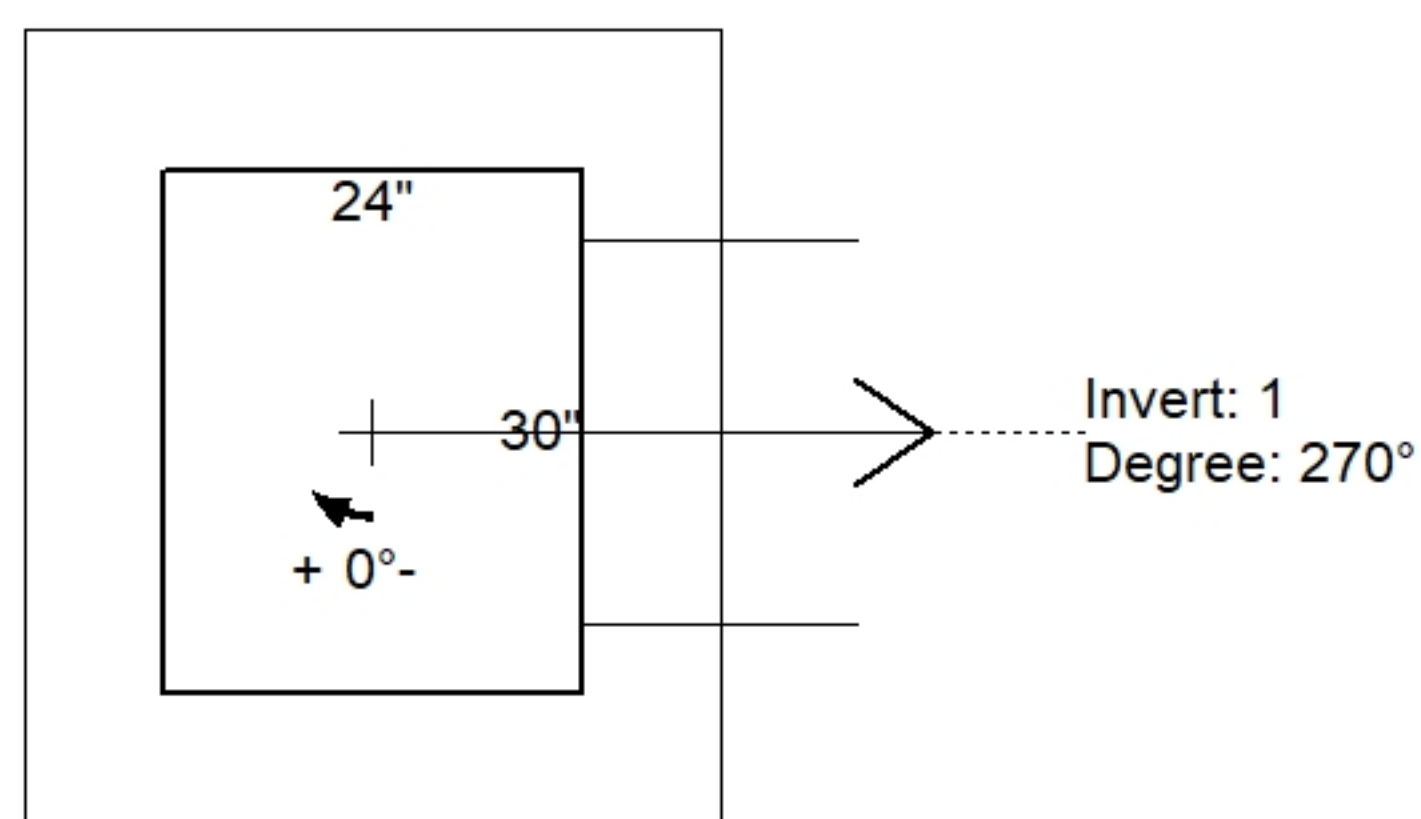

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	545.52'							
Reducer								
Invert 1	542.52'	270°	15" RCP B WALL	19.5"	22"	Hole 22	-2.25"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 30" - BOX BASE 8inW, 8inF, Variable Ht F/n - 32" - (P1)

Default - Interior Dimensions

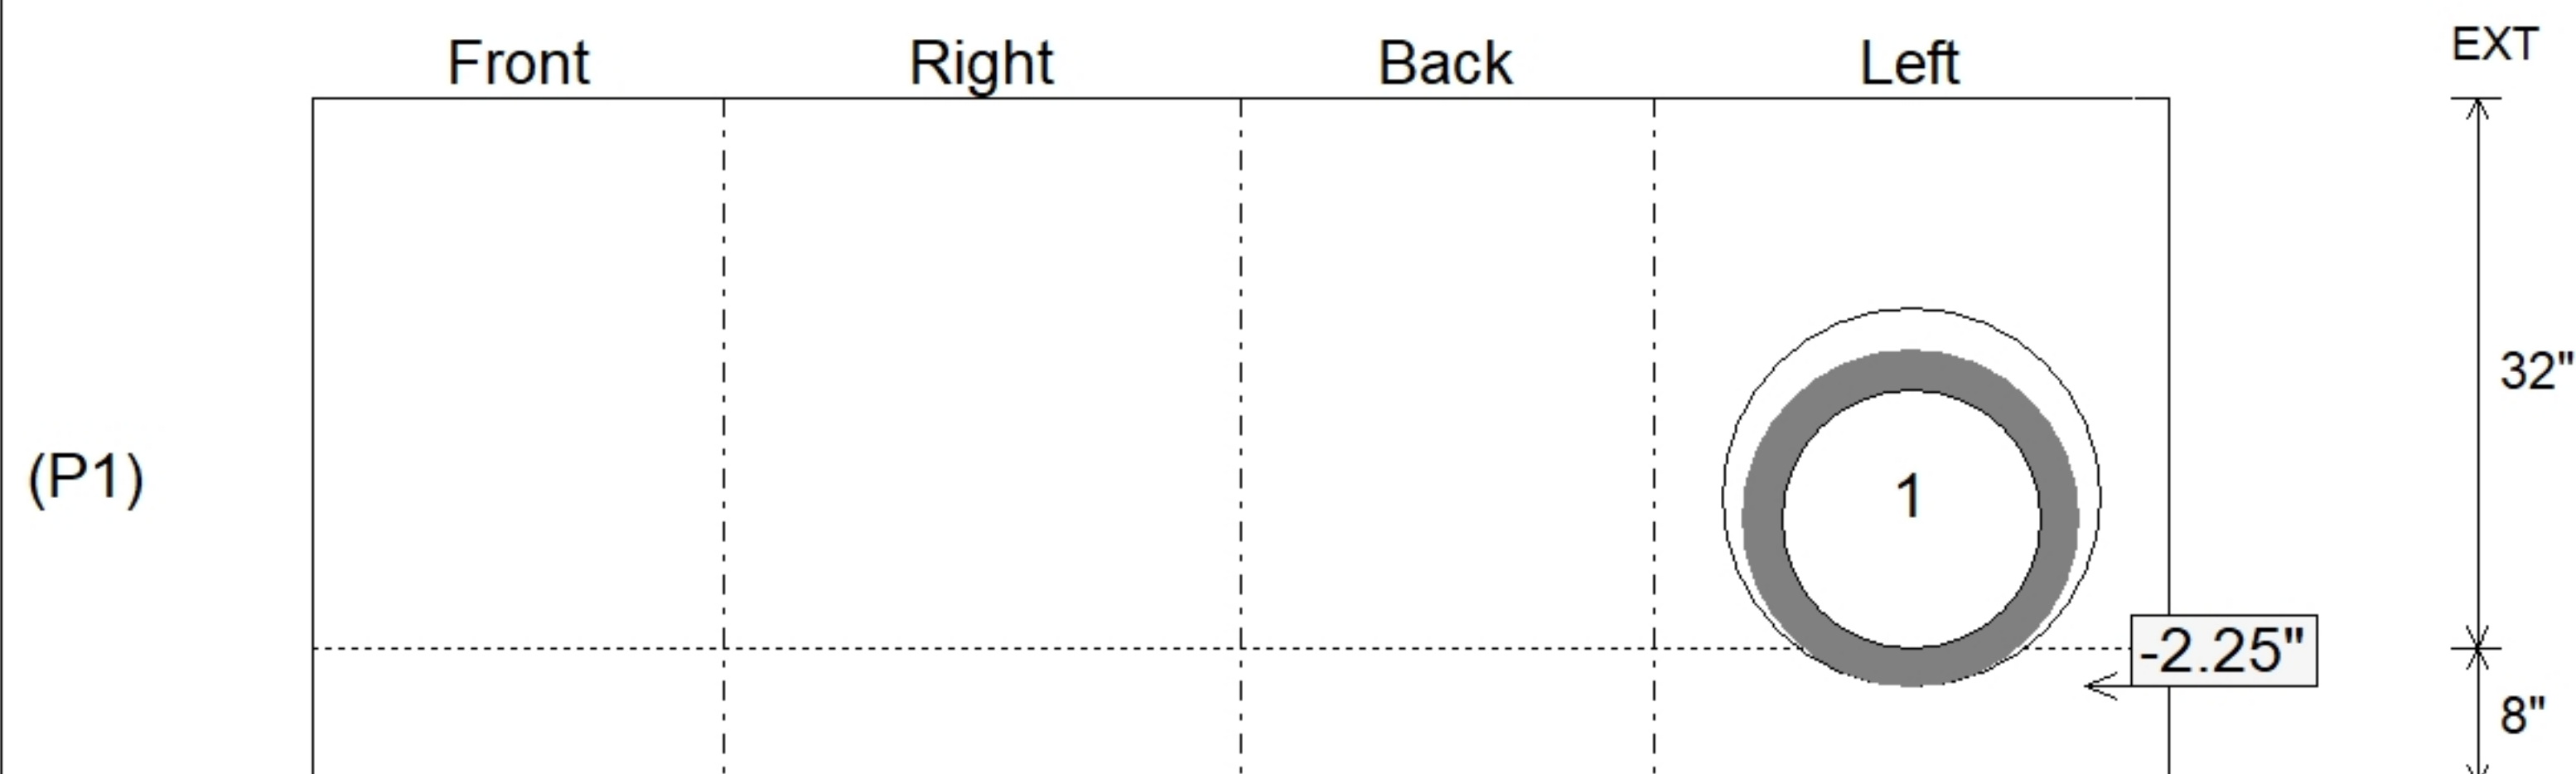

SUBMITTAL
APPROVED BY:
