


PRINT IN COLOR FOR ADDITIONAL CLARITY

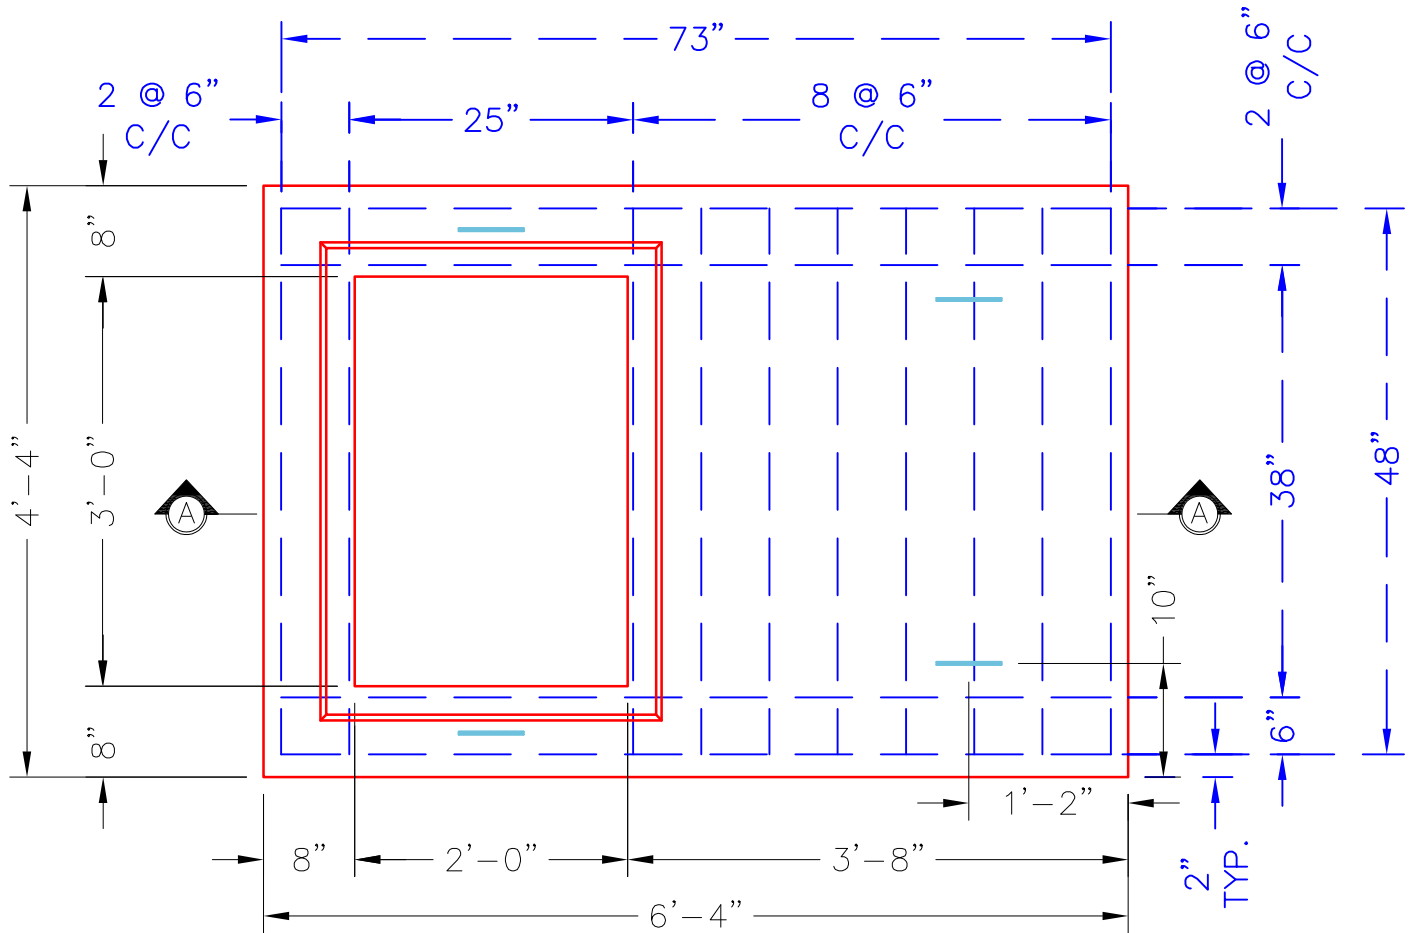

PLAN VIEW

4 EA. CONAC .8 TON 8¹/₁₆"
(6MM) WIRE ROPE ANCHORS
REQUIRED-MINIMUM.

24" X 36" OPENING
OFFSET IN SLAB

TONGUE TO MATCH
GROOVE IN 24"X36" RISER
OR KDOT TYPE A TOP PHASE.

ROUND TOP
EDGES

#5 BAR @ 6" C/C TYP.
(TOP & BOTTOM)

SECTION A-A

8"
2"
CLR.

NOTES:

- CONCRETE: 4500 PSI @ 28 DAYS.
- MANUFACTURED TO ASTM C-913 SPECIFICATIONS.
- REINFORCING: #5 BAR @ 6" C/C AS SHOWN-GRADE 60.
(TOP & BOTTOM LAYER)
- 4 EA. CONAC WIRE LOOP LIFTS REQUIRED (MIN.)

#5 BAR CUT LIST
4 EA. @ 73" LG.
10 EA. @ 48" LG.

PRODUCTION WORK ORDER

PRODUCT I.D.:
BX3660-08TS024036

DESCRIPTION:
CURB INLET TRANSITION SLAB 36" X 60" X 8"



QUALITY CONTROL CHECKLIST

- ☐ ALL DIMENSIONS CORRECT.
- ☐ LIFTERS INSTALLED.
- ☐ OPENING CENTERED.
- ☐ REINFORCING CORRECT.
- ☐ SURFACE QUALITY ACCEPTABLE.
- ☐ EDGES CHAMFERED.
- ☐ ALL PATCHWORK ACCEPTABLE.

PRODUCT VIEW: RIGHT SIDE UP

PLANT: BEAVER DAM, KY.

WEIGHT: 2,073 LBS.

TOP SECTION JOINT: TONGUE

BASE SECTION JOINT: FLAT

QC CHECK INITIALS:

CUSTOMER: SCOTTY'S CONTRACTING & STONE LLC

PROJECT: KYTC CHRISTIAN CO. CALL 100 (ID 241018)

STRUCTURE: 283 (443+60 RT) (SEC. P2)

QUOTE/ORDER NO: 24-4208

PC: C. GOFF

DRAWING: S. FELLETER

DATE: 08/04/26

SCALE: NTS

PG. 1 of 1
