


Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC					Plant: Beaver Dam 8/3/2026 4:22:41 PM		Tech: J. Horsley PC: C. Goff						
Structure ID: 308 (454+25 LT)													
P1		BX2460-08BAVF		BOX BASE 8inW, 8inF, Variable Ht F/n									
P4) 15" x 59" - P.I.P. - BY OTHERS - 8" P3) 15" x 59" - FIELD ADJUSTMENT - 3" P2) 24" x 60" - BX FLAT LID 8inW, w/15"x59" HOLE (KYTC DBI-13S) F/F - 8" P1) 24" x 60" - BOX BASE 8inW, 8inF, Variable Ht F/n - 23" 1) CASTING - HOE KY-230-G F/G (GRADE) 1) 24" x 60" - Conseal CS-102 1.00" 1) Hole - 20 2) Hole - 4						0 lb 0 lb 1461 lb 4901 lb 237 lb 0 lb 0 lb 0 lb ----- Structure Total: 6599 lb		Structure Notes: **KYTC STATE PROJECT** 1. KYTC DBI TYPE 13S / ASTM C-913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-230S F/G SHIPPED LOOSE). 4. STUB #5 BARS 4" OUT TOP OF TOP SLAB (SPA AT 12" C/C) AROUND 15"x59" HOLE. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DBL MAT). - WALLS (As .31) #5 BARS AT 12" C.C.E.W.. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 525.65'		Rim to Invert: 3.51'		Slack: 0.12"		Sump: 0"		Step Position:					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1	522.14'	270°	38"	15" HDPE	17.6"	Hole 20	20"	20"	-1.3"	0"			
Invert 2	523.31'	90°	38"	4" WEEP HOLE	4"	Hole 4	4"	4"	14.04"	0"			
Invert 3	523.31'	270°	56"	4" WEEP HOLE	4"	Hole 4	4"	4"	14.04"	18"			
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													


RIGHT-SIDE UP VIEW (int. dimensions)

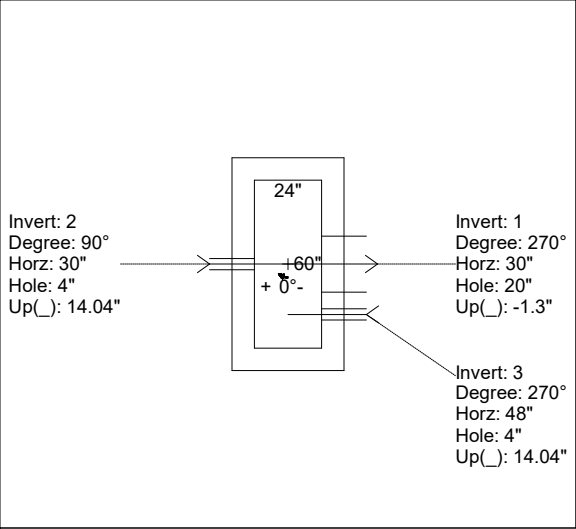

UPSIDE-DOWN VIEW (int. dimensions)


2-Stage Pour Required

First pour drawing
First pour weight = 2,040 LBS
Second pour weight = 2,861 LBS

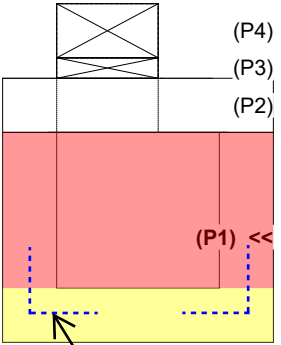

#5 L Bar cast in for wall attachment

INSIDE WALL DIMENSIONS

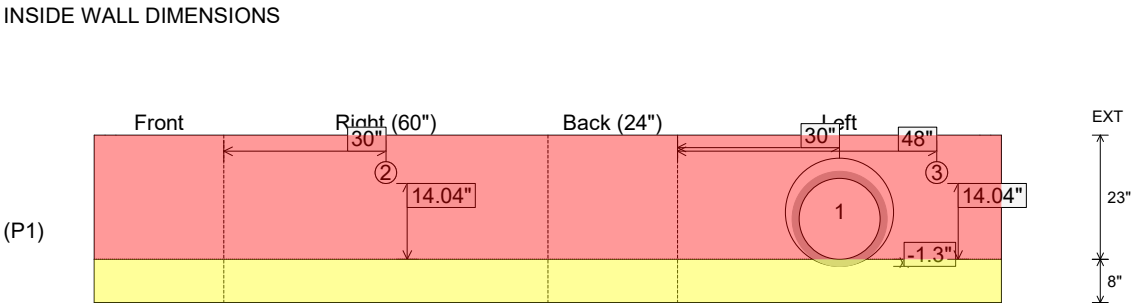

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 23" Height (Ext): 31"	Weight (Net): 4901 lb Volume (Net): 1.25cu.yd
----------------------------------	-------------------------------	--	--	--

Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC					Plant: Beaver Dam 8/3/2026 4:22:41 PM		Tech: J. Horsley PC: C. Goff				
Structure ID: 308 (454+25 LT)											
P1		BX2460-08BAVF		BOX BASE 8inW, 8inF, Variable Ht F/n							
P4) 15" x 59" - P.I.P. - BY OTHERS - 8" P3) 15" x 59" - FIELD ADJUSTMENT - 3" P2) 24" x 60" - BX FLAT LID 8inW, w/15"x59" HOLE (KYTC DBI-13S) F/F - 8" P1) 24" x 60" - BOX BASE 8inW, 8inF, Variable Ht F/n - 23" 1) CASTING - HOE KY-230-G F/G (GRADE) 1) 24" x 60" - Conseal CS-102 1.00" 1) Hole - 20 2) Hole - 4						0 lb 0 lb 1461 lb 4901 lb 237 lb 0 lb 0 lb 0 lb ----- Structure Total: 6599 lb		Structure Notes: **KYTC STATE PROJECT** 1. KYTC DBI TYPE 13S / ASTM C-913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-230S F/G SHIPPED LOOSE). 4. STUB #5 BARS 4" OUT TOP OF TOP SLAB (SPA AT 12" C/C) AROUND 15"x59" HOLE. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DBL MAT). - WALLS (As .31) #5 BARS AT 12" C.C.E.W.. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 525.65'		Rim to Invert: 3.51'		Slack: 0.12"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	522.14'	270°	38"	15" HDPE	17.6"	Hole 20	20"	20"	-1.3"	0"	
Invert 2	523.31'	90°	38"	4" WEEP HOLE	4"	Hole 4	4"	4"	14.04"	0"	
Invert 3	523.31'	270°	56"	4" WEEP HOLE	4"	Hole 4	4"	4"	14.04"	18"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

2-Stage Pour Required

Second pour drawing

First pour weight = 2,040 LBS

Second pour weight = 2,861 LBS

INSIDE WALL DIMENSIONS

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 23"
Height (Ext): 31"

Weight (Net): 4901 lb
Volume (Net): 1.25cu.yd
