


PRINT IN COLOR FOR ADDITIONAL CLARITY

#5 BAR DIAGONALS
TOP & BOTTOM
(8 EA. @ 24" &
8 EA. @ 34")

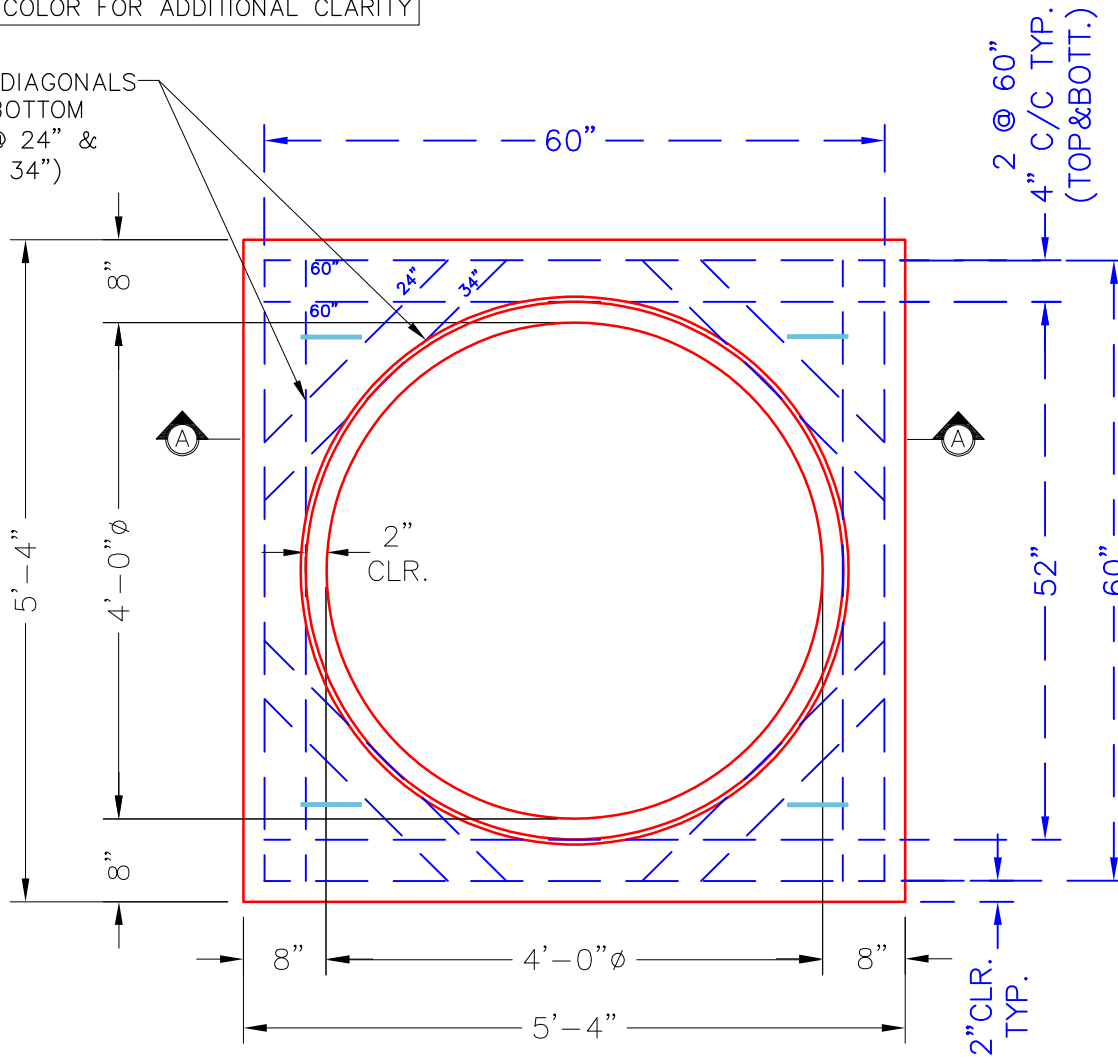

PLAN VIEW

4 EA. CONAC .8 TON $8\frac{1}{16}$ "
(6MM) WIRE ROPE ANCHORS
REQUIRED—MINIMUM.

48"Ø OPENING WITH TONGUE
FOR 48"Ø COMPONENTS.

#5 BAR @ 4"
C/C TYPICAL.
(TOP & BOTTOM)

SECTION A-A

NOTES:

- CONCRETE: 4500 PSI @ 28 DAYS.
- REINFORCING: #5 BAR @ 4" C/C-GRADE 60.
(TOP & BOTTOM LAYERS).
- KYTC CERTIFICATIONS REQUIRED.
- 4 EA. CONAC WIRE LOOP LIFTERS REQUIRED.

KYTC STATE PROJECT

#5 BAR CUT LIST
16 EA. @ 60" LG.
8 EA. @ 34" LG.
8 EA. @ 24" LG.

PRODUCTION WORK ORDER

PRODUCT I.D.:
BX4848_08TS8

DESCRIPTION:
CB TRANSITION SLAB 48"X48" TO 48"Ø



QUALITY CONTROL CHECKLIST

- ☐ ALL DIMENSIONS CORRECT.
- ☐ LIFTERS INSTALLED.
- ☐ OPENING CENTERED.
- ☐ REINFORCING CORRECT.
- ☐ SURFACE QUALITY ACCEPTABLE.
- ☐ EDGES CHAMFERED.
- ☐ ALL PATCHWORK ACCEPTABLE.

PRODUCT VIEW: RIGHT SIDE UP

PLANT: BEAVER DAM, KY.

WEIGHT: 1,535 LBS.

TOP SECTION JOINT: TONGUE

BASE SECTION JOINT: FLAT

QC CHECK INITIALS:

CUSTOMER: SCOTTY'S CONTRACTING & STONE LLC

PROJECT: KYTC CHRISTIAN CO. CALL 100 (ID 241018)

STRUCTURE ID.: MH277 (439+85 RT) (SEC. P2)

QUOTE/ORDER NO: 24-4208

PC: C. GOFF

DRAWING: S. FELLETER

DATE: 07/30/26

SCALE: NTS

PG. 1 of 1
