

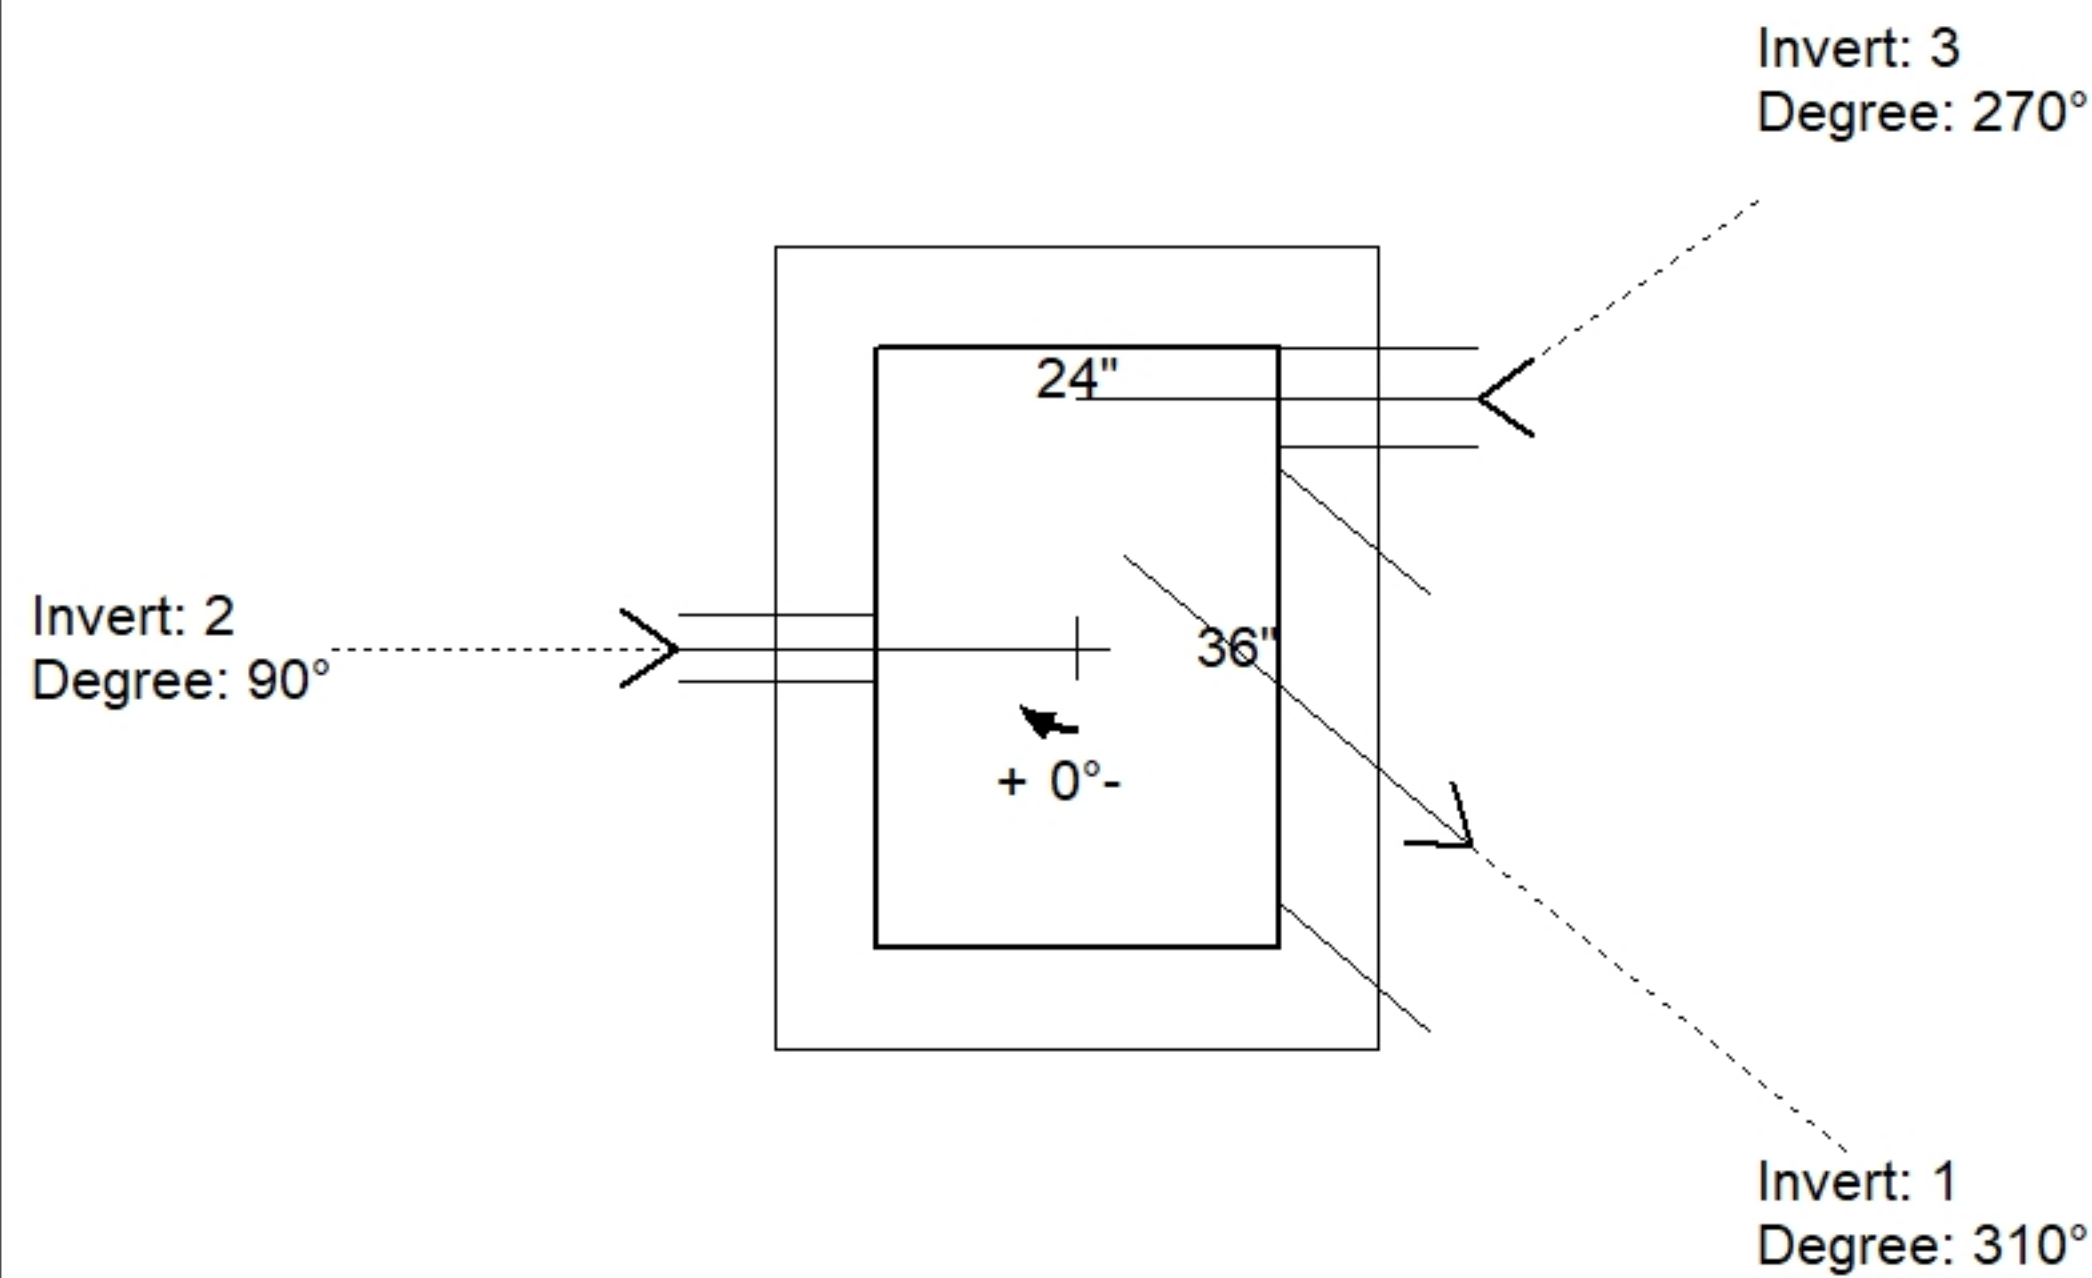
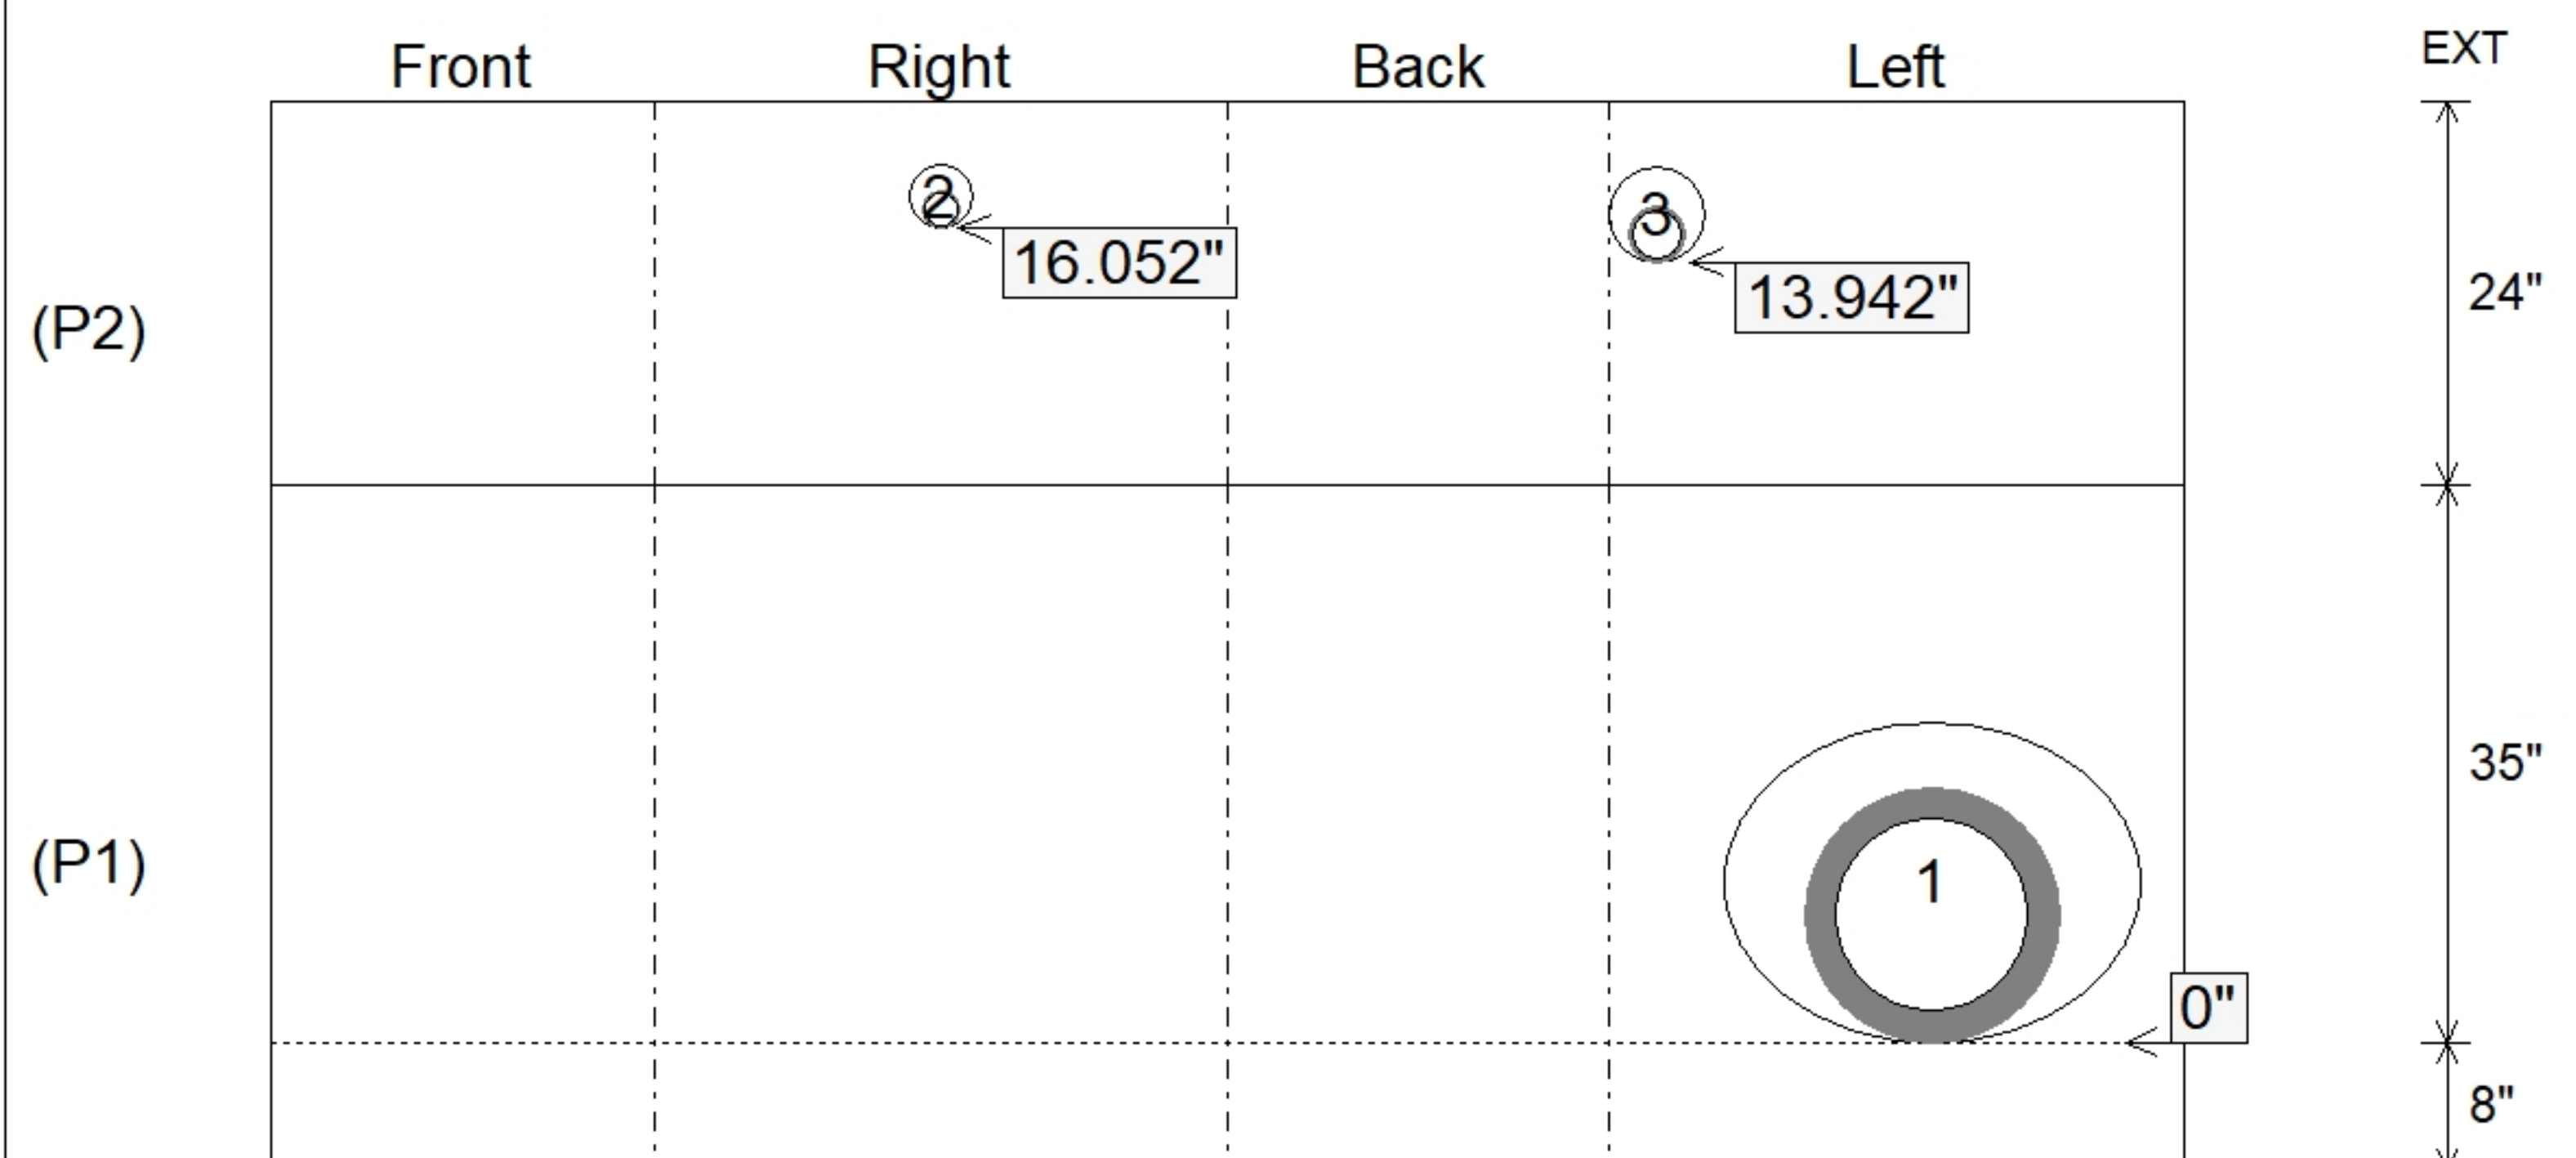


STRUCTURE SUMMARY:	
P3) 24" x 36" - CASTING HEIGHT - 8"	0 lb
P2) 24" x 36" - BOX RISER 6inW, Variable Ht - 24"	1759 lb
P1) 24" x 36" - BOX BASE 6inW, 8inF, Variable Ht - 35"	3491 lb
2) 24" x 36" - SGL 1"x14.5' Butyl	0 lb
1) Hole - 20	0 lb
1) Hole - 4	0 lb
1) Hole - 6	0 lb

Structure Total:	5250 lb



Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	376.5'							
Reducer								
Invert 1	370.8'	310°	12" RCP B WALL	16"	20"	Hole 20	0"	P1
Invert 2	374.9'	90°	2" HDPE DR17	2.375"	4"	Hole 4	16.052"	P2
Invert 3	374.73'	270°	3" HDPE DR17	3.5"	6"	Hole 6	13.942"	P2
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

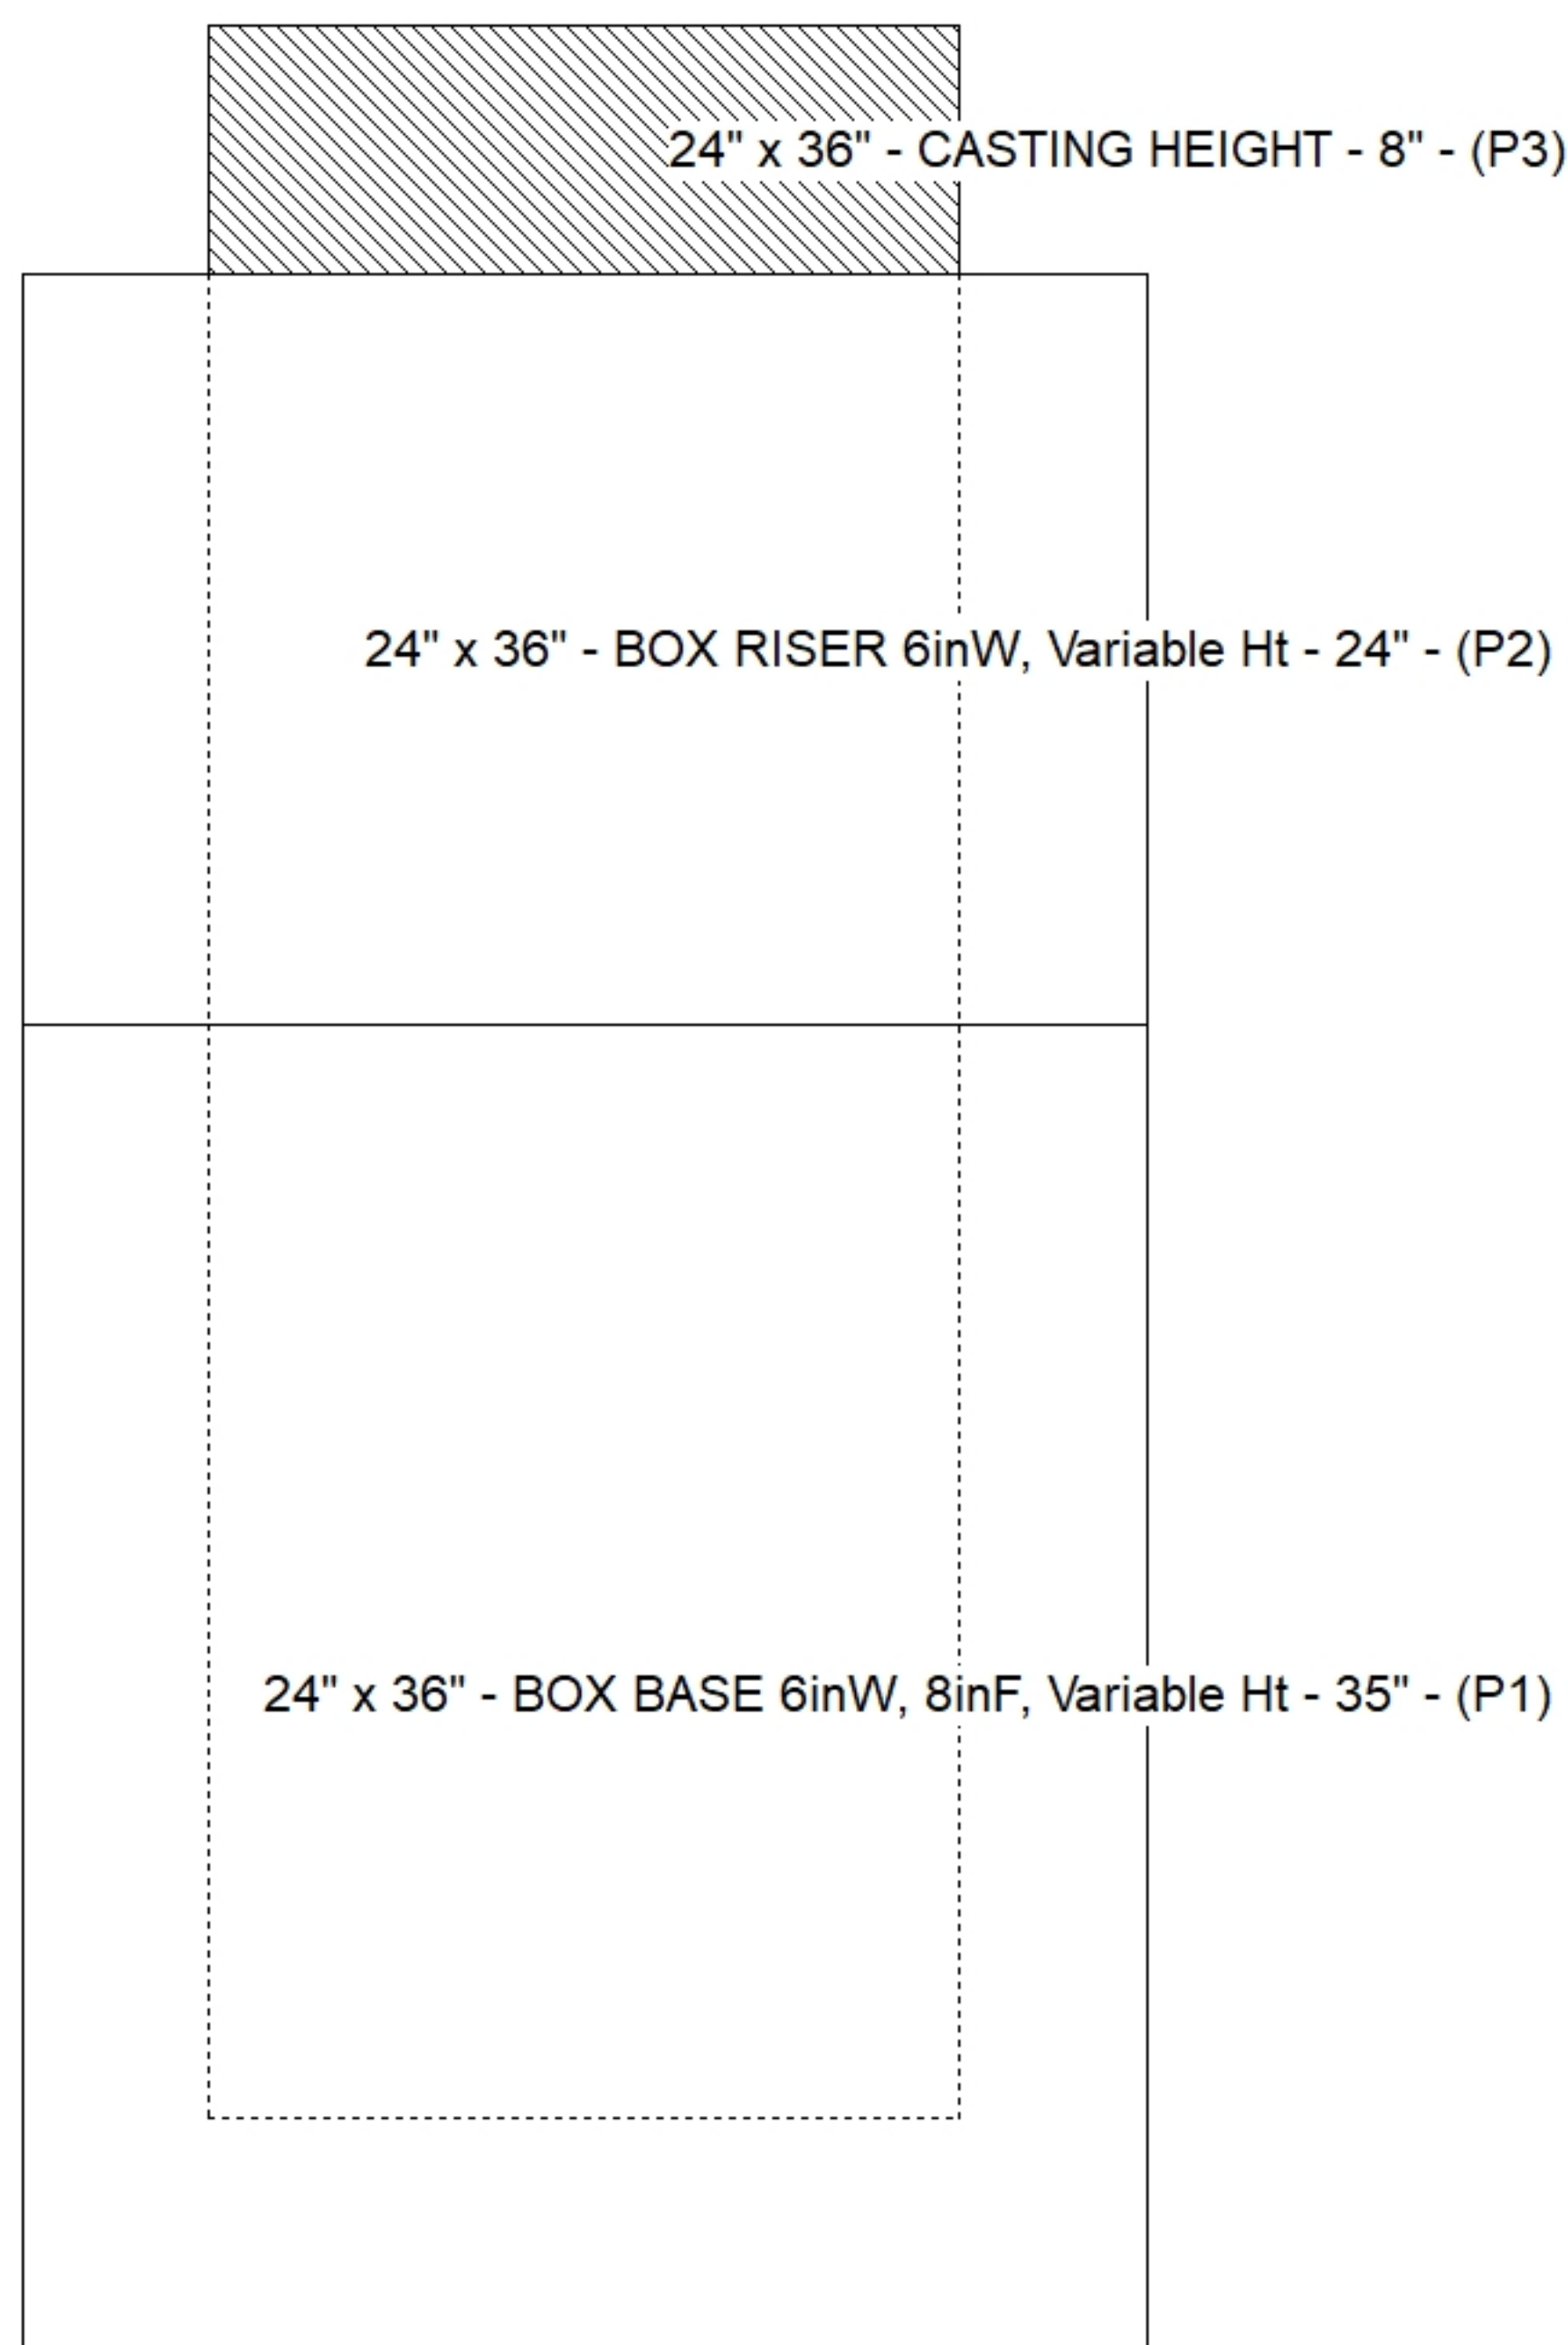

SUBMITTAL
APPROVED BY:
