

Job Name: 25-0199 - Countryview Stormwater Imp. Ph. 3 Sec. 1
Job Location: Henderson, KY 42420
Contractor: Koberstein Contracting, Inc.

PC: E. Bradley
 TECH: K. Cardwell
 Plant: Beaver Dam, KY



Structure ID: **102A**
 Spec: Storm
 Type: BX 8inW, 8inF
 Size: 24" x 24"

Rim: 374'
 Invert: 371'
 Rim to Invert: 3'

Sump: 0"
 Floor (Top): 371'
 Floor Height: 8"

Floor (Bot): 370.333'
 Overall Height: 3.5'
 Slack: 2"


Structure Notes:
 STATION: 1+59 LN AA
 1. PER ASTM C-913 SPECS
 2. CONCRETE: 4,000 PSI AT 28 DAYS
 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60)
 4. 4" CASTING SUPPLIED BY OTHERS

STRUCTURE SUMMARY:


P2) 24" x 24" - CASTING HEIGHT - 4"
 P1) 24" x 24" - BOX BASE 8inW, 8inF F/n - 30"
 1) 24" x 24" - Conseal CS-102 1.00"
 2) Hole - 20

0 lb
 3223 lb
 0 lb
 0 lb


 Structure Total: 3223 lb

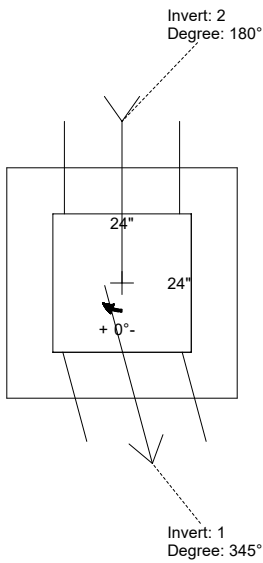

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	374'							
Reducer								
Invert 1	371'	345°	15" ADS N-12	18"	20"	Hole 20	-1.5"	P1
Invert 2	371'	180°	15" ADS N-12	18"	20"	Hole 20	-1.5"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

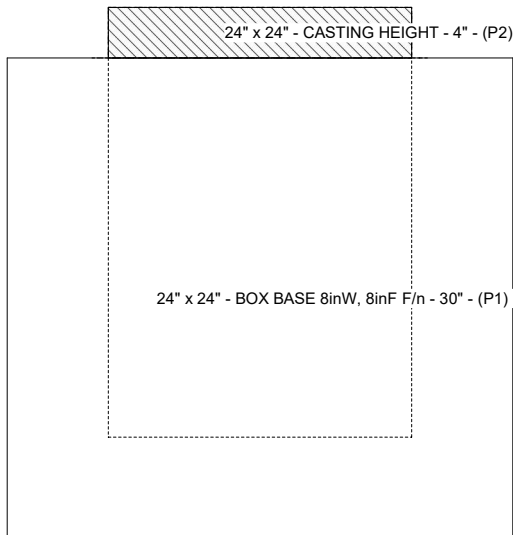

Cast (Int. Dim.) - Interior Dimensions

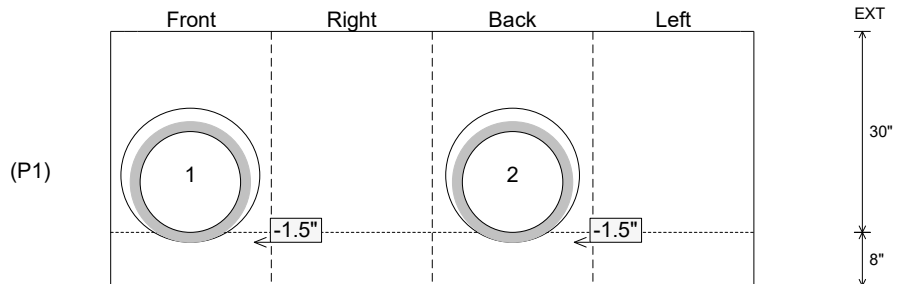

Submittal Drawing
 10/20/2025 12:20:37 PM

SUBMITTAL
 APPROVED BY:
