


4 EA. CONAC 5CA14 ANCHORS  
CAST IN AS SHOWN.


24" TYP.

18"  
P.P.

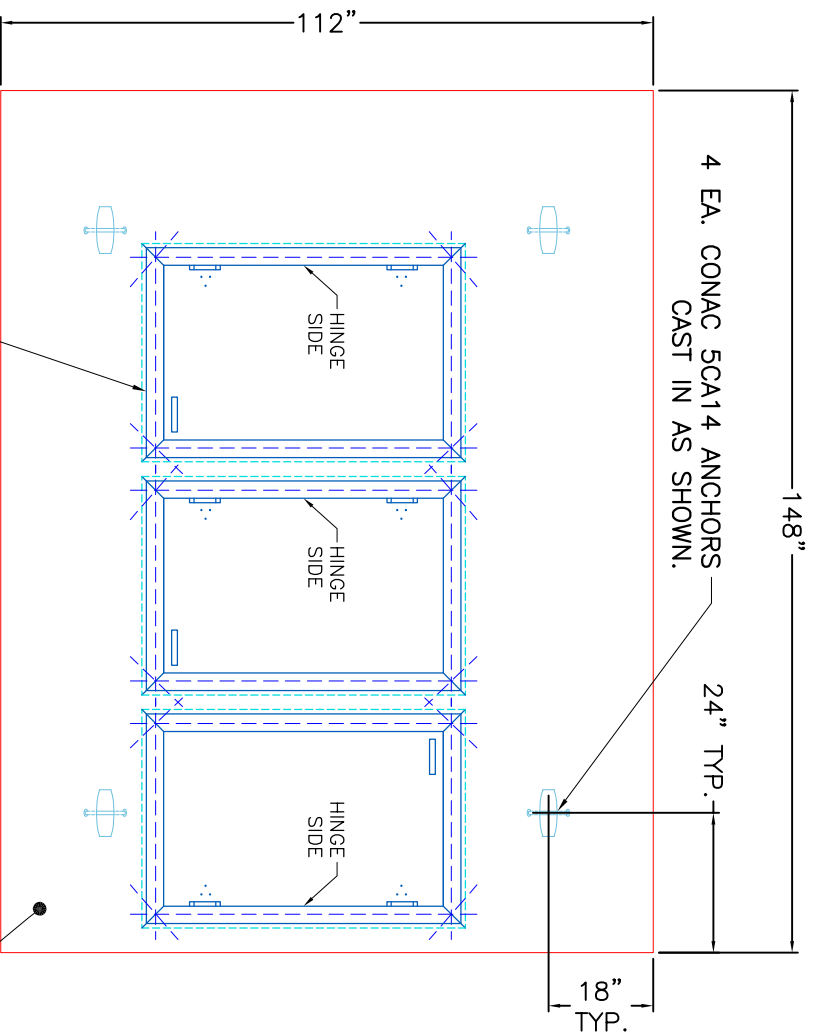


3X HALLIDAY W1S  
30" X 48" HATCHES  
PROVIDED BY ICAST

**TOP VIEW**



**FRONT VIEW**



**RIGHT VIEW**

**GENERAL NOTES:**

1. MANUFACTURED TO ASTM C-913 (LATEST REVISION).
2. CONCRETE: 5,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 8" E.W. O.C. (GRADE 60). PER ASTM A615 (GRADE 60)
4. WEIGHT: 8,227 LBS
5. 3X HALLIDAY 30" X 48" W1S HATCHES BY ICAST.
6. HATCHES TO BE CAST IN TOP SLAB.

**PRODUCTION WORK ORDER**



- QUALITY CONTROL CHECKLIST
- ALL DIMENSIONS CORRECT.
  - LIFTERS INSTALLED.
  - HATCHES CORRECT LOCATION.
  - REINFORCING CORRECT.
  - SURFACE QUALITY ACCEPTABLE.
  - EDGES CHAMFERED.
  - ALL PATCHWORK ACCEPTABLE.

|                                |  |
|--------------------------------|--|
| PRODUCT I.D.: BX096132-08LD08S | DESCRIPTION: 112" X 148" X 8" THICK TOP SLAB |
| PRODUCT VIEW: RIGHT SIDE UP    | CUSTOMER: W&O CONSTRUCTION                   |
| PLANT: BEAVER DAM, KY.         | PROJECT: THOMPSON'S STATION WWTP (PH. 2)     |
| WEIGHT: 8,227 LBS.             | STRUCTURE: VALVE VAULT                       |
| TOP SECTION JOINT: N/A         | ORDER NO: 25-1026                            |
| BASE SECTION JOINT: N/A        | PE: J.H. ROSS                                |
| QC CHECK INITIALS:             | DATE: 10/20/25                               |
|                                | DRAWING: J. COPPAGE                          |
|                                | SCALE: NTS                                   |
|                                | PG. 1 of 1                                   |

THIS DRAWING IS THE PROPERTY OF INFRASTRUCTURE PRECAST, INC. ANY USE OR DUPLICATION OF THIS DRAWING WITHOUT PRIOR AUTHORIZATION IS STRICTLY PROHIBITED.
