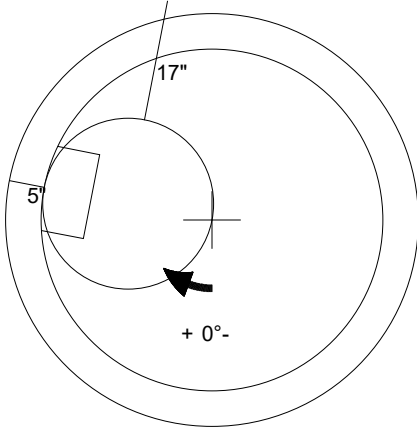



Job Name: 25-1026B Thompson's Station WWTP (Ph. 2)		Plant: Beaver Dam	Tech: J. Horsley		
Job Location: Thompson's Station Contractor: W&O Construction		10/5/2026 1:32:31 PM	PC: A. Chambers		
Structure ID: MH B2 SS-MH					
P4 MH048CN36X		ECC XYPEX CONE w/ 24" HOLE			
P5) 24" - CASTING HEIGHT - 7" P4) 48" - ECC XYPEX CONE w/ 24" HOLE - 36" P3) 48" - MH RISER w/XYPEX - 72" P2) 48" - MH RISER w/XYPEX - 72" P1) 48" - MH BASE w/XYPEX - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) CASTING - JBS 1150 F/C SANITARY 3) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 24L DD 1) PSX - 22M DD 17) MH Step ML-10-TDS-NCR - 10"		0 lb 2251 lb 5030 lb 5030 lb 3064 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 8 lb 8 lb 0 lb ----- Structure Total: 17081 lb	Structure Notes: 1. JBS-1150 SANITARY PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
					
					
Coating (Int): Coating (Ext):		Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 2251 lb Volume (Net): 0.57cu.yd
