


Contractor: W&O Construction

Plant: Beaver Dam




Slack: 0.4"

Structure Total: 17359 lb

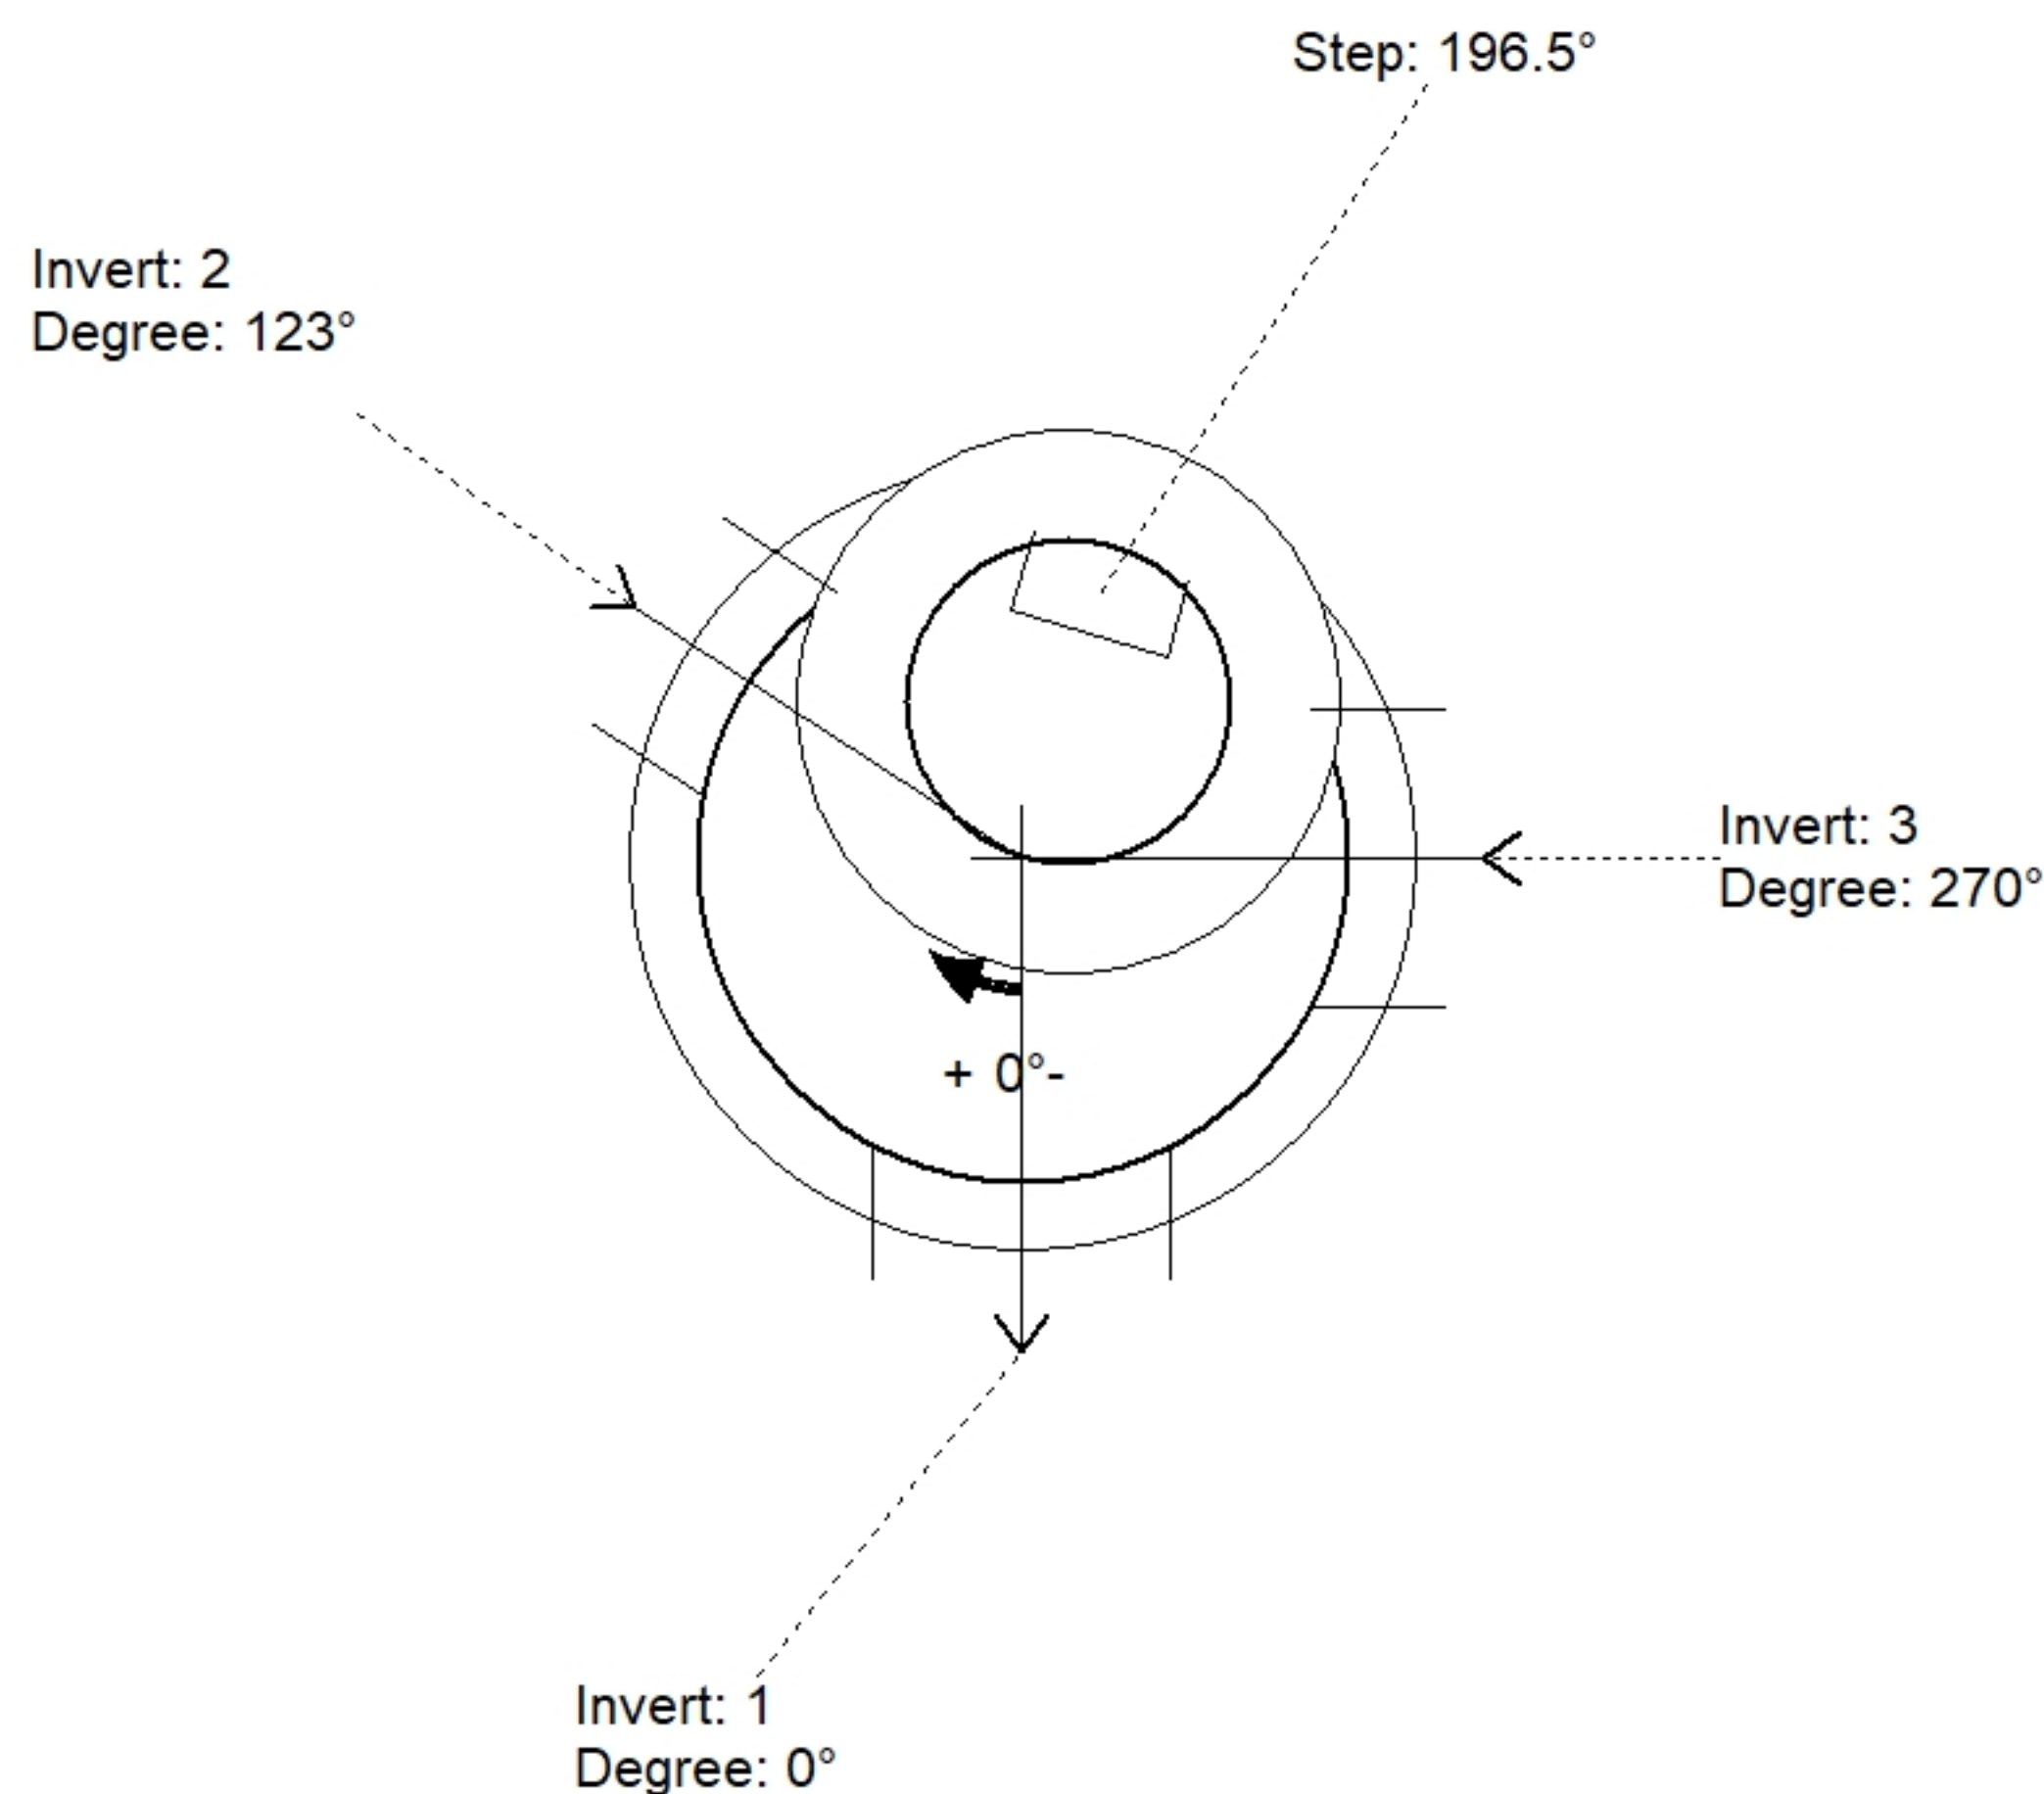

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	738'							
Reducer								
Invert 1	719.8'	0°	18" DI	19.5"	22"	Kor-N-Seal2 S206-22L	0"	P1
Invert 2	720.6'	123°	15" PVC SDR35	15.3"	18"	Kor-N-Seal2 S206-18L	10.1"	P1
Invert 3	719.9'	270°	18" DI	19.5"	22"	Kor-N-Seal2 S206-22L	1.2"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

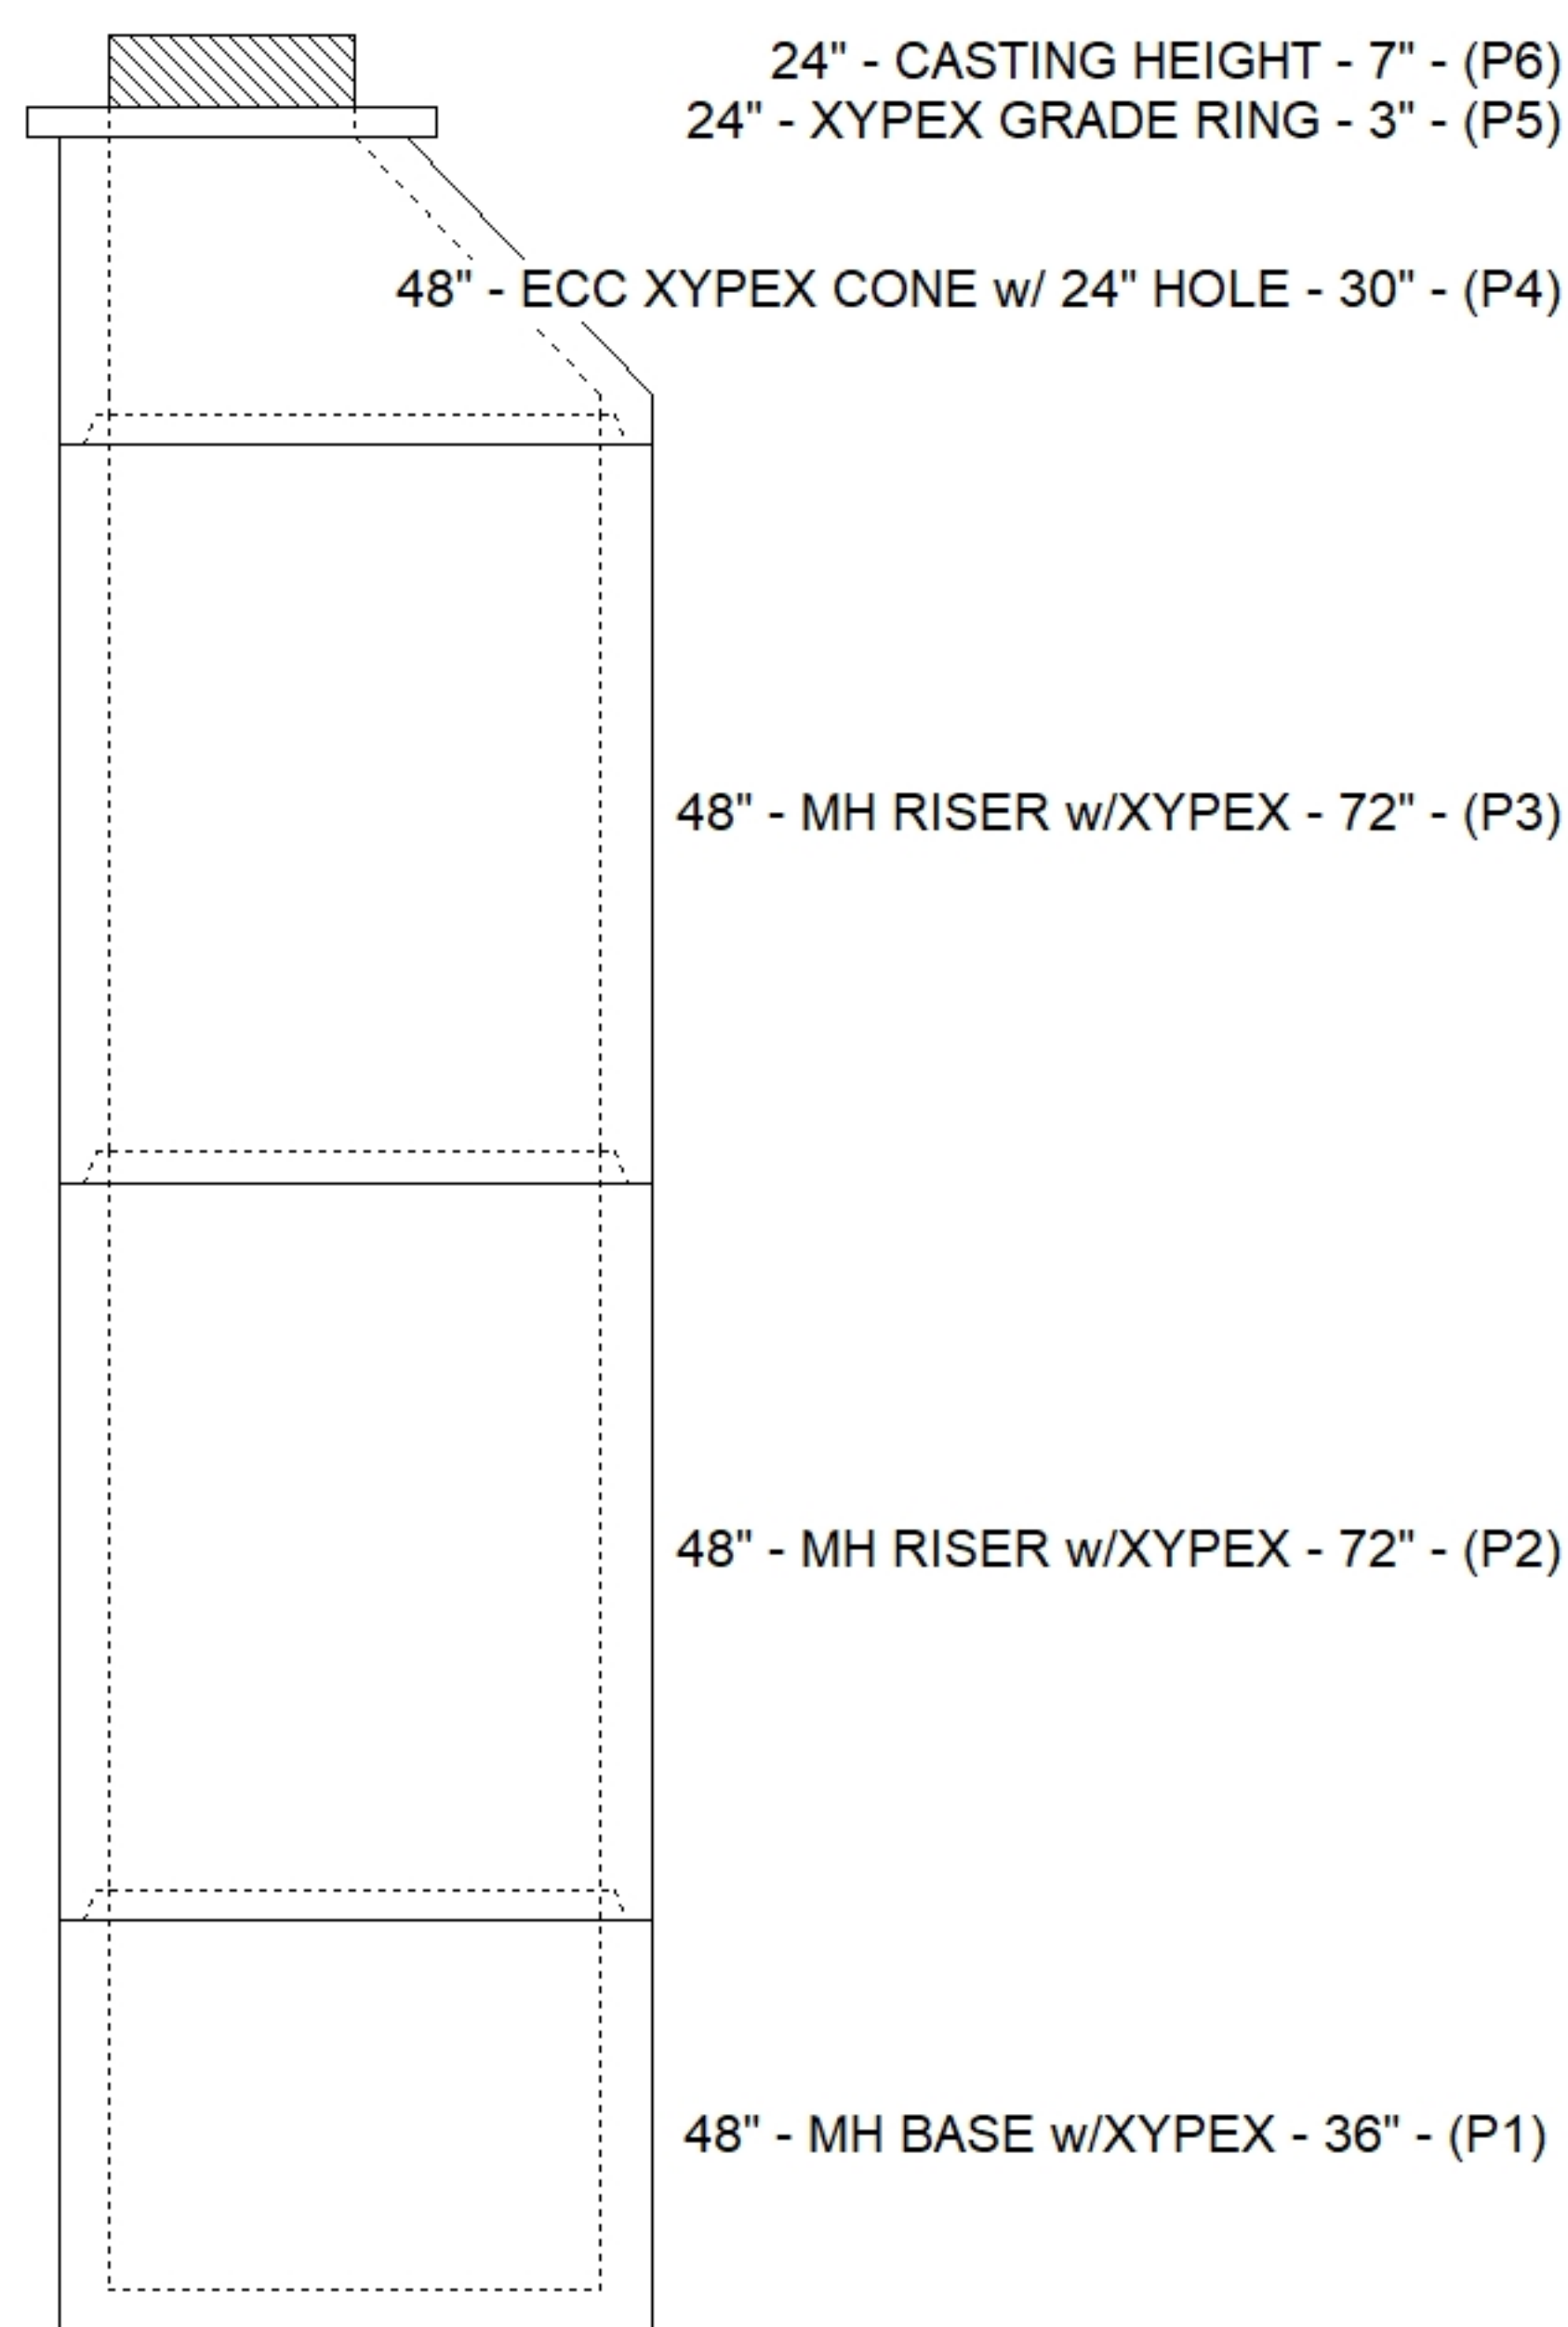

SUBMITTAL
APPROVED BY:
