

Job Name: 25-1137B - East Bank Regional Pump Station  
 Job Location: Nashville, TN  
 Contractor: Garney Companies, Inc.

Plant: Beaver Dam

Tech: J. Coppage

3/3/2026 11:46:50 AM

PC: J. Jarvis



**Structure ID: MH-004 6+34**

**P5 MH048RS36X**

**MH RISER w/XYPEX**

- P8) 24" - CASTING HEIGHT - 7"
- P7) 24" - XYPEX GRADE RING - 6"
- P6) 48" - CON XYPEX CONE w/24" HOLE - 36"
- P5) 48" - MH RISER w/XYPEX - 36"
- P4) 48" - MH RISER w/XYPEX - 72"
- P3) 96" - MH Transition Slab 48" Hole w/ Xypex - 17"
- P2) 96" - MH RISER w/XYPEX - 96"
- P1) 96" - MH BASE SLAB w/XYPEX - 8"
- 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
- 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
- 1) CASTING - JBS 1150 F/C SANITARY
- 2) 96" - Conseal CS-102 1.00" (Double)
- 3) 48" - Conseal CS-102 1.00" (Double)
- 1) Kor-N-Seal2 - S206-54L
- 1) Kor-N-Seal2 - S206-30



- Structure Notes:**
1. JBS-1150 METRO SANITARY BY ICAST.
  2. PER ASTM C478 SPECIFICATIONS.
  3. CONCRETE = 4,500 PSI AT 28 DAYS.
  4. REINFORCING PER ASTM A615 (GRADE 60)
    - TOP (As .62) #5 BAR AT 6" C/C E.W.
    - WALLS (As .18) WWF OR EQUIV.
    - FLOOR (As .20) #4 BAR AT 12" C/C E.W. DOUBLE MAT
- NOTE: KOR-N-SEAL BOOTS SUPPLIED BY OTHERS

0 lb  
 405 lb  
 2251 lb  
 2515 lb  
 5030 lb  
 9106 lb  
 21554 lb  
 10880 lb  
 0 lb  
 0 lb  
 250 lb  
 0 lb  
 0 lb  
 0 lb  
 6 lb  
 6 lb


Rim: 419.43' Rim to Invert: 21.46' Slack: 1.56" Sump: 14.04" Structure Step Position: 225

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (L)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

**RIGHT-SIDE UP VIEW (int. dimensions)**

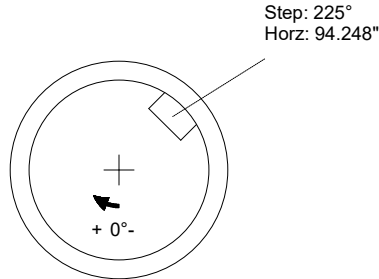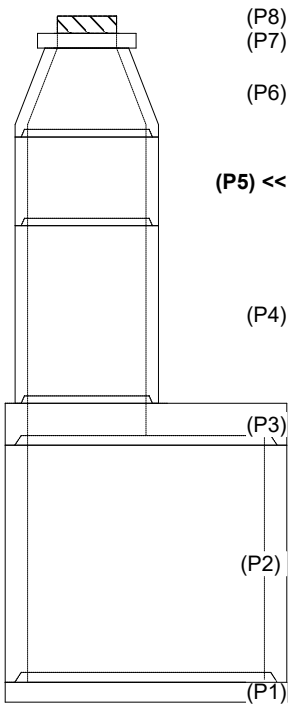

**INSIDE WALL DIMENSIONS**



Coating (Int):	Seam Up: Tongue	Wall Thickness: 5"	Height (Int): 36"	Weight (Net): 2515 lb
Coating (Ext):	Seam Dn: Groove	Floor Height: 0"	Height (Ext): 36"	Volume (Net): 0.64cu.yd
