

Job Name: 25-1137B - East Bank Regional Pump Station
 Job Location: Nashville, TN
 Contractor: Garney Companies, Inc.

Plant: Beaver Dam

3/3/2026 11:46:18 AM

Tech: J. Coppage

PC: J. Jarvis



Structure ID: MH-005 8+45



P4 MH048CCN36X-S

CON XYPEX CONE w/24" HOLE-SPECIAL

- P6) 24" - CASTING HEIGHT - 7"
- P5) 24" - XYPEX GRADE RING - 4"
- P4) 48" - CON XYPEX CONE w/24" HOLE-SPECIAL - 36"
- P3) 48" - MH RISER w/XYPEX - 48"
- P2) 48" - MH RISER w/XYPEX - 60"
- P1) 48" - MH BASE Custom Ht, w/XYPEX - 43"
- 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
- 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
- 1) 48" - SAN. INV. CHANNEL w/XYPEX - FULL HEIGHT
- 1) CASTING - JBS 1150 F/C SANITARY
- 3) 48" - Conseal CS-102 1.00" (Double)
- 2) Kor-N-Seal2 - S206-30

Structure Notes:
 1. JBS-1150 METRO SANITARY BY ICAST.
 2. PER ASTM C478 SPECIFICATIONS.
 3. CONCRETE = 4,500 PSI AT 28 DAYS.
 4. REINFORCING PER ASTM A615 (GRADE 60)
 - CONE (As .12)
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
 NOTE: KOR-N-SEAL BOOTS SUPPLIED BY OTHERS

Structure Total: 15471 lb

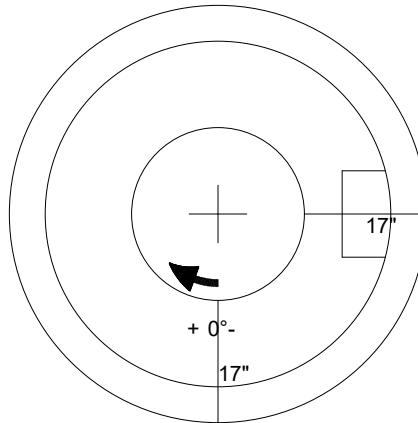

48" - CON XYPEX CONE w/24" HOLE-SPECIAL - 36" - (P4)

Coating (Int):
 Coating (Ext):

Seam Up: Flat
 Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 36"

Weight (Net): 2251 lb
 Volume (Net): 0.57cu.yd
