

Job Name: 25-1137B - East Bank Regional Pump Station  
 Job Location: Nashville, TN  
 Contractor: Garney Companies, Inc.

Plant: Beaver Dam

11/5/2025 12:06:46 PM

Tech: J. Coppage

PC: J. Jarvis





**Structure ID: MH-200 1+04**

**P5 MH048CCN36X**

**CON XYPEX CONE w/24" HOLE**

- P7) 24" - CASTING HEIGHT - 7"
- P6) 24" - XYPEX GRADE RING - 3"
- P5) 48" - CON XYPEX CONE w/24" HOLE - 36"
- P4) 48" - MH RISER w/XYPEX - 48"
- P3) 48" - MH RISER w/XYPEX - 48"
- P2) 72" - XYPEX MH FT REDUCER 48" HOLE - 15"
- P1) 72" - MH BASE w/XYPEX - 72"
- 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
- 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
- 1) 72" - SAN. INV. CHANNEL - FULL HEIGHT
- 1) 72" - DBL 1"x14.5' Butyl (2x)
- 3) 48" - DBL 1"x14.5' Butyl (2x)
- 1) A-Lok - 1240

<ul style="list-style-type: none"> <li>0 lb</li> <li>202 lb</li> <li>2251 lb</li> <li>3353 lb</li> <li>3353 lb</li> <li>3864 lb</li> <li>13620 lb</li> <li>0 lb</li> <li>0 lb</li> <li>5422 lb</li> <li>0 lb</li> <li>0 lb</li> <li>1 lb</li> </ul>	<p><u>Structure Notes:</u></p> <ol style="list-style-type: none"> <li>1. JBS-1150 METRO SANITARY BY ICAST.</li> <li>2. PER ASTM C478 SPECIFICATIONS.</li> <li>3. CONCRETE = 4,500 PSI AT 28 DAYS.</li> <li>4. REINFORCING PER ASTM A615 (GRADE 60)</li> </ol> <ul style="list-style-type: none"> <li>- TOP (As .62) #5 BAR AT 6" C/C E.W.</li> <li>- WALLS (As .18) WWF OR EQUIV.</li> <li>- FLOOR (As .20) #4 BAR AT 12" C/C E.W. DOUBLE MAT</li> </ul>
<p>Structure Total: 32068 lb</p>	

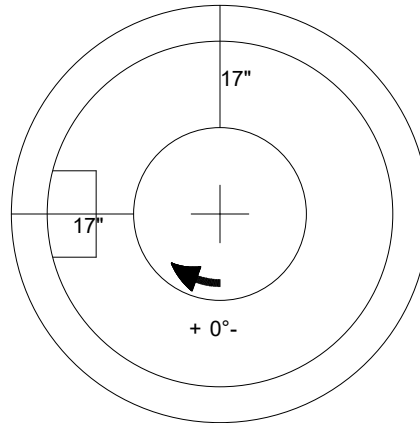

48" - CON XYPEX CONE w/24" HOLE - 36" - (P5)

Coating (Int):  
 Coating (Ext):

Seam Up: Flat  
 Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 36"

Weight (Net): 2251 lb  
 Volume (Net): 0.57cu.yd
