

Job Name: 25-1145B - 7959 Poplar Creek
Job Location: Nashville, TN 37221
Contractor: Elite Constructors, Inc.

Plant: Beaver Dam, KY
7/22/2026 12:17:28 PM

Tech: J. Horsley
PC: A. Chambers



Structure ID: SAN-A2



P3 MH048CCN24CDARED

CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G

- P5) 24" - CASTING HEIGHT - 7"
P4) 24" - GRADE RING w/ConBlock-CDA Red F/F - 4"
P3) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 24"
P2) 48" - MH RISER w/DROP/ConBlock-CDA Red T/G - 48"
P1) 48" - MH BASE w/DROP/ConBlock-CDA Red T/n - 24"
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
1) CASTING - JBS 1150 F/C SANITARY
2) 48" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
1) PSX - 12-08 NYLO
1) Drop Elbow - 8" PVC
1) Drop Tee - 8" PVC
8) MH Step ML-10-TDS-NCR - 10"

- 0 lb
270 lb
1297 lb
3329 lb
2935 lb
0 lb
0 lb
1440 lb
250 lb
0 lb
0 lb
8 lb
0 lb
0 lb
0 lb
- Structure Notes: .
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. ADMIXTURE = CONBLOCK CDA RED.
4. CASTING BY ICAST (JBS 1150 F/C "SAN")
5. EXTERIOR ROP ASSEMBLY AT 203° BY ICAST.
.
REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 9529 lb

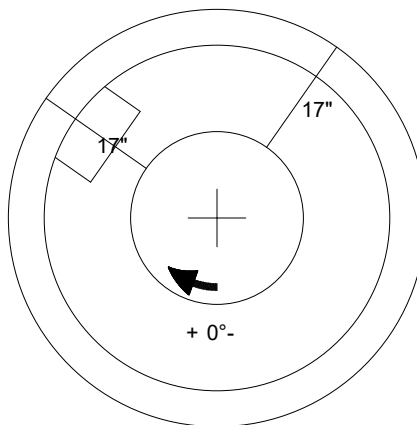

48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 24" - (P3)

Coating (Int):	Seam Up: Flat	Wall Thickness: 5"	Height (Ext): 24"	Weight (Net): 1297 lb
Coating (Ext):	Seam Dn: Groove			Volume (Net): 0.33cu.yd
