

Job Name: 25-1172 - Midland Farms Job Location: Somerset, KY 45203 Contractor: Weddle Enterprises, Inc	Plant: 100 12/16/2025 1:26:47 PM	Tech: J. Horsley - F PC: C. Goff	
--	-------------------------------------	-------------------------------------	--

**Structure ID: ARV 1**

**P1 MH048DHVF**

**MH DH RISER Custom Ht T/F**


P3) 24" - CASTING HEIGHT - 7"	0 lb
P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/G - 12"	1561 lb
P1) 48" - MH DH RISER Custom Ht T/F - 29"	2026 lb
1) JOINT WRAP - 0.065"x6"x50" CONSEAL CS212	0 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) 48" - Conseal CS-102 1.00" (Double)	0 lb
1) Hole - 0	0 lb
<b>Structure Total:</b>	<b>3587 lb</b>

**Structure Notes:**  
 1. PER ASTM C-478 SPECIFICATIONS  
 2. CONCRETE: 4,000 PSI AT 28 DAYS  
 3. REINFORCEMENT: PER ASTM A615  
 4. NO STEPS  
 5. CASTING SUPPLIED BY OTHERS (7" FRAME & SOLID COVER)


Rim: 4'	Rim to Invert: 4'	Slack: 0"	Sump: 0"	Step Position:
---------	-------------------	-----------	----------	----------------

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (L)	Offset
Invert 1				NO OPENINGS						
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

**RIGHT-SIDE UP VIEW (int. dimensions)**

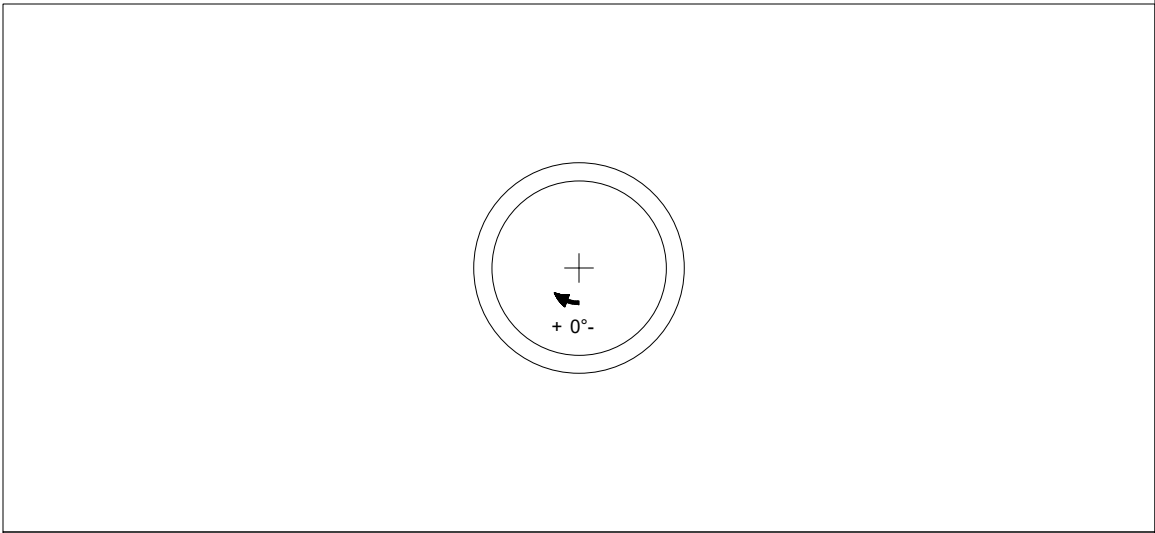

**INSIDE WALL DIMENSIONS**

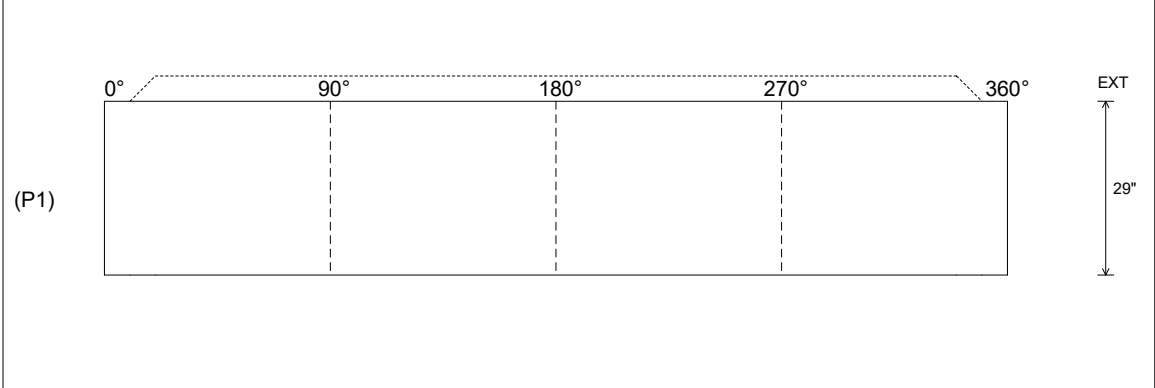

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Flat	Wall Thickness: 5" Floor Height: 0"	Height (Int): 29" Height (Ext): 29"	Weight (Net): 2026 lb Volume (Net): 0.52cu.yd
----------------------------------	----------------------------------	--	--	--
