

Job Name: 25-1385C W6 Ph.II-A Force Main Improvements
Job Location: Burlington, KY
Contractor: Lawrence Construction & Leasing, Inc.

PC: J. Jarvis
 TECH: J. Coppage
 Plant: Beaver Dam



Structure ID: **51385C 2-2**
 Spec: Sanitary
 Type: SAN.MH
 Size: 48"

Rim: 0'
 Invert: 0'
 Rim to Invert: 0'

Sump: 0"
 Floor (Top): -3"
 Floor Height: 0"

Floor (Bot): -3'
 Overall Height: 3'
 Slack: 0"

Structure Notes:


1. PER ASTM C-478 SPECS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: PER ASTM A615
4. A-LOK DURA-PLATE 100 LINER REQUIRED

STRUCTURE SUMMARY:

- P1) 48" - MH RISER Custom Ht T/G - 36"
 1) A-LOK DURA-PLATE 100 LINER - PSSPEC-EA
 1) 48" - Conseal CS-102 1.00" (Double)
 3) MH Step ML-10-TDS-NCR - 10"



2515 lb
 0 lb
 0 lb
 0 lb

Structure Total: 2515 lb



Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	0'							
Reducer								
Invert 1								
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Cast (Int. Dim.) - Interior Dimensions

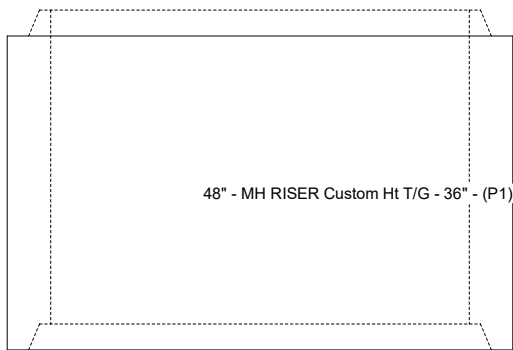

Submittal Drawing
 11/26/2025 1:01:58 PM

SUBMITTAL
 APPROVED BY:
