

Job Name: 25-1431 - Georgetown Commons
 Job Location: Georgetown, KY
 Contractor: Winwater Hartford KY Co.

Plant: Beaver Dam

4/23/2026 11:20:20 AM

Tech: J. Coppage

PC: A. Chambers



Structure ID: CBI 131

P1 BX2436-08BA60

BOX BASE 8inW, 8inF

- P4) 24" x 120" - CB INLET KY A 10' TOP LEFT - 10"
- P3) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18"
- P2) 24" x 36" - BOX RISER 8inW, Variable Ht - 37"
- P1) 24" x 36" - BOX BASE 8inW, 8inF - 60"
- 2) 24" x 36" - Conseal CS-102 1.00"
- 1) Hole - 20
- 1) Hole - 18
- 1) Hole - 6

- Structure Notes:**
1. JR HOE KY-206 PROVIDED BY ICAST.
 2. CASTING FRAME TO BE CAST INTO THE TOP PHASE.
 3. PER KYTC CBI TYPE A / ASTM C913 SPEC'S.
 4. CONCRETE = 4,000 PI AT 28 DAYS.
 5. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

3400 lb
 5270 lb
 3756 lb
 7042 lb
 0 lb
 0 lb
 0 lb
 0 lb




Structure Total: 19468 lb

Rim: 878.98' Rim to Invert: 10.23' Slack: 0.26" Sump: 2.5" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	868.75'	270°	26"	15" HDPE	17.6"	Hole 20	20"	20"	0"	0"
Invert 2	868.75'	140°	34.278"	12" HDPE	14.5"	Hole 18	18"	28.003"	-0.5"	-10"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

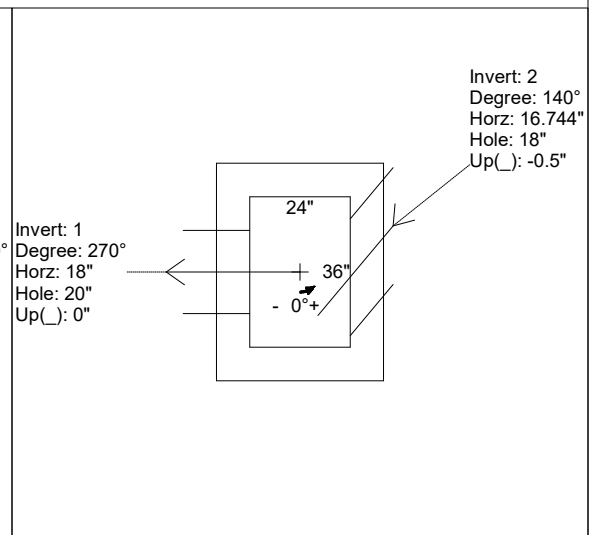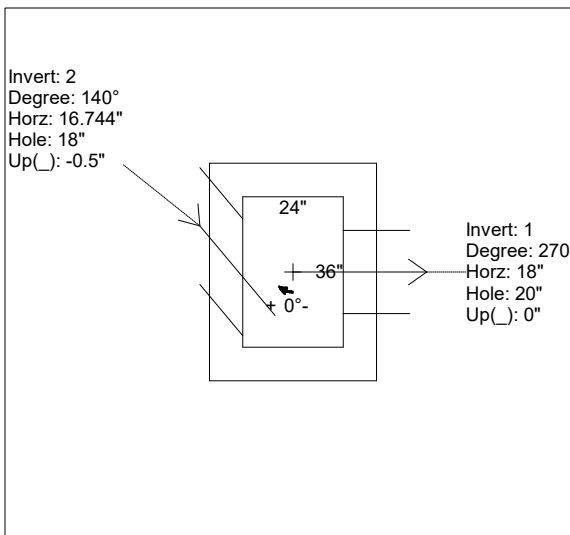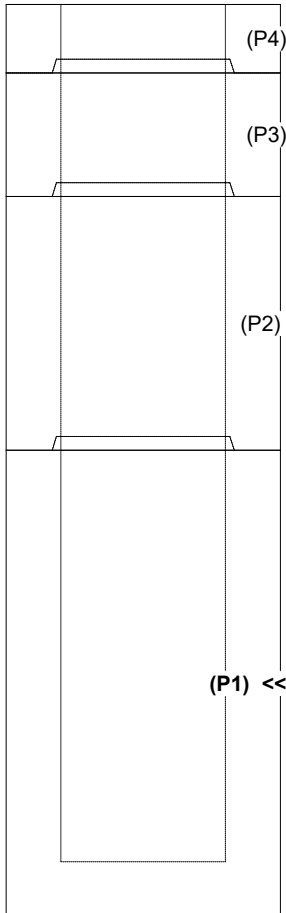

INSIDE WALL DIMENSIONS

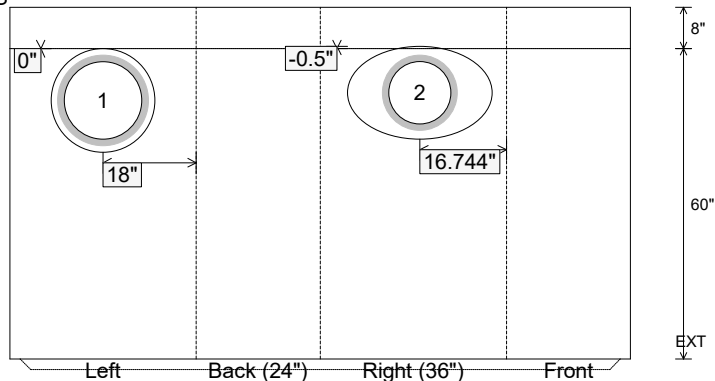

Coating (Int):
 Coating (Ext):

Seam Up: Tongue
 Seam Dn: n/a

Wall Thickness: 8"
 Floor Height: 8"

Height (Int): 60"
 Height (Ext): 68"

Weight (Net): 7042 lb
 Volume (Net): 1.8cu.yd
