

Job Name: 25-1431 - Georgetown Commons
 Job Location: Georgetown, KY
 Contractor: Winwater Hartford KY Co.

Plant: Beaver Dam

Tech: J. Coppage

4/22/2026 9:12:44 AM

PC: A. Chambers



Structure ID: CBI 240

P1 BX2436-08BA18

BOX BASE 8inW, 8inF

- P3) 24" x 60" - CB INLET KY A 5' TOP LEFT - 10"
- P2) 24" x 60" - CB INLET KY A 5' BOTTOM LEFT - 18"
- P1) 24" x 36" - BOX BASE 8inW, 8inF - 18"
- 1) 24" x 36" - Conseal CS-102 1.00"
- 1) DOGHOUSE INVRTD - 20"x18"
- 1) DOGHOUSE INVRTD - 6"x6"

1895 lb
 2670 lb
 2995 lb
 0 lb
 0 lb
 0 lb

 Structure Total: 7560 lb



- Structure Notes:**
1. JR HOE KY-206 PROVIDED BY ICAST.
 2. CASTING FRAME TO BE CAST INTO THE TOP PHASE.
 3. PER KYTC CBI TYPE A / ASTM C913 SPEC'S.
 4. CONCRETE = 4,000 PI AT 28 DAYS.
 5. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 887.17' Rim to Invert: 3.92' Slack: 2.54" Sump: 1.5" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	883.25'	270°	26"	15" HDPE	17.6"	DOGHOUSE INVRTD 20"x18"	20" x 18"	20"	0"	0"
Invert 2	884.2'	180°	20"	4" HDPE (perf pipe)	4.8"	DOGHOUSE INVRTD 6"x6"	6" x 6"	6"	11.9"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

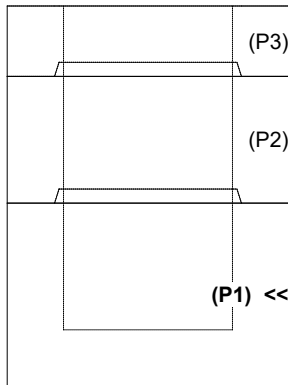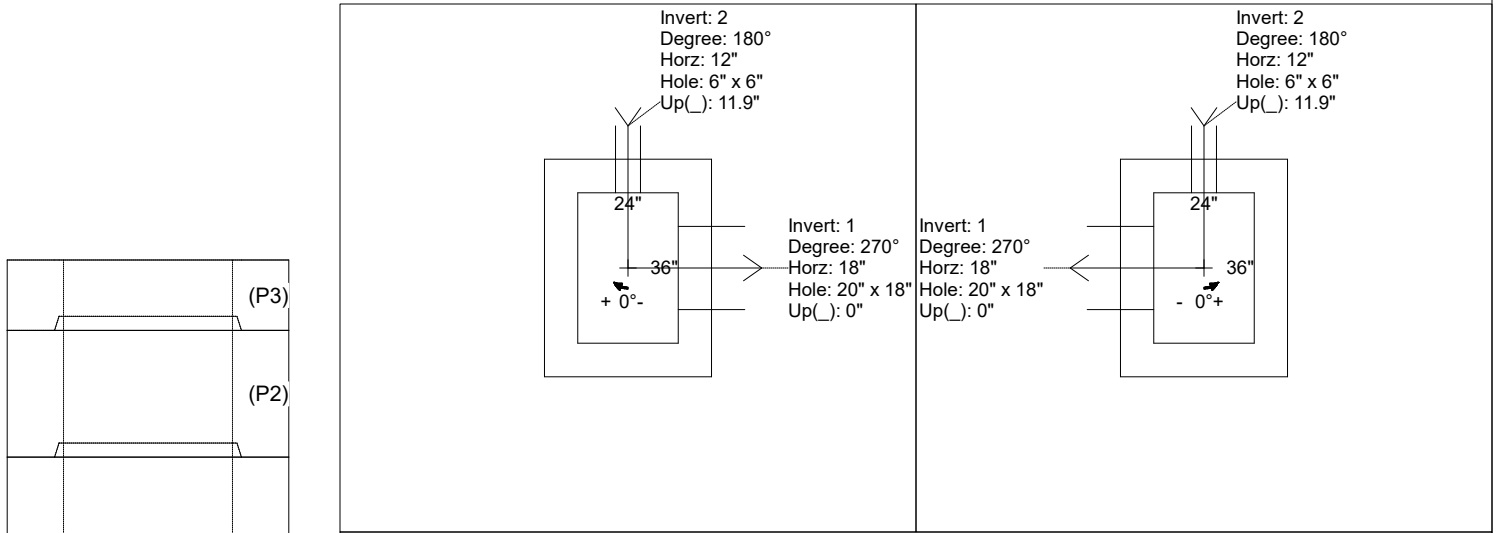

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 18" Height (Ext): 26"	Weight (Net): 2995 lb Volume (Net): 0.76cu.yd
----------------------------------	---------------------------------	--	--	--
