

Job Name: 25-1431 - Georgetown Commons
 Job Location: Georgetown, KY
 Contractor: Winwater Hartford KY Co.

Plant: Beaver Dam
 4/23/2026 11:30:43 AM

Tech: J. Coppage
 PC: A. Chambers



Structure ID: DCI 104

P2 BX4848-08LD08-S


CB FLAT TOP 8"W w/24"x36" HOLE

- P3) 24" x 36" - CASTING HEIGHT - 6"
- P2) 48" x 48" - CB FLAT TOP 8"W w/24"x36" HOLE - 8"
- P1) 48" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 50"
- 1) CASTING - HOE 470 SET (F/G/H)
- 2) Hole - 40

- Structure Notes:**
1. JR HOE HOE-470 PROVIDED BY ICAST.
 2. PER ASTM C913 SPECIFICATIONS.
 3. CONCRETE = 4,000 PSI AT 28 DAYS.
 4. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
 - RISER/WALLS (As .18)
 - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

0 lb
 2170 lb
 8581 lb
 394 lb
 0 lb

 Structure Total: 11145 lb

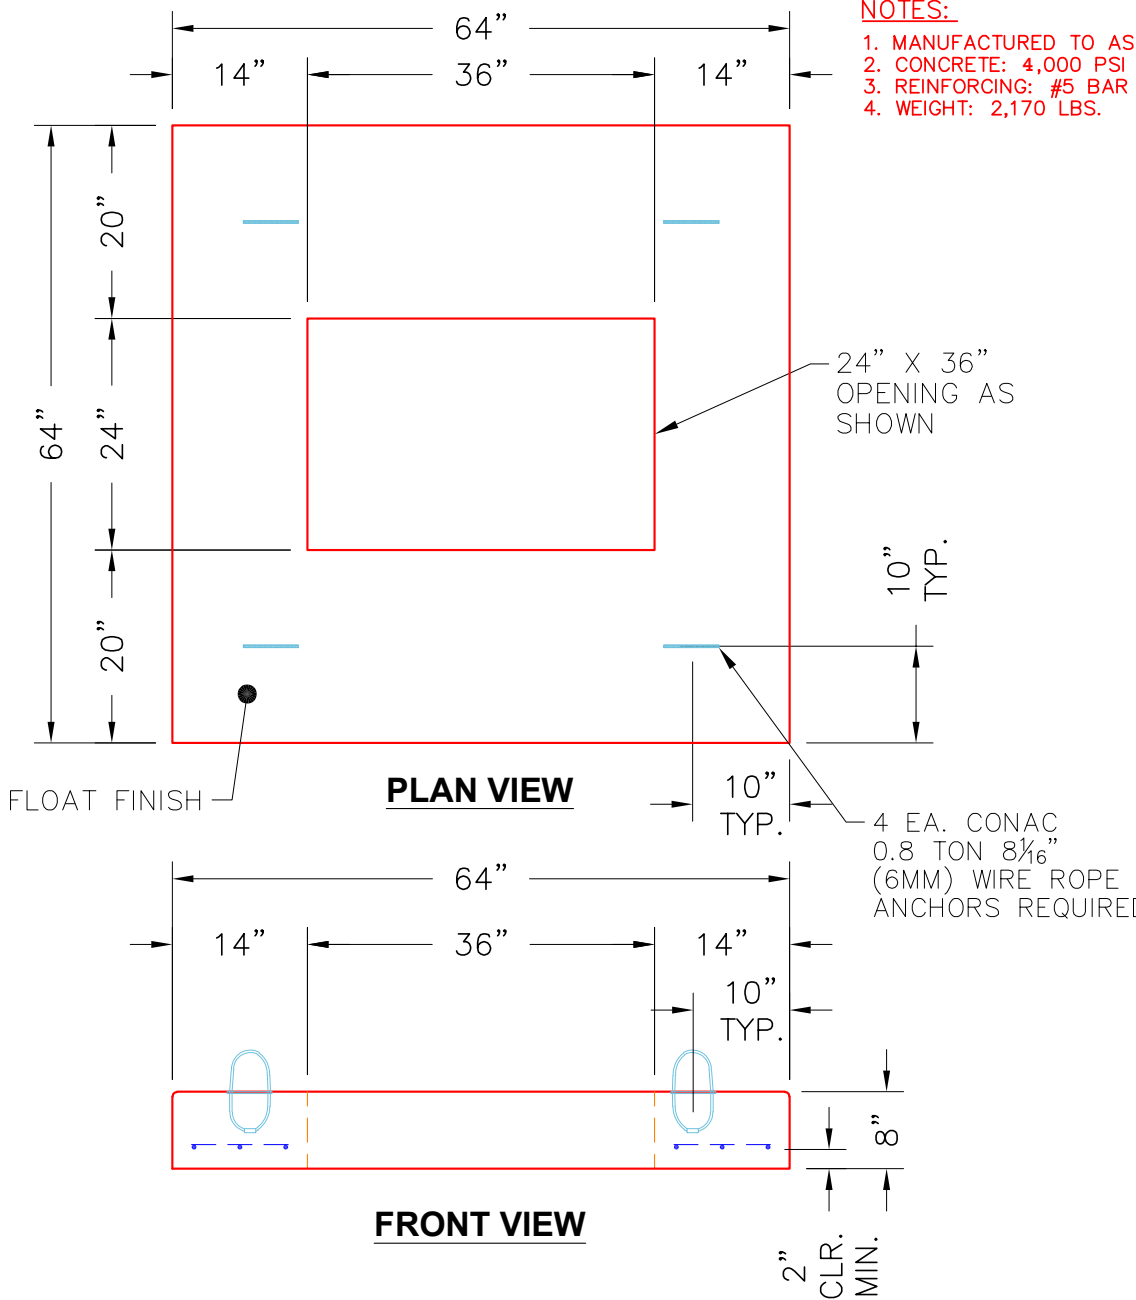

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 8"	Weight (Net): 2170 lb Volume (Net): 0.55cu.yd
----------------------------------	--------------------------------	--------------------	------------------	--
