

Job Name: 25-1431 - Georgetown Commons
 Job Location: Georgetown, KY
 Contractor: Winwater Hartford KY Co.

Plant: Beaver Dam
 4/9/2026 10:01:01 AM

Tech: J. Coppage
 PC: A. Chambers




Structure ID: DCI 143

P3 BX4848-08LD08-S

CB FLAT TOP 8"W w/24"x36" HOLE

- P4) 24" x 36" - CASTING HEIGHT - 6"
- P3) 48" x 48" - CB FLAT TOP 8"W w/24"x36" HOLE - 8"
- P2) 48" x 48" - BOX RISER 8inW - 60"
- P1) 48" x 48" - BOX BASE 8inW, 8inF - 60"
- 1) CASTING - HOE 470 SET (F/G/H)
- 2) Hole - 46
- 1) Hole - 30

| | |
|-------------------------|--|
| 0 lb | Structure Notes: |
| 2170 lb | 1. JR HOE HOE-470 PROVIDED BY ICAST. |
| 8923 lb | 2. PER ASTM C913 SPECIFICATIONS. |
| 9061 lb | 3. CONCRETE = 4,000 PSI AT 28 DAYS. |
| 394 lb | 4. REINFORCING PER ASTM A615 (GRADE 60). |
| 0 lb | - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. |
| 0 lb | - RISER/WALLS (As .37) #5 BARS AT 10" C.C.E.W. |
| 0 lb | - FLOOR (As .37) #5 BARS AT 10" C.C.E.W. |
| Structure Total: | 20547 lb |

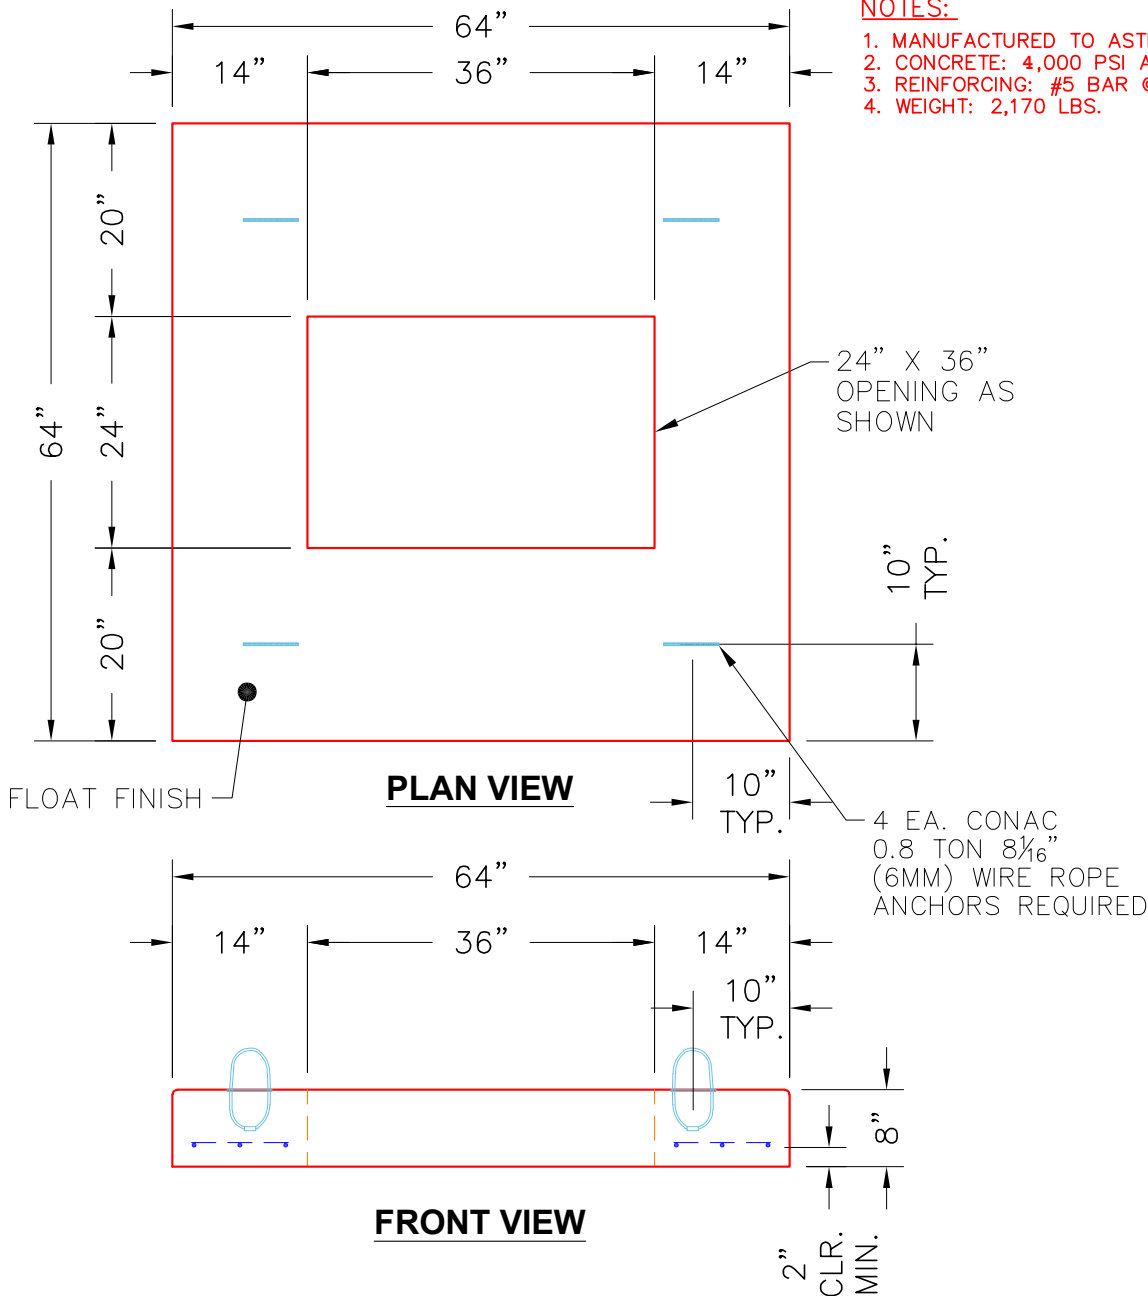

| | | | | |
|----------------------------------|--------------------------------|--------------------|------------------|--|
| Coating (Int): Coating (Ext): | Seam Up: Flat Seam Dn: Flat | Wall Thickness: 8" | Height (Ext): 8" | Weight (Net): 2170 lb Volume (Net): 0.55cu.yd |
|----------------------------------|--------------------------------|--------------------|------------------|--|
