

Job Name: 25-1431 - Georgetown Commons
 Job Location: Georgetown, KY
 Contractor: Winwater Hartford KY Co.

Plant: Beaver Dam
 4/17/2026 1:05:45 PM

Tech: J. Copping
 PC: A. Chambers




Structure ID: MH 320

P2 BX084084-12TS48

CB FT REDUCER 48" HOLE

- P5) 24" - CASTING HEIGHT - 7"
- P4) 48" - ECC CONE w/ 24" HOLE - 24"
- P3) 48" - MH RISER - 36"
- P2) 84" x 84" - CB FT REDUCER 48" HOLE - 12"
- P1) 84" x 84" - BOX BASE 8inW, 8inF, Variable Ht - 94"
- 1) SECONDARY POUR - WALLS
- 1) CASTING - HOE MC-420 F/C Storm LOU-MSD
- 1) 84" x 84" - Conseal CS-102 1.00"
- 2) 48" - Conseal CS-102 1.00"
- 1) Hole - 82
- 1) DOGHOUSE - 66"x66"
- 13) MH Step ML-10-TDS-NCR - 10"

0 lb	Structure Notes:
1550 lb	1. JR HOE MC-420 PROVIDED BY ICAST.
2515 lb	2. PER ASTM C478 SPECIFICATIONS.
8247 lb	3. CONCRETE = 4,000 PSI AT 28 DAYS.
23045 lb	4. REINFORCING PER ASTM A913 (GRADE 60).
0 lb	- TRANS SLAB - AS SHOWN BELOW
340 lb	- RISER/WALLS (As .37) #5 BARS AT 10" C.C.E.W.
0 lb	- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.
0 lb	
0 lb	
0 lb	
0 lb	
Structure Total:	35697 lb

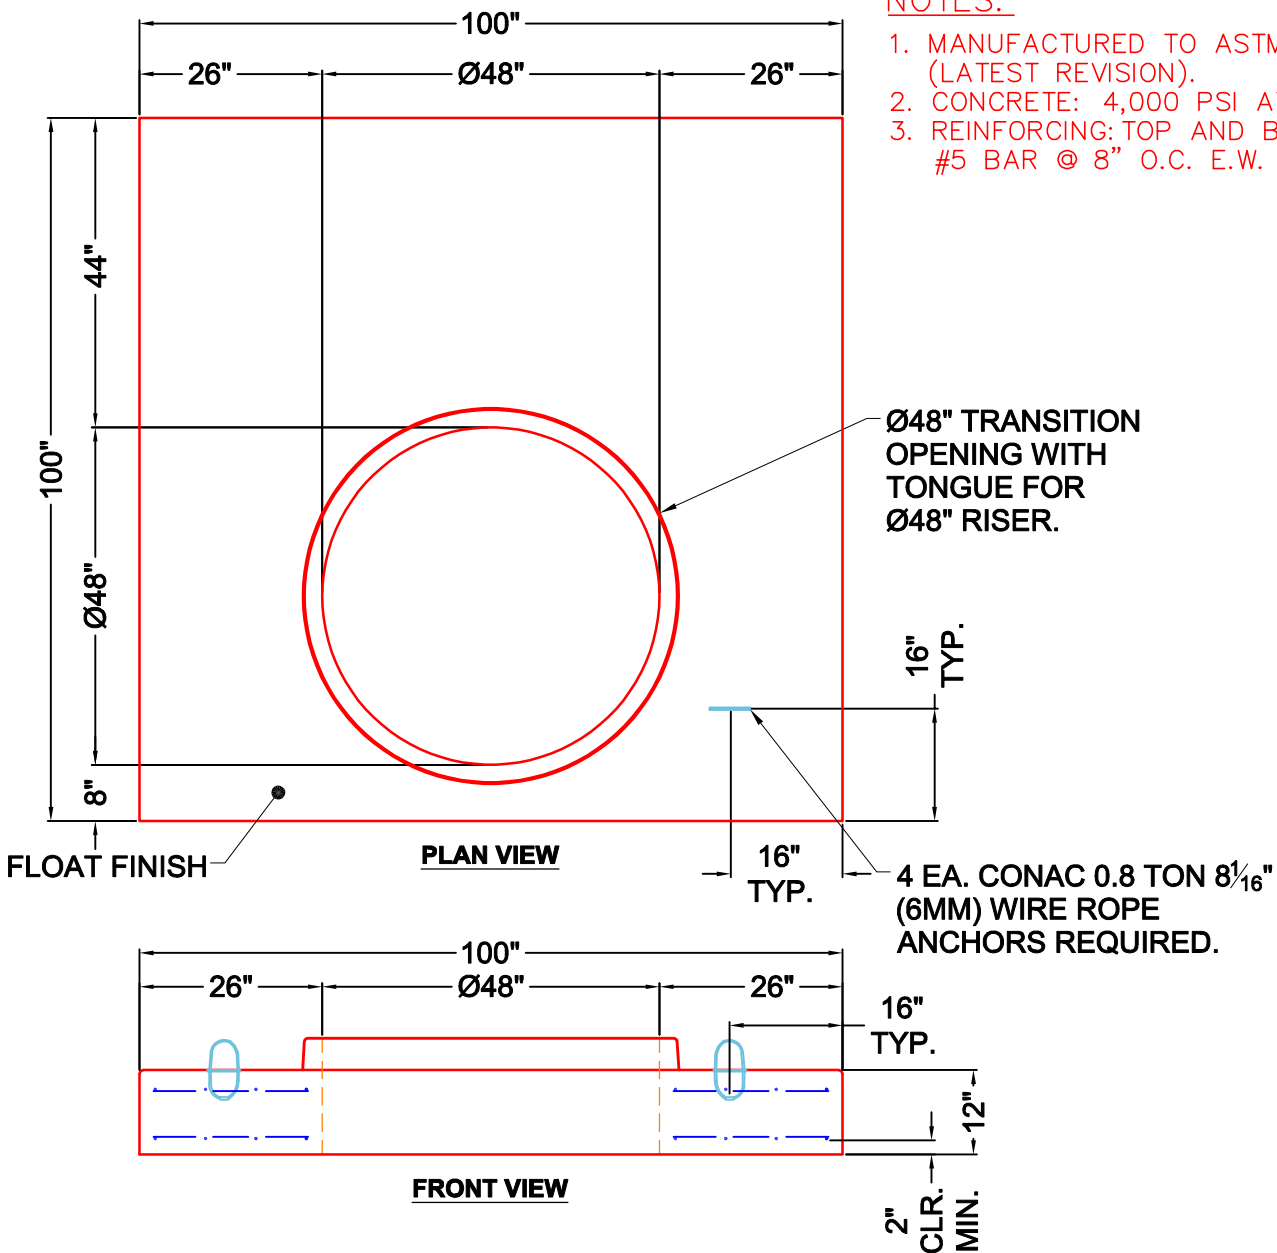

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 12"	Weight (Net): 8247 lb Volume (Net): 2.11cu.yd
----------------------------------	----------------------------------	--------------------	-------------------	--
